

Bond Update


December 14, 2015

Agenda:

- Bond Summary
- Project by Project Update
- Roberts Road Design Update
- CTE / Ag Sciences Design Update
- Questions / Suggestions



Bond Summary:



• Total Expenditures to Date

- \$71,320,000 Budget
- \$2,150,968 Encumbered
- 3% Complete

• Schedules

- Package A (Jones, RR, CTE, & Ag.)
 - On Schedule
 - Out to Bid 2/25/16
 - Complete by Fall 2017
- Package B (Schultz & Bus Paving)
 - On Schedule
 - Out to Bid 4/26/16
 - Complete by January 2017
- Package C (Mechanical/Electrical)
 - On Schedule (Start Design Fall 16)
 - Out to Bid 2/21/17
 - Complete by Fall 2018
- **Miscellaneous** (Portables, Paving, Buses, Technology)
 - Portables (3 purchased 6 pending)
 - Stadium Parking Complete
 - Bus Purchases (10 ordered)
 - Technology and Access Control TBD
- Misc.
 - Elementary School site contract is extremely time sensitive



Project Update

- Contract Documents 75% Complete
- Survey (Boundary, Topographic, Tree)
- Geotechnical Investigations
- Geo-Thermal Test Well

Budget Review


- \$24,860,000
- 85/20 Goal

Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- On Schedule for Fall 2017 Open

Look Ahead

 Board Update 1/11/16 – Interior and Exterior Colors and Finishes

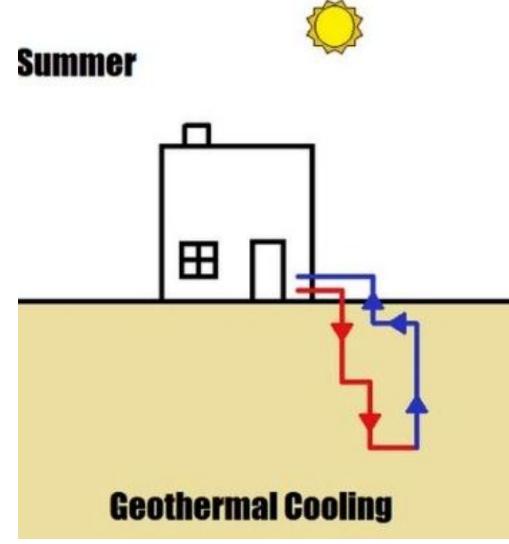

Project Update

- Contract Documents 75% Complete
- Survey (Boundary, Topographic, Tree)
- Geotechnical Investigations
- Geo-Thermal Test Well

Budget Review

- \$24,860,000
- 85/20 Goal

Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- On Schedule for Fall 2017 Open

Look Ahead

Board Update 1/11/16 – Interior and Exterior Colors and Finishes









Roberts Road Addition:



Project Update

- Contract Documents 50% Complete
- Survey (Topographic)
- Geotechnical Investigations
- Existing Pipe Testing

Budget Review

- \$4,290,175
- 85/20 Goal

Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- On Schedule for Fall 2017 Open

Look Ahead

 Board Update 1/11/16 – Interior and Exterior Colors and Finishes

Roberts Road Addition:



Roberts Road Addition:



High School CTE & Ag:



Project Update

- Contract Documents 50% Complete
- Survey (Topographic)
- Geotechnical Investigations

Budget Review

- \$4,019,120
- 85/20 Goal


Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- Ahead of Schedule for Fall 2017 Open

Look Ahead

 Board Update 1/11/16 – Interior and Exterior Colors and Finishes

High School Ag:

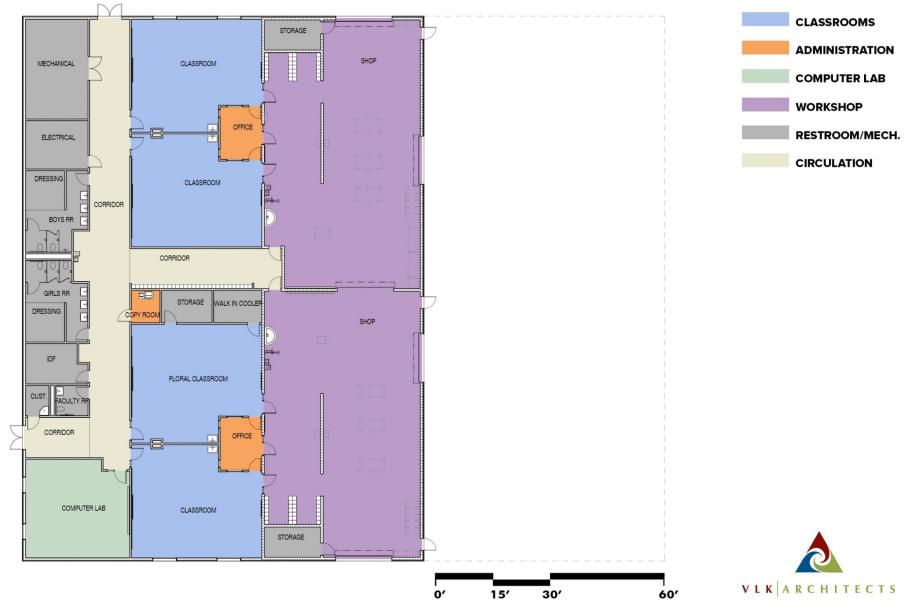

High School CTE:

0 0 0 0 0 0



Schultz Tennis & Track:

• Project Update

- Survey (Topographic)
- Geotechnical Investigations


• Budget Review


- \$2,895,225
- Schedule
 - Out to Bid 4/26/16
 - Receive Proposal 5/24/16
 - Award Construction Contract 6/03/16
 - Ahead of Schedule for 1/17 Open

• Look Ahead

• Board Update 2/8/16 – Schematic Design Presentation

Thank You . . .





Contractor Selection Criteria

December 14, 2015




- Based on Cost and Quality
- Must Publish Selection Criteria
- Must Rank Proposals
- Must Negotiate with Contractors in Rank Order

• Typical Selection Criteria

- Proposed Cost for Project
- Years In Business
- School Construction Experience
- Proposed Team and History Together
- References
- Experience with District and/or Architect

Process

- Establish Proposal Evaluation Team
- Establish Criteria and Weighting
- Architect Publishes Criteria with Plans/Specs.
- Receive, Evaluate, and Rank all Proposals
- Negotiate with top Ranked Firm
- If Agreement Not Reached- notify, and proceed to next firm until agreement reached.



New Elementary School

(July 2015 - July 2017)

Robert's Road Addition

(August 2015 - July 2017)

Waller High School CTE / Ag

(August 2015 - July 2017)

Schultz Tennis Courts and Track

(January 2016 - August 2016)

Additional Bus Parking

(January 2016 - August 2016)

Mechanical / Electrical

(February 2016-August 2016???)

Miscellaneous (Portables, Technology, Buses, Etc.)

(Ongoing)



Packaging Projects:

r ISD Proj	ect Summary		\$71,320	0,000.00
2015 Bond		\$ 71,322,871.00	(Actual	Bond Amount)
			•	· · · · · · · · · · · · · · · · · · ·
Student Grow	th	\$ 44,075,000.00		
New	Elementary #6			\$ 30,500,000.0
Port	able Buildings			\$ 720,000.0
Lan	d Aqusition			\$ 6,525,000.0
	Two Elementary S	Schools		
	One Junior High S	School		
	One High School			
Rob	erts Road Elementary S	School Additions		\$ 6,330,000.0
Facility Additi	ons and Renovations	\$ 16,250,000.00		
ruency ruure		• 10,200,000.00		
Wall	ler High School CATE/A	la Building		\$ 5,320,000.0
	Existing CATE/AC			
		Renovate Existing S	Shops	
	New CTE/Ag Build	ding		
		Two Shops, Classro	oms, Locker Ro	oms
Fac	ility Assesment – Carpe	t, Mechanical, Electric	al and Plumbing	\$10,930,000.0
Transportation	n	\$ 4,349,871.00		
Bus	ses Replacement and r	new		\$ 3,849,871.0
	30 Regular Educ	ation Busses		
	9 Special Needs	Busses		
Add	litional Parking			\$ 500,000.0
Technology		\$ 3,008,000.00		
	Upgrades at 8 Campu			\$ 370,000.0
IDF Upgrades at 8 Campuse				\$ 500,000.0
Wireless Accsess Points				\$ 708,000.0
	nputer Replacements			\$ 1,430,000.0
	· .			
Athletics		\$ 2,890,000.00		
	ler ISD Stadium – Crush	-		\$ 210,000.0
	ltz Junior High School -	-		\$ 1,780,000.0
Scu	ltz Junior High School -	• Tennis		\$ 900,000.0
Safety and Sec		\$ 750,000.00		
New Security Cameras and				\$ 250,000.0
Carr	Reader's at All Acces	s Points		\$ 500,000.0

Projects/Budgets:

