

2019 BOND

UPDATE

October 2022




2019 Bond Project Update

October 2022

- ❖ **New Waller High School -**
 - School official opened August 22, 2022.
 - New Waller High School Dedication October 12th.
- ❖ **Waller Junior High School Renovations and Additions**
 - Project is On Budget and On Schedule for opening Phase 1 in August 2023.
 - East Gym (Phase 1A) was complete for use, with ongoing work.
- ❖ **Schultz JH Renovation**
 - Phase 1 is complete for the start of 2022-23 school year.
 - Phase 2 has started in Athletic areas, in addition to finish work in Phase 1.
- ❖ **Holleman Elementary**
 - Demolition 98% complete.
 - Paint and Flooring are ongoing.

NEW HIGH SCHOOL CONSTRUCTION UPDATE

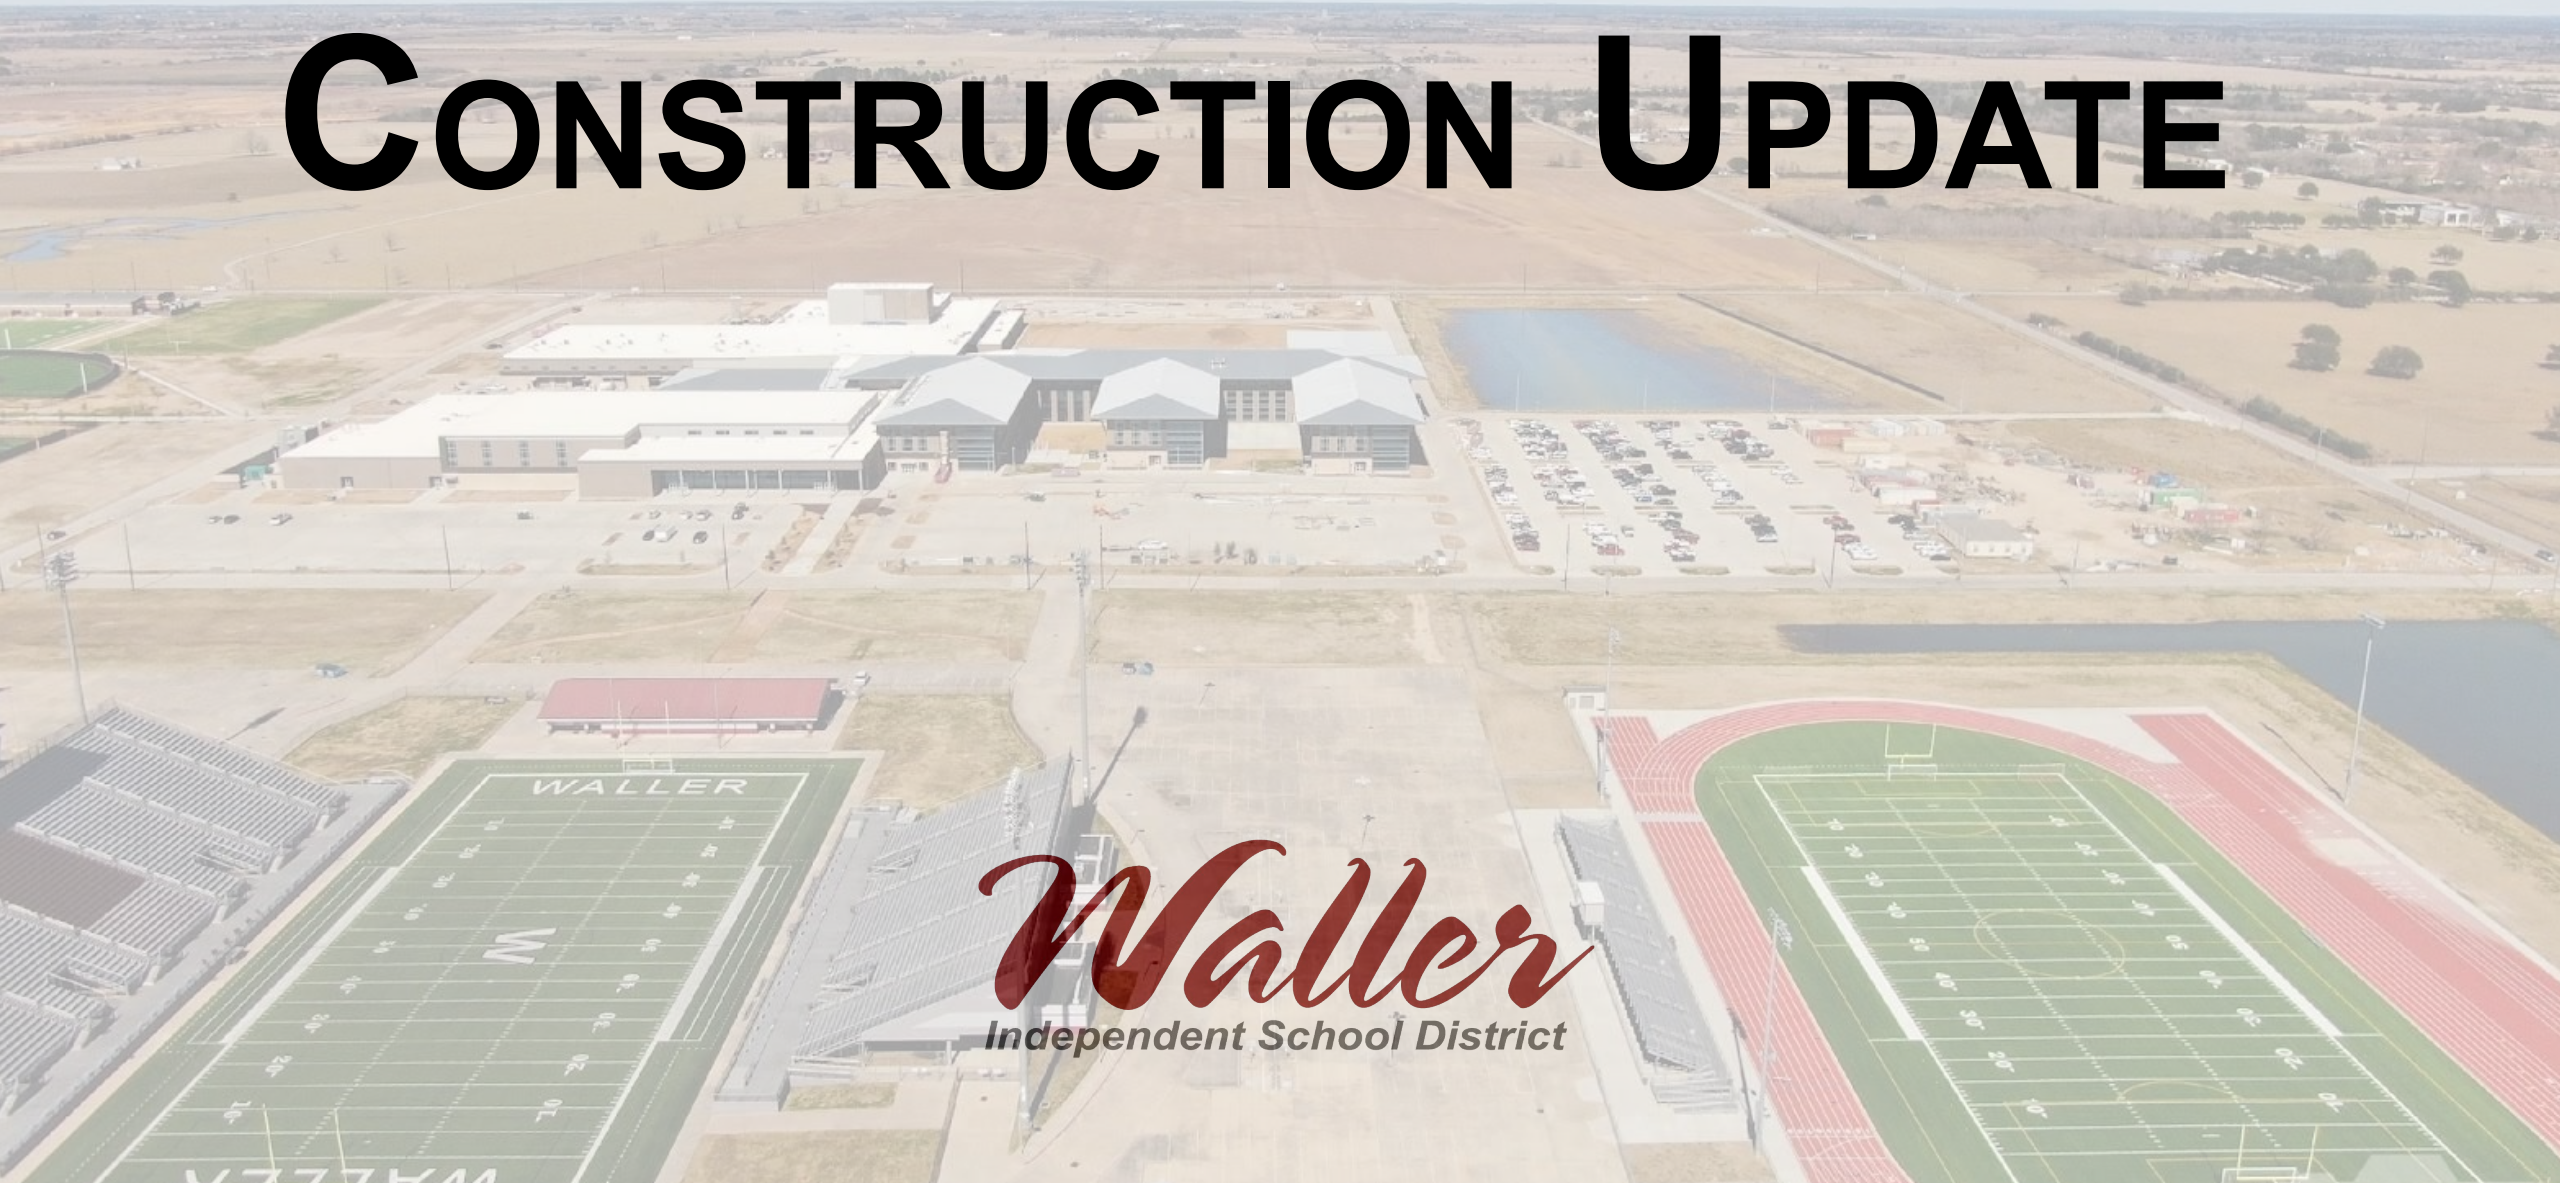

Waller
Independent School District

2019 Bond Project Update



Front Entry

2019 Bond Project Update



Library

2019 Bond Project Update




Auditorium Lobby

2019 Bond Project Update




Bistro

2019 Bond Project Update

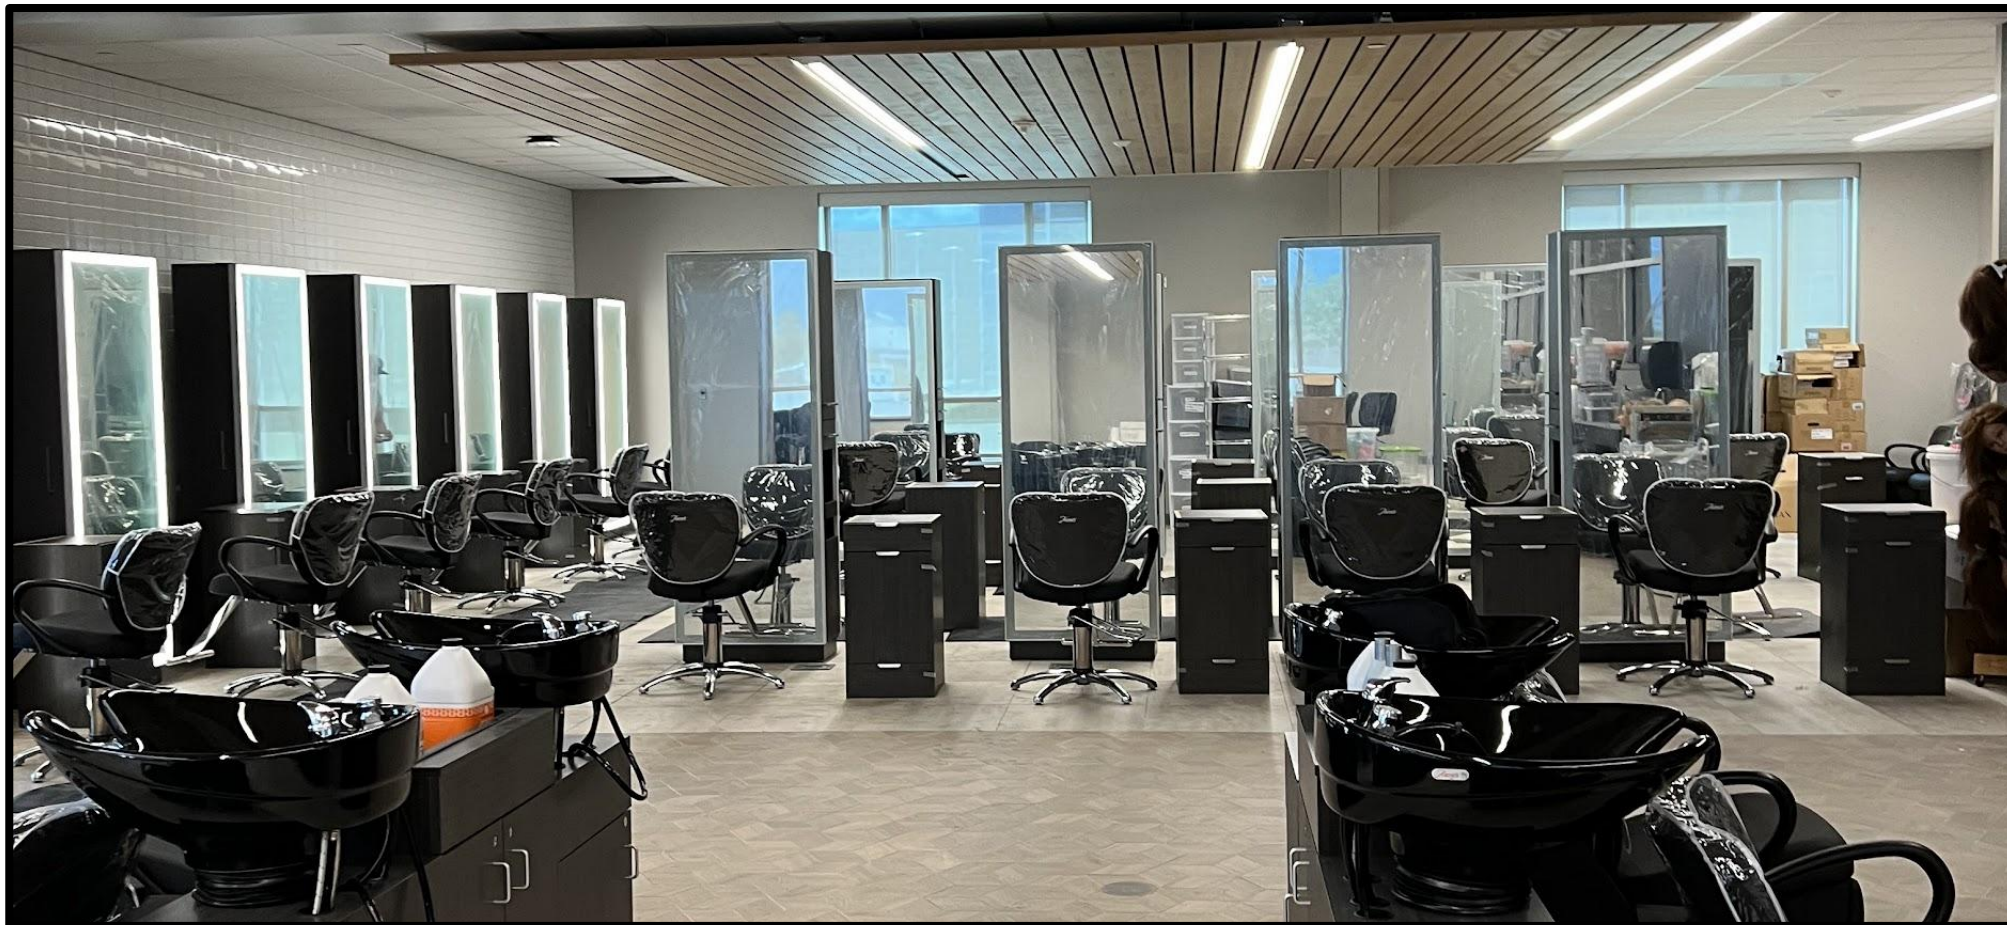

Cosmetology

2019 Bond Project Update

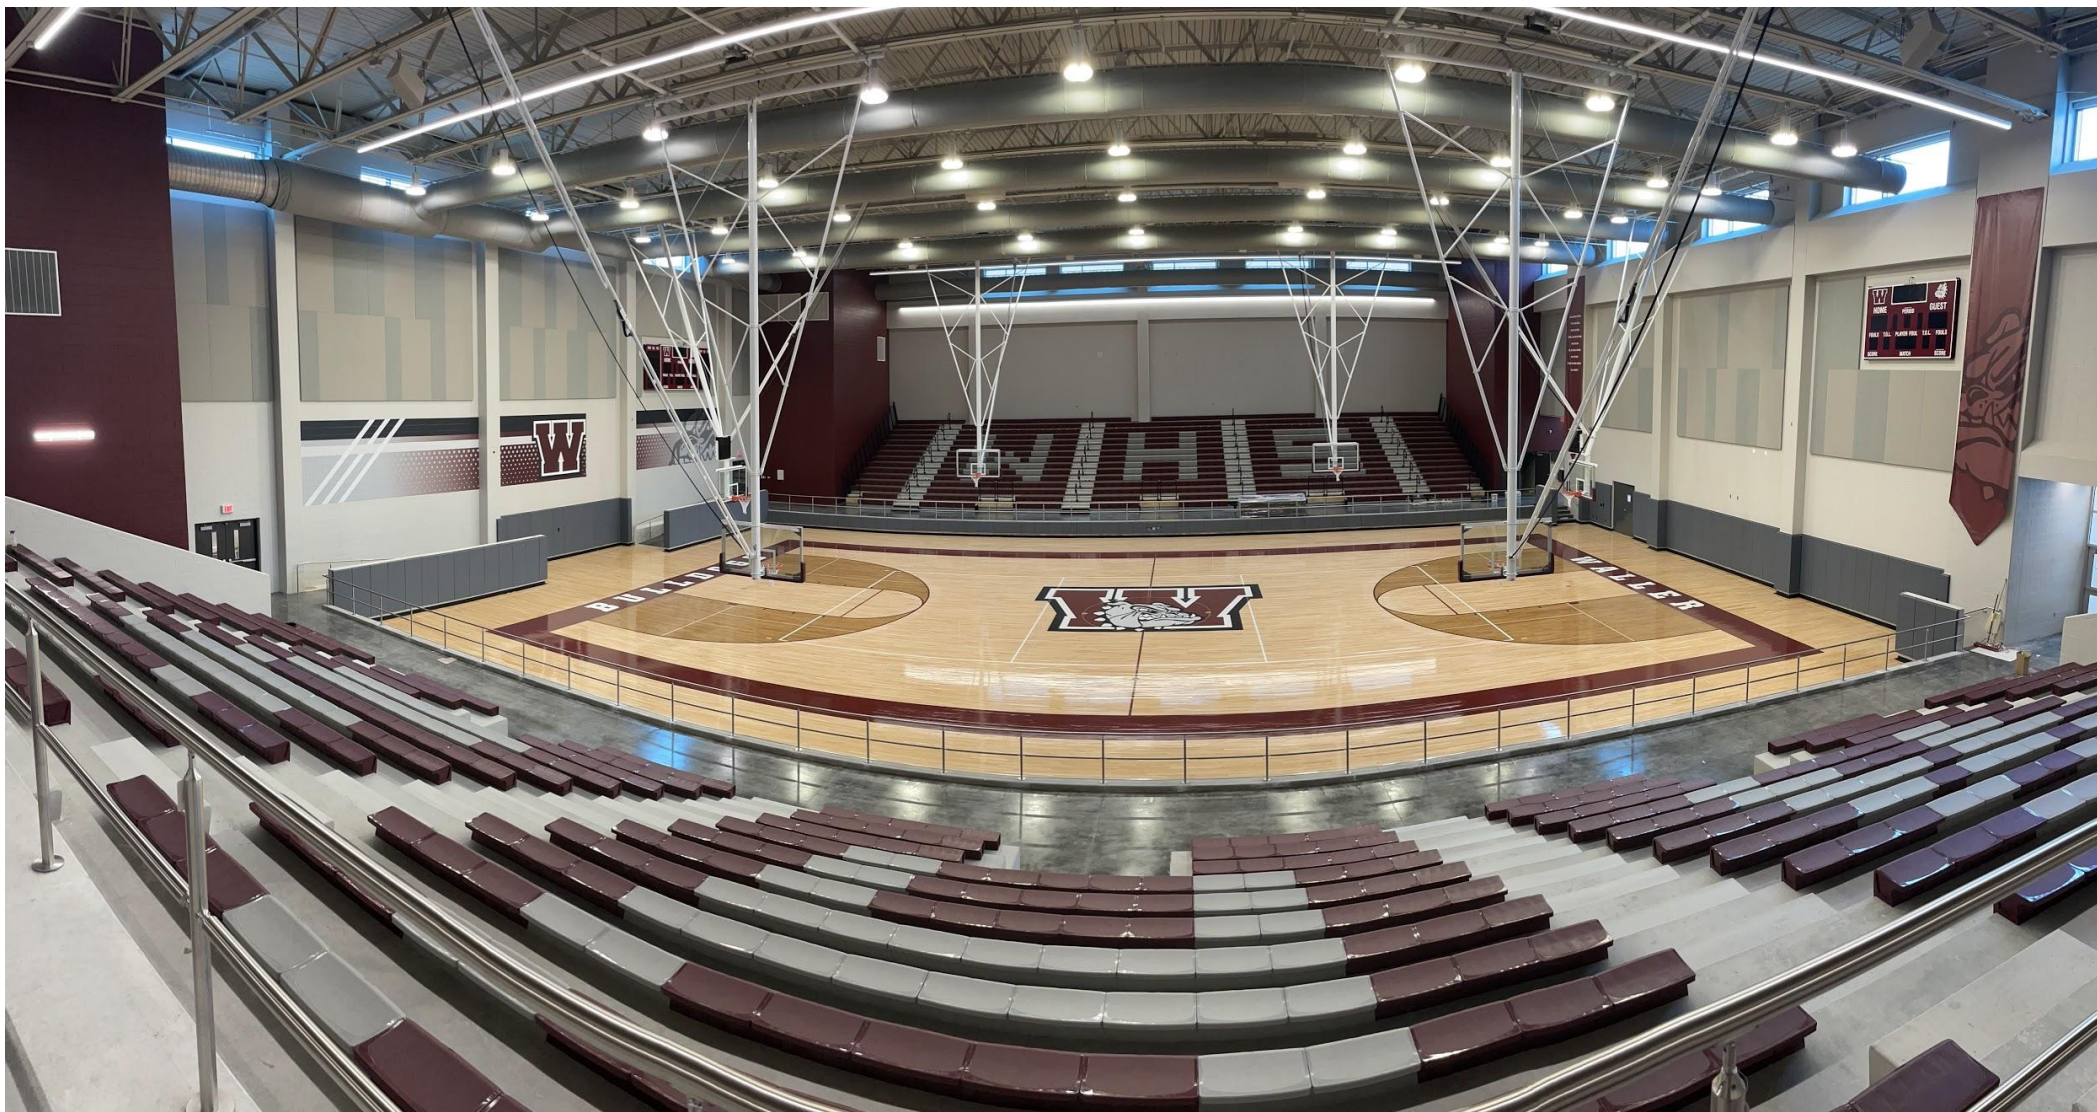

2019 Bond Project Update



High School Weight Room



Athletic Training

2019 Bond Project Update



Field House Weight Room

Project Update - New Waller High School

VLK has written punch lists for the entire campus with 14,000+ items.

- Substantial Completion approved.
- Drymalla continues working on final cleaning and punch lists items.
- Harris County Health Dept issued certificates for both the kitchen and gym concession, and scheduled to inspect Culinary and Bistro.
- Auditorium lighting and local sound are operational.
- Wall and building graphics remain ongoing.
- Marque installation is anticipated in November.
- Access control system installation programming in progress. Building secured.
- Furniture deliveries are 98% complete.

WALLER JUNIOR HIGH CONSTRUCTION UPDATE



2019 Bond Project Update



East Gym Renovation

2019 Bond Project Update



East Gym Locker Rooms

2019 Bond Project Update



Gym Lobby




Second Gym

2019 Bond Project Update



7th Grade Neighborhood

2019 Bond Project Update

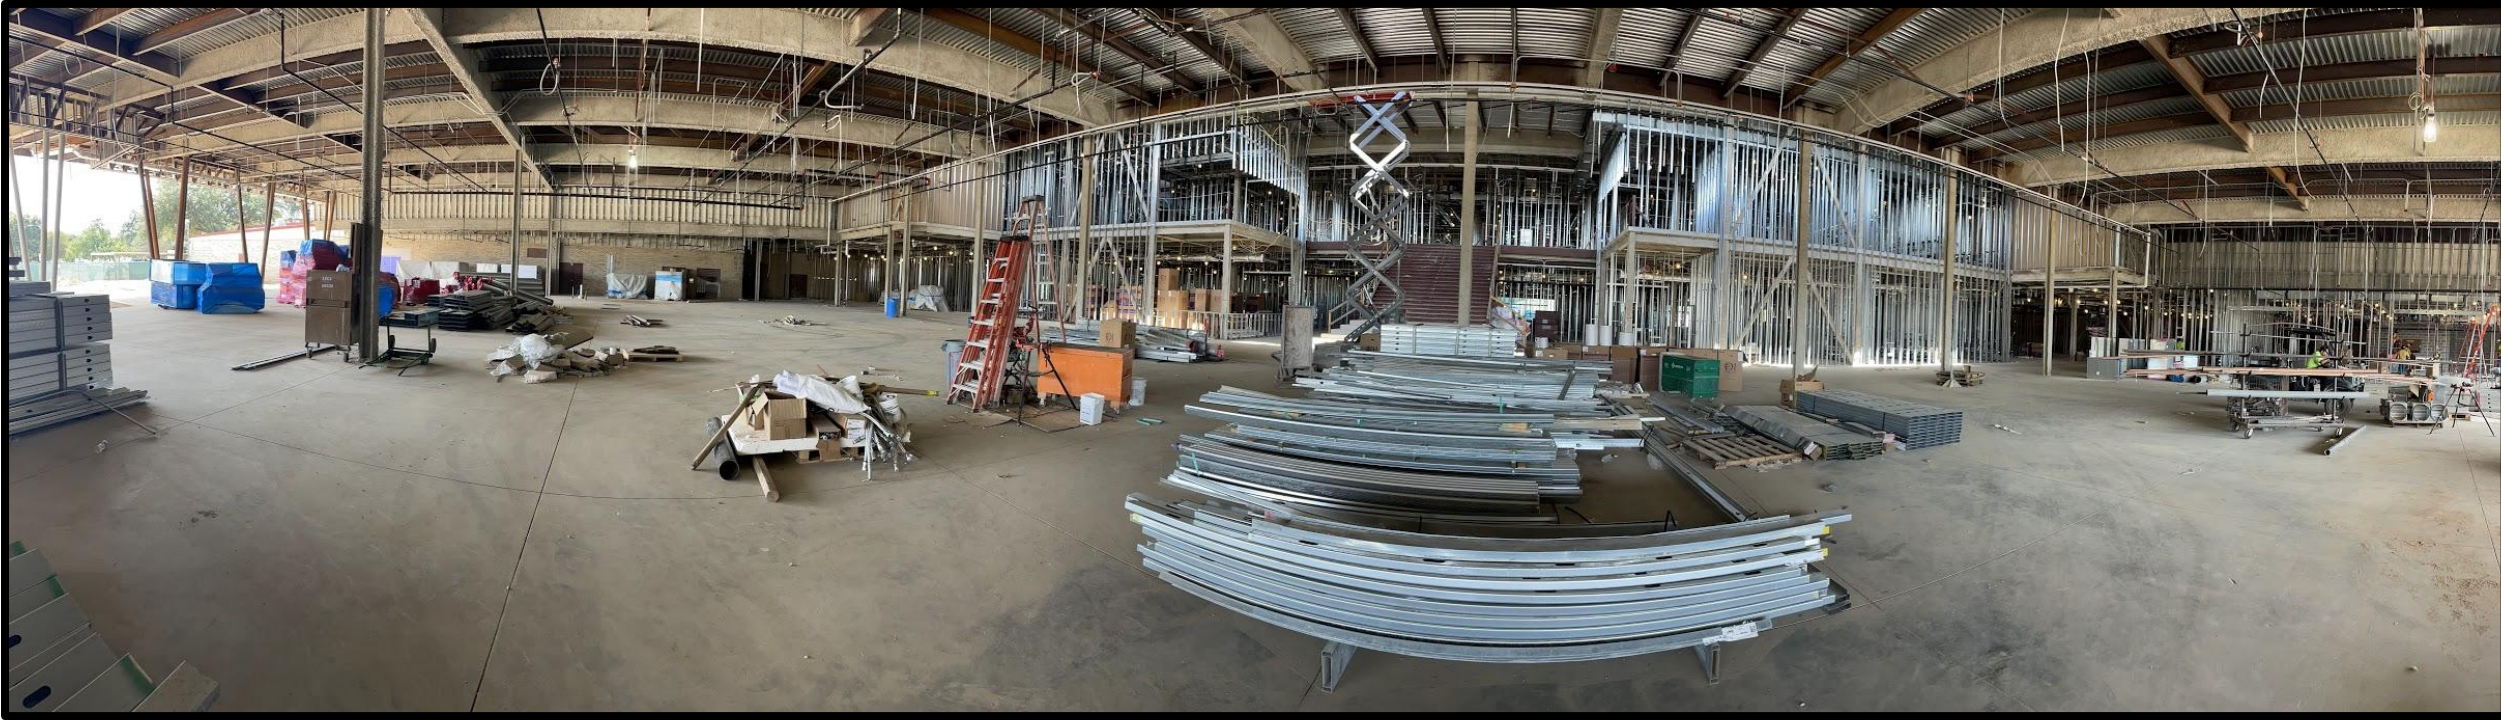

Cafeteria

2019 Bond Project Update



**7th Grade Neighborhood
(Side View)**

2019 Bond Project Update



**Front WJH Entry
Driveway and Parking**

Project Update - Waller JH Addition

- Phase 1A summer paving in front of the school and bus drive are complete.
- East Gym renovation is 98% complete, and released for district use.
- CMU wall is 70% complete in second gym.
- MEP rough-in remains in progress throughout both the 1st and 2nd floors.
- Interior and exterior metal wall framing still in progress.
- CMU wall construction has started and 50% complete.
- Roof installation is underway, as weather allows.
- Window frame and glazing have finished and building is dried in.
- Exterior brick is arriving in short time.
- Project mockup panel is installed and finishes are being installed.


SCHULTZ JUNIOR HIGH CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update

PHASING PLAN
PRIME CONTRACTORS, INC.
02 June 2022

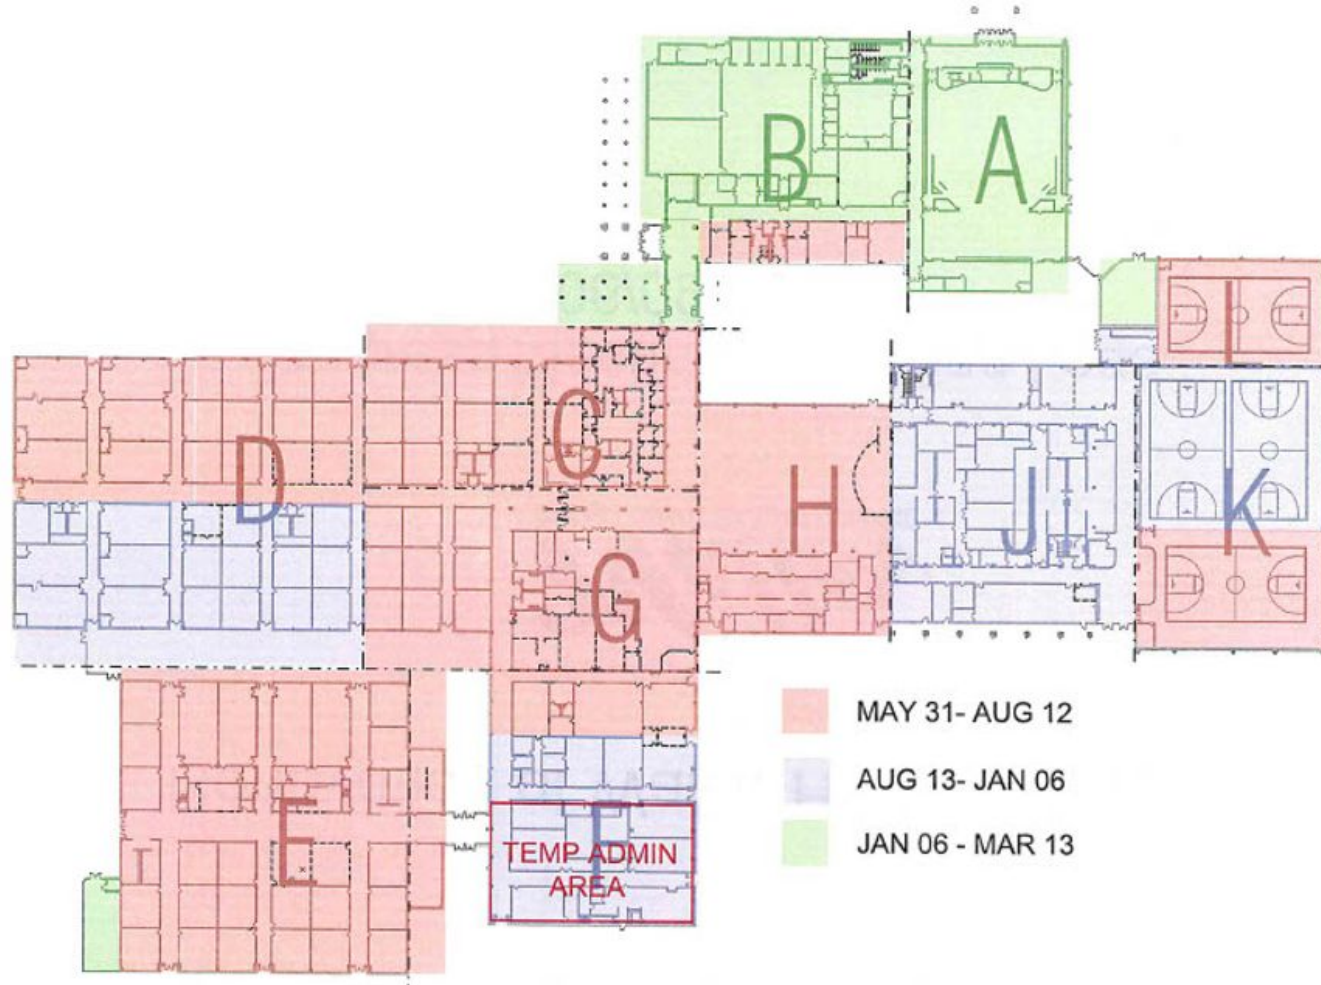

2019 Bond Project Update



Entry Vestibule and Front Office Area

2019 Bond Project Update



Conference Room



Admin Area Kitchenette

2019 Bond Project Update



Gym Lobby Flooring



Gym Concessions Reno

2019 Bond Project Update



Cafeteria

2019 Bond Project Update



New Cafeteria Hall



Main Hallway

2019 Bond Project Update



Library

2019 Bond Project Update



Classroom Hall



Fine Arts Hallway

2019 Bond Project Update



200 Hallway Collab Area


Project Update - Schultz JH Renovation

- Temporary Fire Alarm testing for Phase 1 is completed.
- Phase 1 is 95% completed with minor items to be installed.
- Phase 2 demo work is nearly completed in Athletic areas.
- New Fire Sprinklers for Systems #5, in Athletic areas, has started.
- New Entry Canopy and Marquee have been finalized and ordered.

HOLLEMAN ELEMENTARY CONSTRUCTION UPDATE

Waller
Independent School District

2019 Bond Project Update



Holleman ES Walkthrough

Project Update - Holleman Renovation

- Substantial demolition has completed with select demo continuing.
- Paint and flooring throughout the instructional areas has begun.
- Metal wall studs and drywall being installed in new addition areas

Thank You!

