

2019 BOND

UPDATE

September 2022



2019 Bond Project Update

September 2022

❖ **New Waller High School -**

- Final Certificate of Occupancy issued by the city August 18, 2022.
- School official opened August 22, 2022.

❖ **Waller Junior High School Renovations and Additions**

- Project is On Budget and On Schedule for opening Phase 1 in August 2023.
- East Gym (Phase 1A) was complete for use, with ongoing work.

❖ **Schultz JH Renovation**

- Phase 1 is complete for the start of 2022-23 school year.
- Phase 2 has started in Athletic areas, in addition to finish work in Phase 1.

❖ **Holleman Elementary**

- Demolition started and 90% complete.
- Materials are being ordered.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update



Front Entry

2019 Bond Project Update

Central Staircase



Nurse's Office

2019 Bond Project Update




Cafeteria



Auditorium Lobby

2019 Bond Project Update

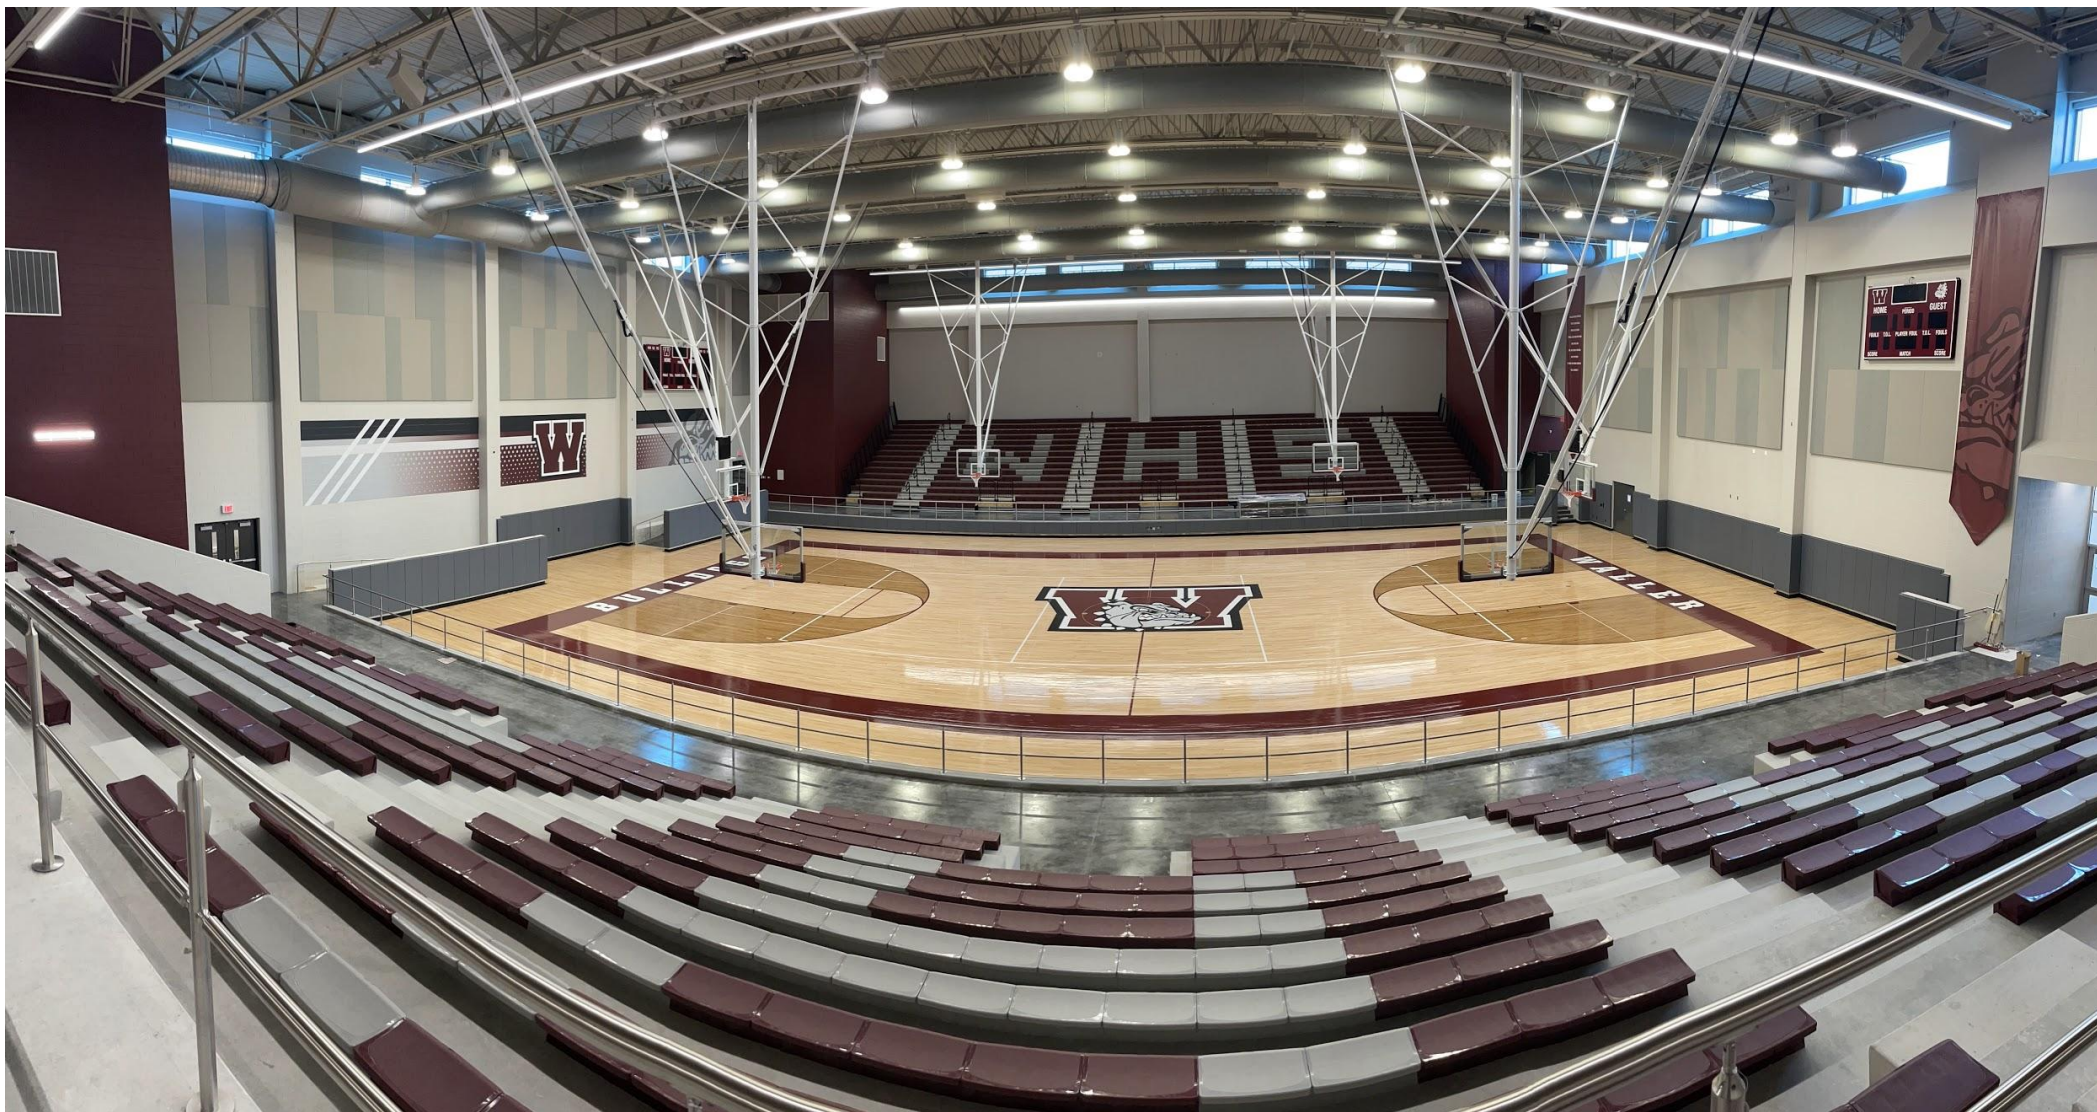

2019 Bond Project Update



High School Weight Room



Athletic Training

2019 Bond Project Update



Field House Weight Room

Project Update - New Waller High School

VLK has written punch lists for the entire campus with 14,000+ items.

- Substantial Completion approved.
- Drymalla continues working on final cleaning and punch lists items.
- Harris County Health Dept issued certificates for both the kitchen and gym concession, and scheduled to inspect Culinary and Bistro.
- Auditorium lighting and local sound are operational with temporary equipment.
- Wall and building graphics remain ongoing.
- Marque installation is anticipated in October.
- Access control system installation programming in progress. Building secured.
- Building Commissioning and Air Balance being finalized.
- Furniture deliveries are 95% complete.

WALLER JUNIOR HIGH CONSTRUCTION UPDATE



2019 Bond Project Update



East Gym Renovation

2019 Bond Project Update



East Gym Locker Rooms

2019 Bond Project Update



**WJH two-story addition
Rear- North Elevation**

2019 Bond Project Update



**Front WJH Entry
Driveway and Parking**

2019 Bond Project Update



Main Staircase



Wall Studs

2019 Bond Project Update



Main Corridor

2019 Bond Project Update



Second Gym

2019 Bond Project Update



Side Staircase



Cafeteria

Project Update - Waller JH Addition

- Phase 1A summer paving in front of the school and bus drive are complete.
- East Gym renovation is 95% complete, and released for district use.
- Last concrete slab area was pour in second gym.
- MEP rough-in remains in progress throughout both the 1st and 2nd floors.
- Interior and exterior metal wall framing still in progress.
- CMU wall construction has started and 25% complete.
- Roof installation is underway, as weather allows.
- Window frame and glazing are scheduled for delivery in later in September.
- Exterior brick is scheduled to arrive September 19th.
- Project mockup panel is being installed and prepared for review.


SCHULTZ JUNIOR HIGH CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update

PHASING PLAN
PRIME CONTRACTORS, INC.
02 June 2022

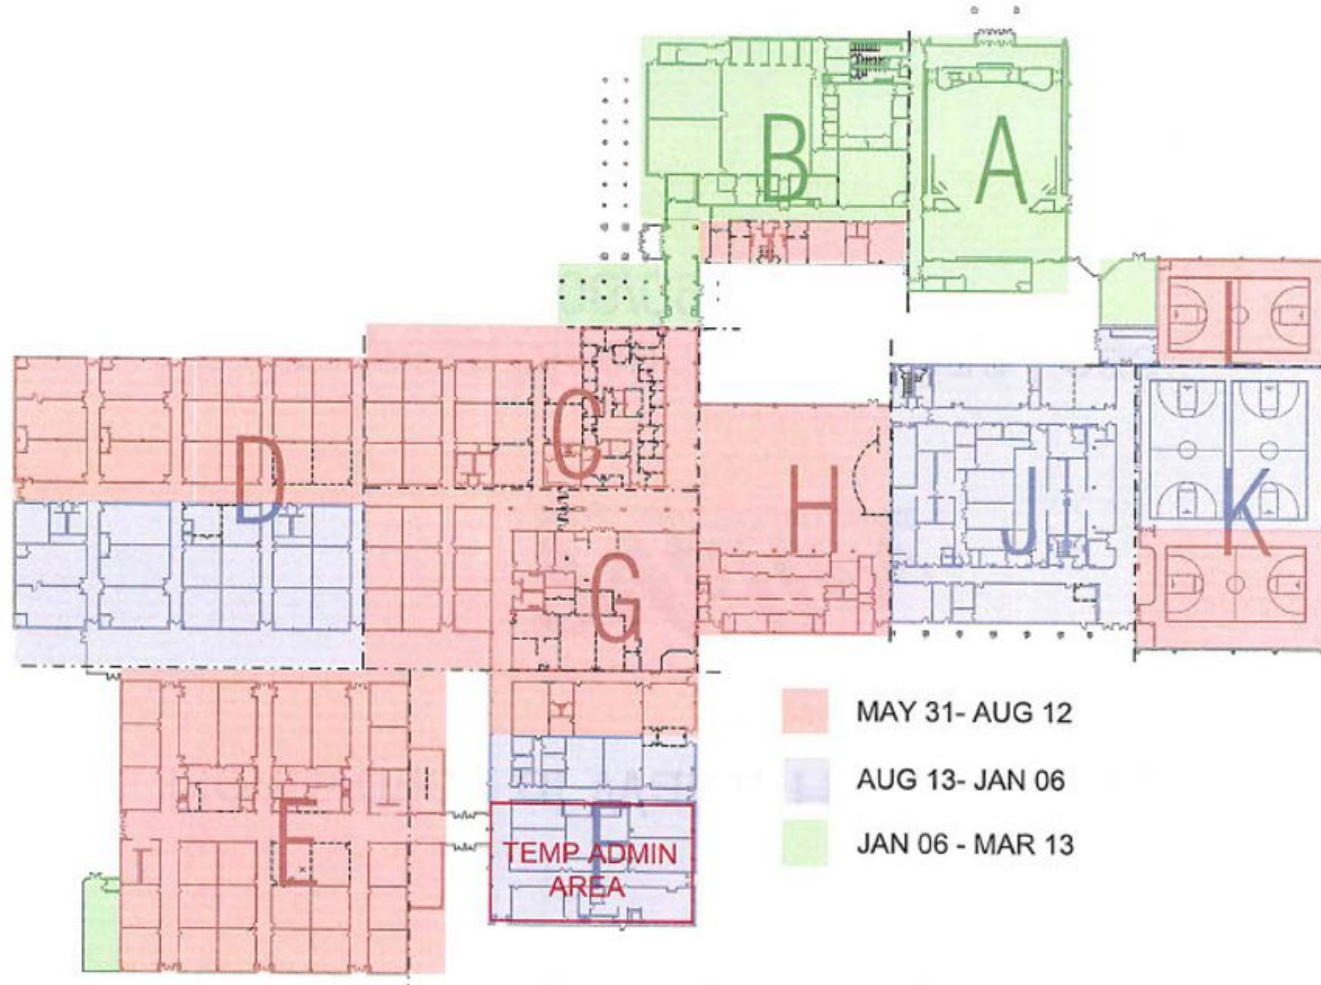

2019 Bond Project Update



Entry Vestibule and Front Office Area

2019 Bond Project Update



Conference Room



Admin Area Kitchenette

2019 Bond Project Update



Future Display Case



Main Entry Hallway

2019 Bond Project Update



Cafeteria

2019 Bond Project Update



New Cafeteria Hall



Main Hallway

2019 Bond Project Update



Library



100 Hallway

2019 Bond Project Update



Classroom Hall



Fine Arts Hallway

2019 Bond Project Update



200 Hallway Collab Area

Project Update - Schultz JH Renovation

- Temporary Fire Alarm testing for Phase 1 is completed.
- Phase 1 was cleaned up before the start of school, with some areas still being finished. Semester started August 22nd, as scheduled.
- Phase 2 renovation work has started in Athletic areas.
- New Fire Sprinklers for Systems #5, in Athletic areas, has started.
- New Entry Canopy and Marquee have been finalized and ordered.

HOLLEMAN ELEMENTARY CONSTRUCTION UPDATE


Waller
Independent School District

2019 Bond Project Update



Front Office Demolition

2019 Bond Project Update

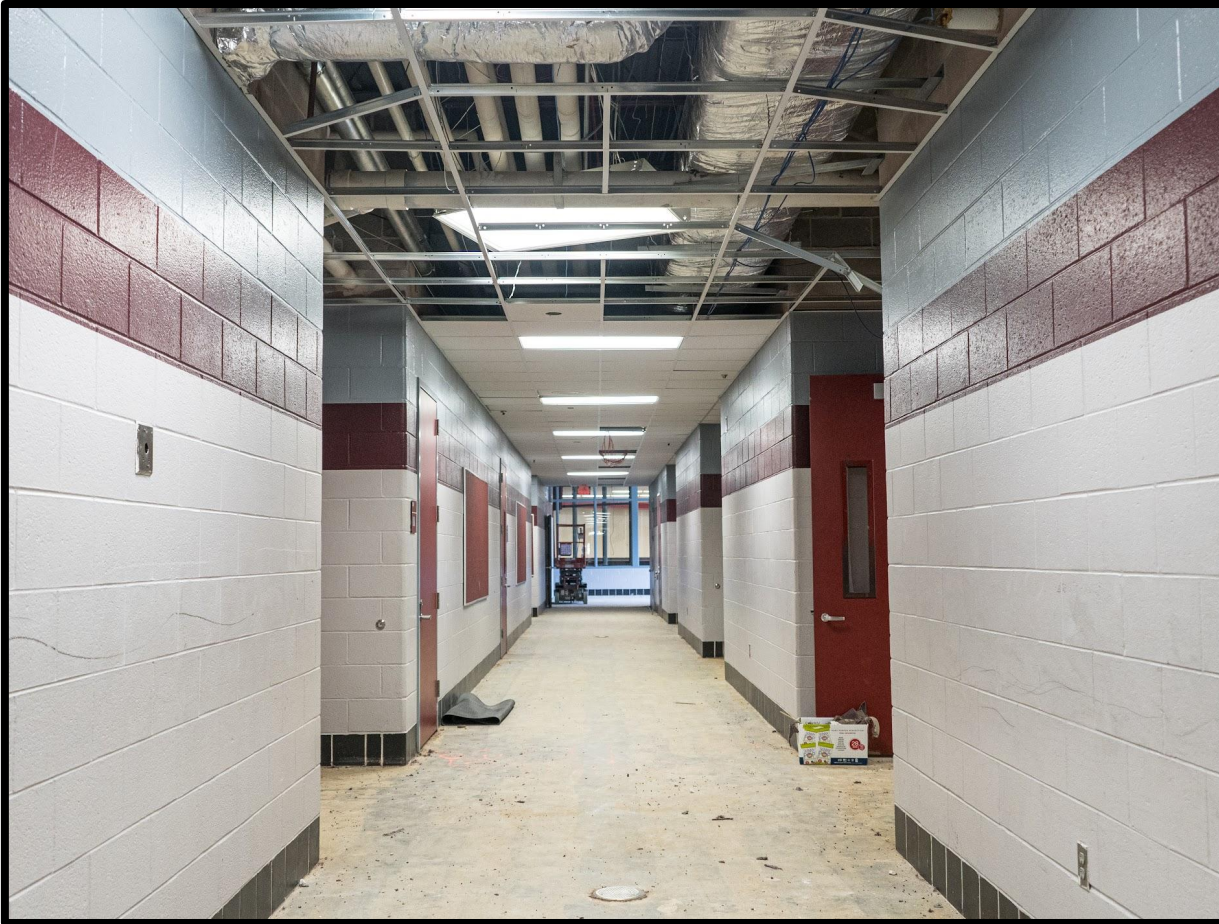

Classroom Hallway



Classroom Remodel

2019 Bond Project Update



Library

2019 Bond Project Update



Teacher's Lounge

2019 Bond Project Update



New LGI Room

Thank You!

