

2019 BOND

UPDATE

May 2021



2019 Bond Project Update

❖ New Waller High School –

50% complete through 50% of scheduled and budget.

Project remains on time and on schedule.

Soccer-Track Complex and Field House complete in June '21.

Auto Tech renovation and new Baseball/Softball start in May.

❖ Waller Junior High School Renovations and Additions –

Design Development complete and presentation planned at the June Board meeting.

Construction Documents nearly 50%.

Other Renovations Projects with VLK Architect scheduled for completions


- ❑ Schultz Junior High Renovations of WHS
- ❑ Holleman Elementary Renovations of SJH
- ❑ Roberts Road Elementary Vestibule and Renovations

*Scope and Design Kickoff meetings and initial design meeting held in April
2nd design meetings are scheduled are scheduled on May 18th.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



New Waller High School

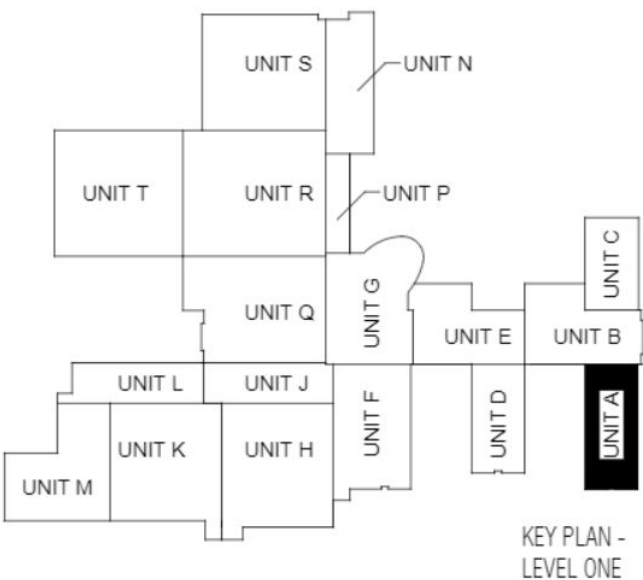

Floor Plan

New Waller High School



East Elevation from Student Parking

New Waller High School

Mockup classroom



New Waller High School

**Mechanical equipment and piping
being finalized in areas A-F.**



New Waller High School



Doors are arriving and low voltage wiring in progress

New Waller High School



**Main Gym is enclosed.
Painters and MEP trades
working on rough in.**



New Waller High School



**Soccer-Track stadium is 99% complete.
Beynon Sports has started on track surface**

New Waller High School



Field House Renovations

New Chillers are set, flushed, and ready for startup.

New Waller High School



Field House Renovations



**Lockers are being set and
prepping for epoxy flooring**

New Waller High School



Field House Renovations



Rubber Flooring has started in Weight Room and Team Meeting Rooms

New Waller High School

**60 yard synthetic turf
practice field**



Field House Renovations

Coaches' office cabinets



Project Update - New Waller High School

Construction Activity Status

- Soccer-Track Complex 99% complete for June completion
- Field House Renovation nearing completion
- Baseball/Softball summer work begins in May with December completion
- Auto Tech renovation scheduled for this summer
- Exterior Brick continuing around the north and south.
- Interior and Exterior CMU block walls continue
- Window Frames/Glass ongoing
- MEP Interior rough-in – ongoing. 90% complete in Areas A-F. Chill and Hot water mains are complete and flushing is scheduled in June before Chiller startup in July
- Reliant permanent power is scheduled for early July

Thank You!

