

# 2019 BOND

# UPDATE

**May 2022**




# NEW HIGH SCHOOL CONSTRUCTION UPDATE



*Waller*  
Independent School District

# New Waller High School

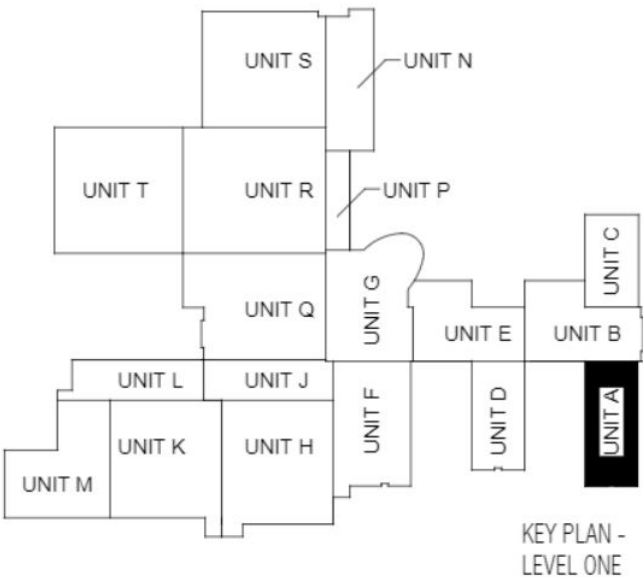

Floor Plan



# 2019 Bond Project Update


## Auditorium





# 2019 Bond Project Update

## Central Staircase

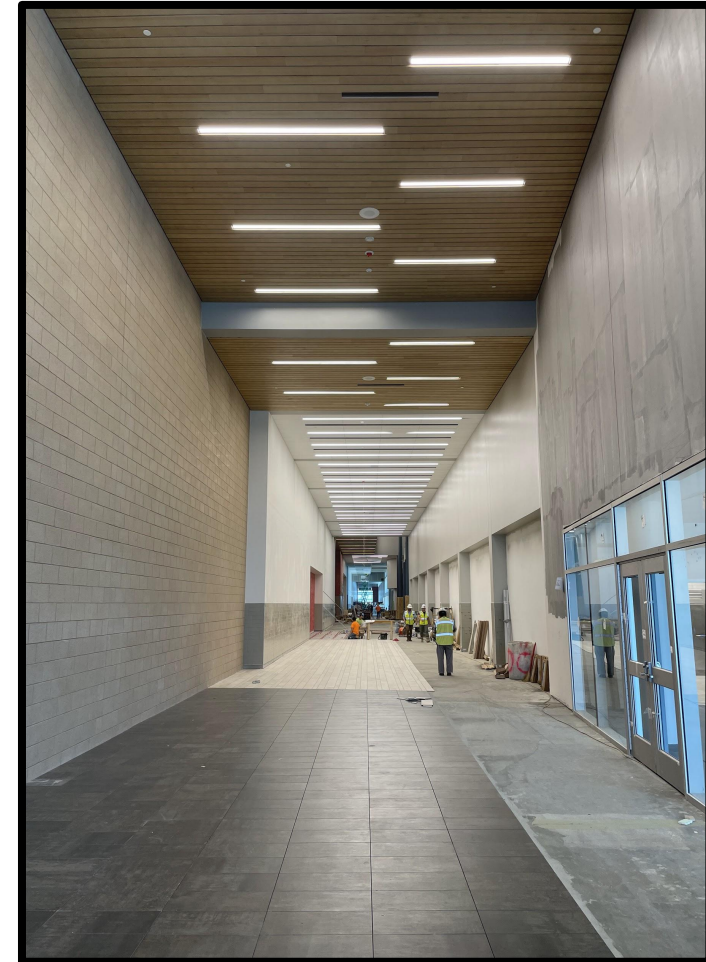

## Main Hallway



# 2019 Bond Project Update



**Large Cafeteria**



# 2019 Bond Project Update



## Large Cafeteria & Side Cafeteria




# 2019 Bond Project Update



## Cafeteria Food Lines



# 2019 Bond Project Update

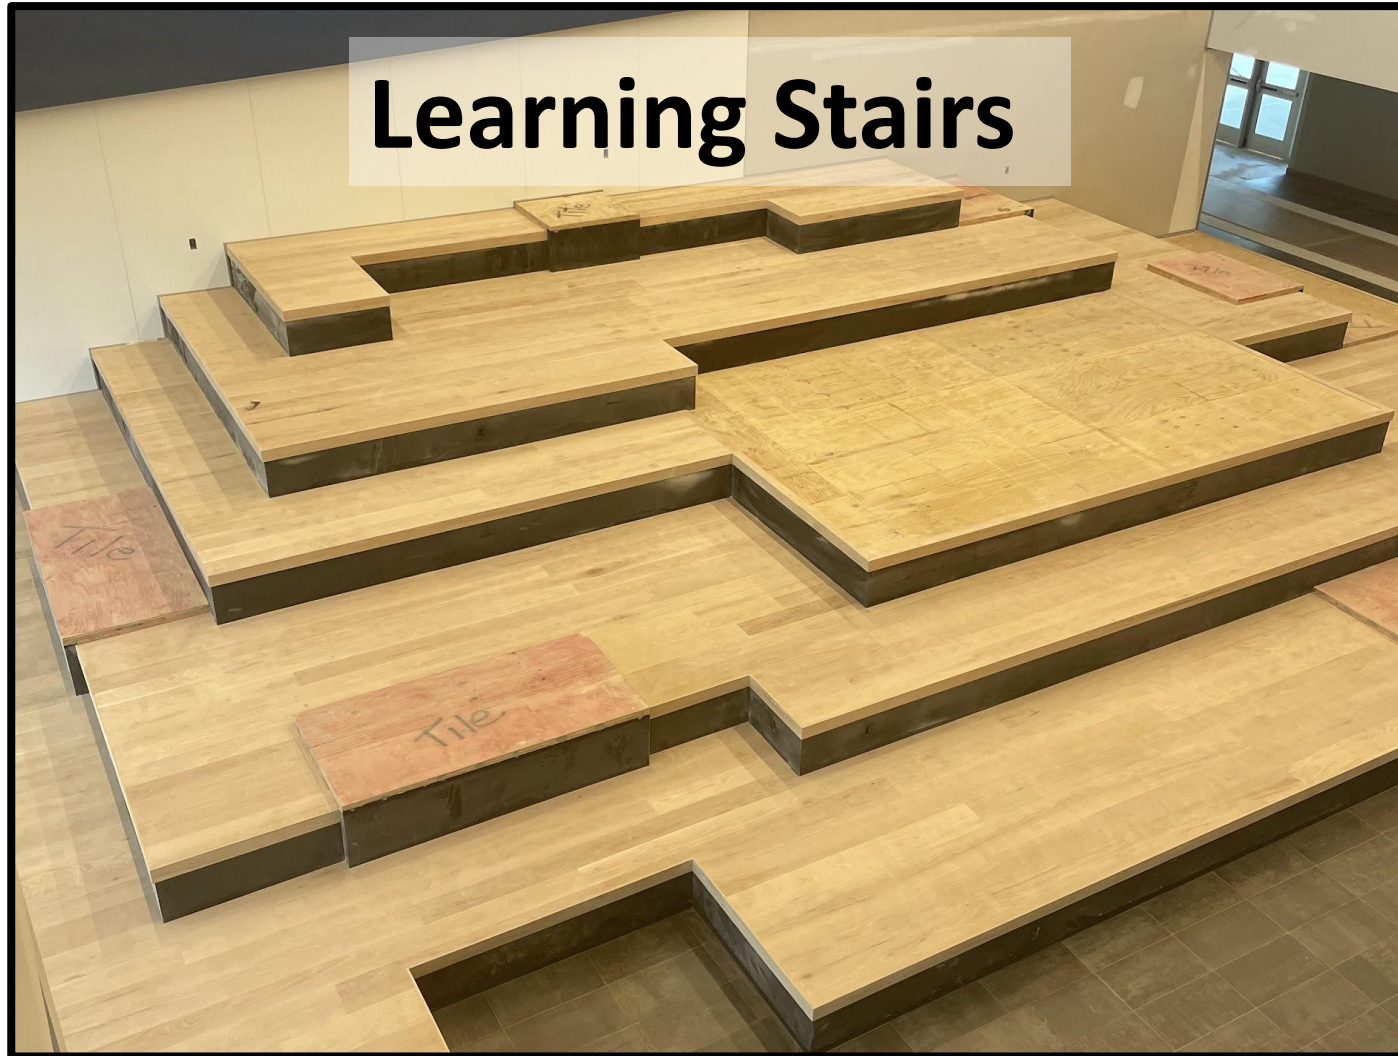

**Theater Display  
Area**



# 2019 Bond Project Update



**Locker Room**



# 2019 Bond Project Update



**Dance Gym**



**Auxiliary Gym**



# 2019 Bond Project Update



**Wrestling**



**Weight Room**



# 2019 Bond Project Update



**Athletic  
Training**



**Whirlpool Room**



# 2019 Bond Project Update



**Library Flex Rooms**



# 2019 Bond Project Update



**Woodshop Lab**



**Welding Lab**



# 2019 Bond Project Update



**Band Hall**



**Choir Hall**



# 2019 Bond Project Update



**Architecture Class**



**HVAC Lab**




# 2019 Bond Project Update



**Front Entry Glass &  
Receptionist Area**



# 2019 Bond Project Update

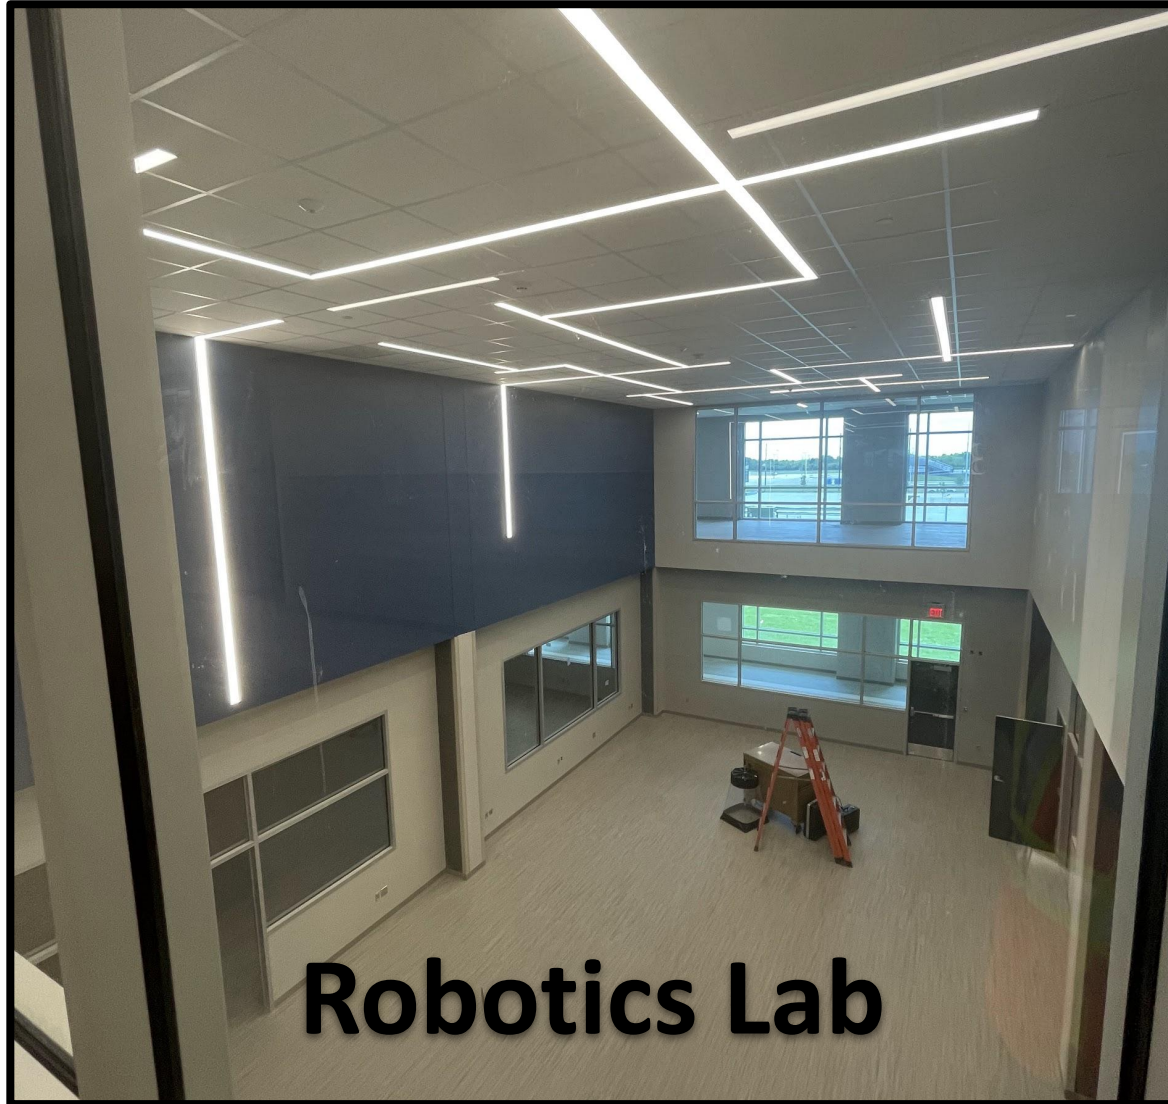

**EMT**



# 2019 Bond Project Update



**Aquatics Class**



**Pharmacy Tech Lab**



# 2019 Bond Project Update



**ROTC Practice Area**



**ROTC Classroom**



# 2019 Bond Project Update



**PLC Common Area**



**PLC Workroom**



# 2019 Bond Project Update



**Cosmo Advanced Lab**



**Cosmo Lab**



# 2019 Bond Project Update



**Advanced Culinary Lab**



**Intro to Culinary Lab**



# 2019 Bond Project Update



**Bistro Kitchen**



**Bistro**




# Project Update - New Waller High School

---

## Construction Activity Status

- Ceiling grid ongoing and tile installation is 99% complete in 3 story wings.
- Linear wood walls and decorative wood ceiling are 50% complete.
- Interior window frames and glass are 90% complete.
- Gym wood floors are installed. Painting complete and sealing in progress.
- Epoxy floors are complete in Athletic areas and kitchens. Working in hallways.
- Athletic lockers are 99% complete.
- Terrazzo flooring in auditorium lobby is complete
- Porcelain floor tile are 60% complete throughout the 1st floor.
- Classroom flooring and 2<sup>nd</sup>-3<sup>rd</sup> floor corridor LVT flooring complete.
- Window roller shades and blinds installation ongoing.
- Kitchen, Culinary, and Bistro equipment 99% complete.
- Auditorium rigging complete, and lighting and local sound have all started.
- Data cabling and classroom front row sound in progress and 95% complete.
- Final system testing are scheduled in May and June with the city.



The image shows the exterior of Waller Jr. High school. The building is a single-story structure with a light-colored brick facade and a dark red roofline. A sign above the entrance reads "WALLER JR. HIGH". The entrance features large glass doors and windows. There are several trees in front of the building, including a large green tree on the right and a smaller red-leafed tree on the left. A paved walkway leads from the foreground towards the entrance. The foreground is a green lawn.

WALLER JR. HIGH

# **WALLER JUNIOR HIGH CONSTRUCTION UPDATE**



# 2019 Bond Project Update

---



## WJH Foundation Prep



# 2019 Bond Project Update



## WJH Foundation Prep



# 2019 Bond Project Update



**Gym Reno**



**Laundry Room Reno**



# 2019 Bond Project Update



## Locker Room Reno



# 2019 Bond Project Update

---

- East gym demolition complete. Locker room underground plumbing complete.
- Ceiling paint of East gym is 90% complete.
- Drilled piers started and completed in April.
- Grade beam have started and poured in first area of slab.
- First slab pour is schedule for May 9th, and planned one per week.
- Underground plumbing started and 50% completed.
- Structural steel shop drawings are approved and steel in fabrication.
- Steel deliveries are scheduled to begin the week on May 16th, and planned one area each week.
- Material deliveries are arriving early, if possible.
- Finalizing utility abandonment documents before city can dedicate Farr St.



# Thank You!

