


# 2019 BOND

# UPDATE

July 2022



# 2019 Bond Planning Schedule

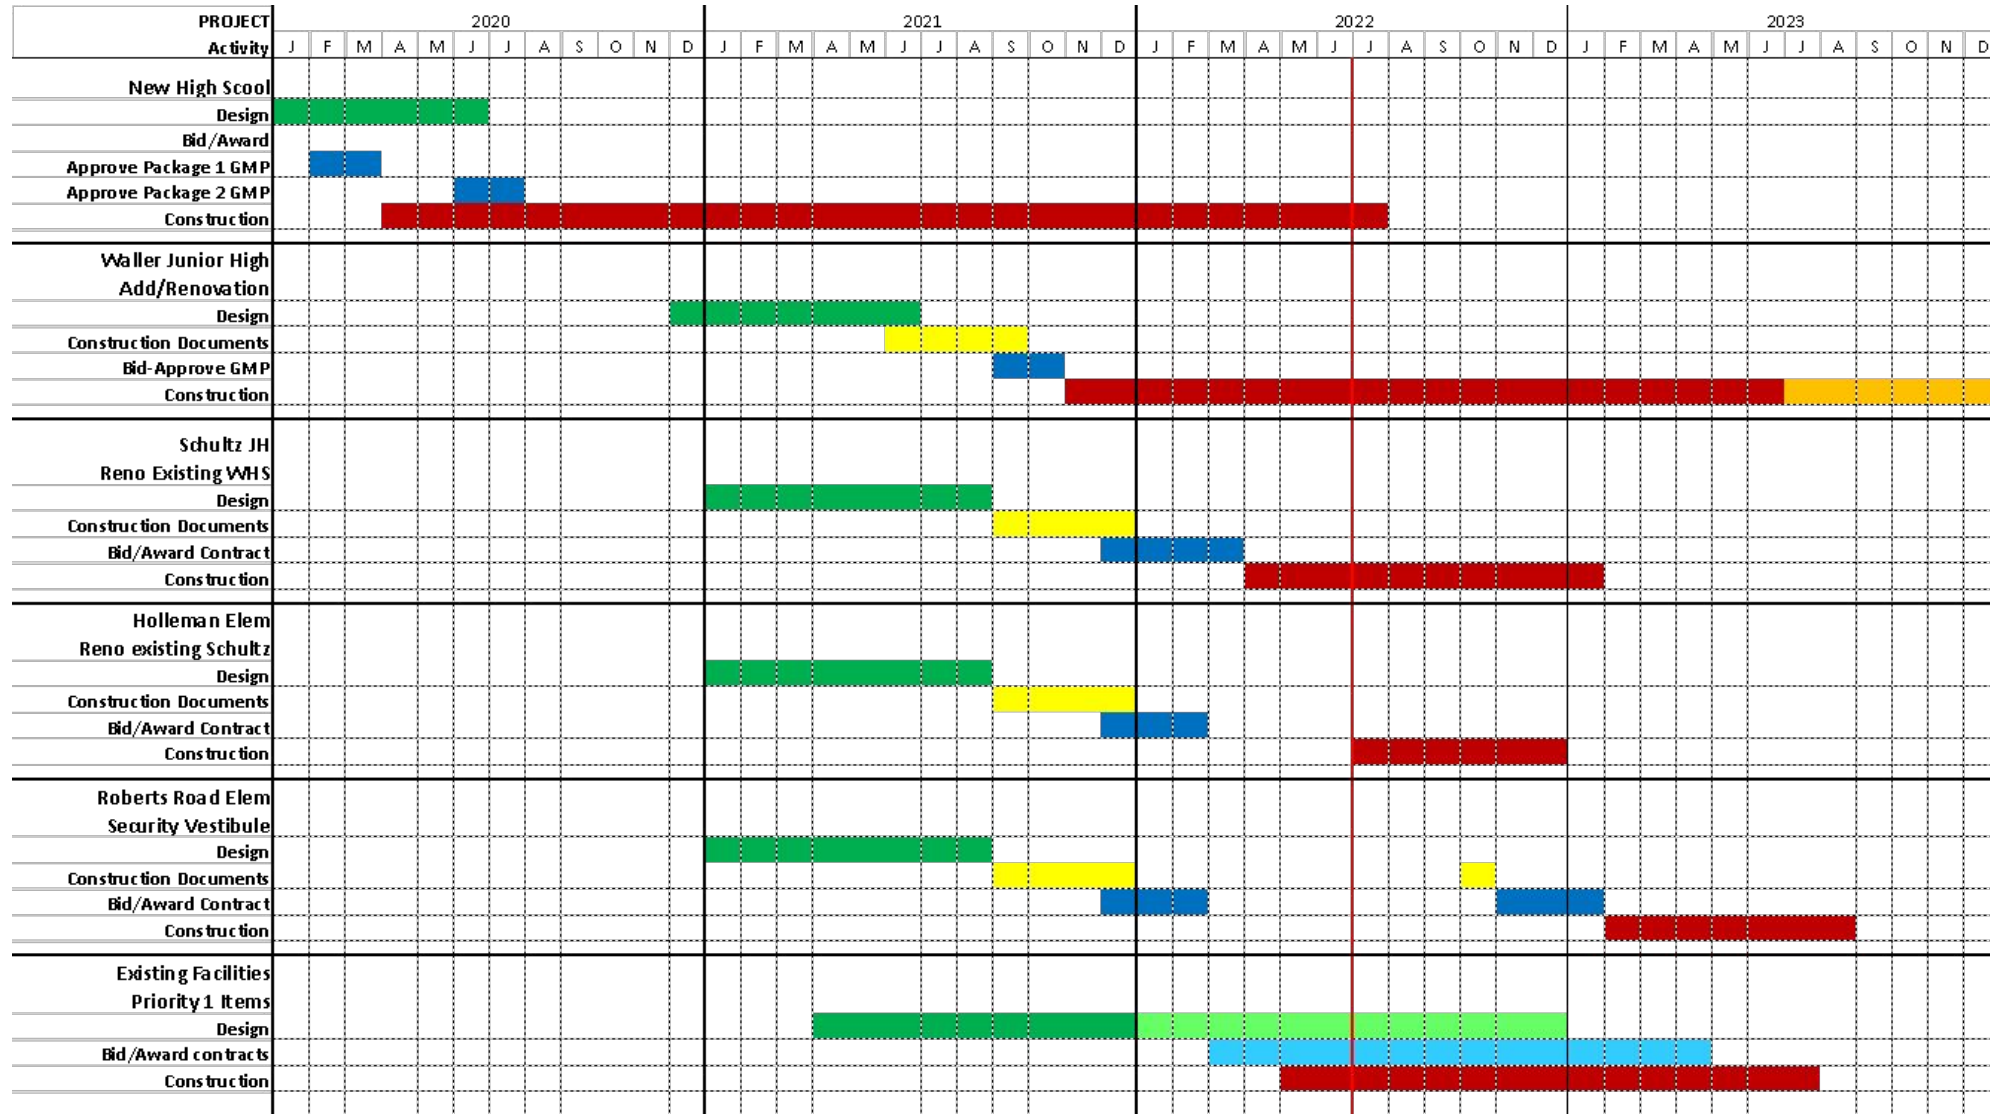



# 2019 Bond Project Update

---

## July 2022

- ❖ **New Waller High School - Substantial completion in July 2022.**
  - Remains On Budget and On Schedule for August 2022 opening.
  - Substantial Completion anticipated August 1
  - Furniture deliveries ongoing started and teacher's materials are being moved.
- ❖ **Waller Junior High School Renovations and Additions**
  - Project is On Budget and On Schedule for opening Phase 1 in August 2023.
  - Steel erection complete.
- ❖ **Schultz JH Renovation**
  - Steel erection complete.
- ❖ **Holleman, and Roberts Road Renovations**
  - Projects have been bid. Contracts are being reviewed and preconstruction activities started.


# NEW HIGH SCHOOL CONSTRUCTION UPDATE



*Waller*  
Independent School District



# New Waller High School

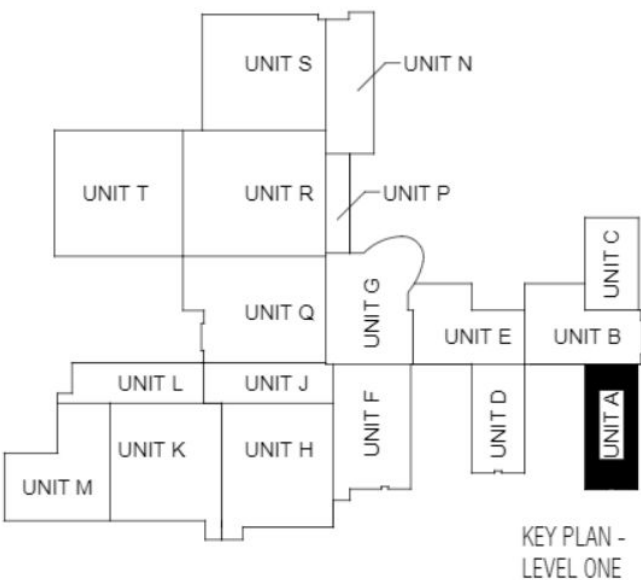

Floor Plan

# 2019 Bond Project Update



## Front Entry



# 2019 Bond Project Update


## Auditorium





# 2019 Bond Project Update

## Central Staircase

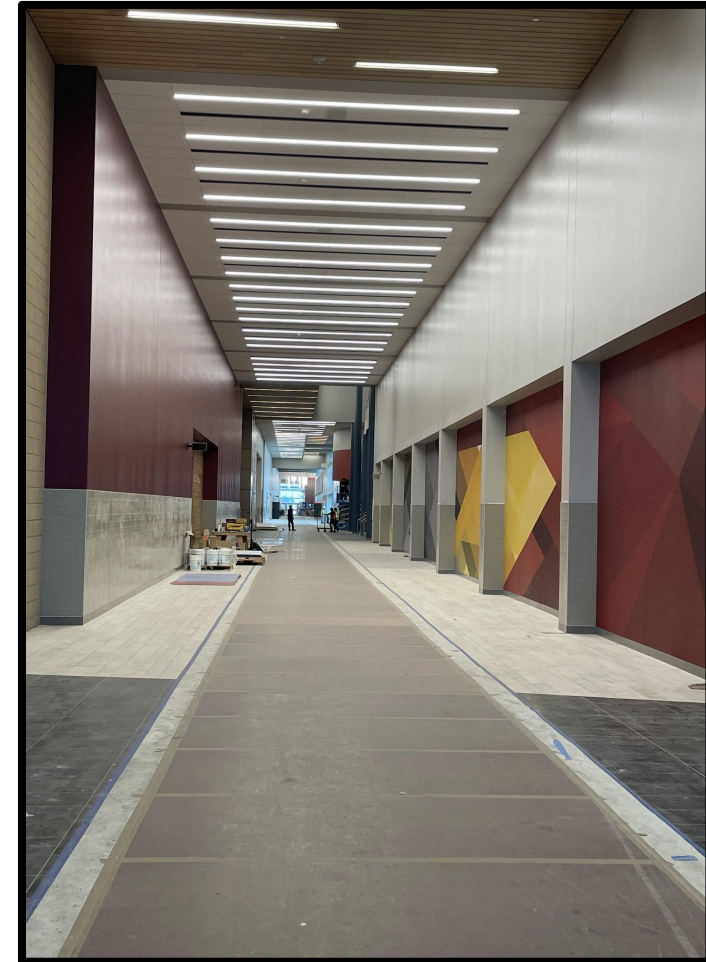

## Main Hallway



# 2019 Bond Project Update



## Cafeteria and Classroom Furniture




# 2019 Bond Project Update



## Wall Graphics and Coffee Bar




# 2019 Bond Project Update

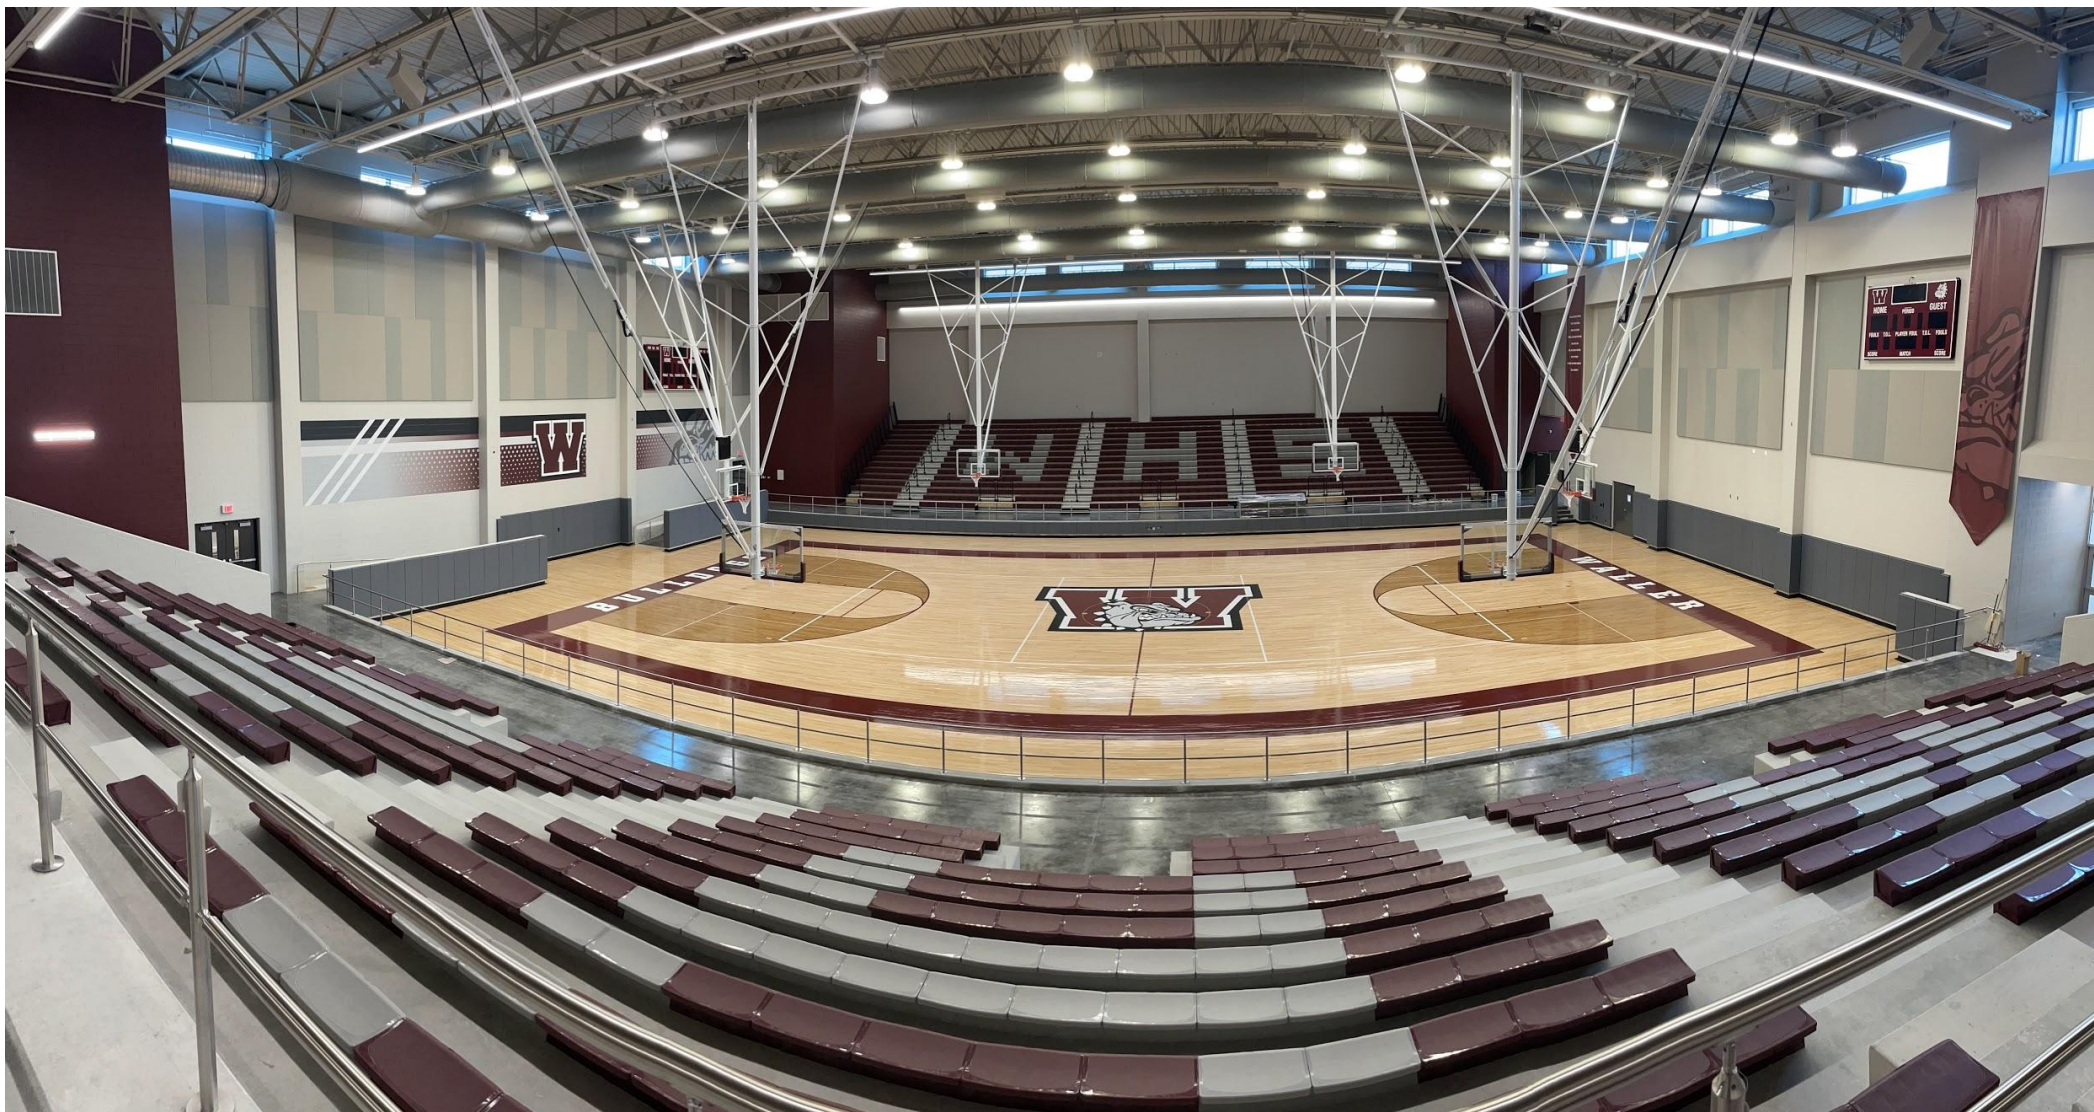



# 2019 Bond Project Update

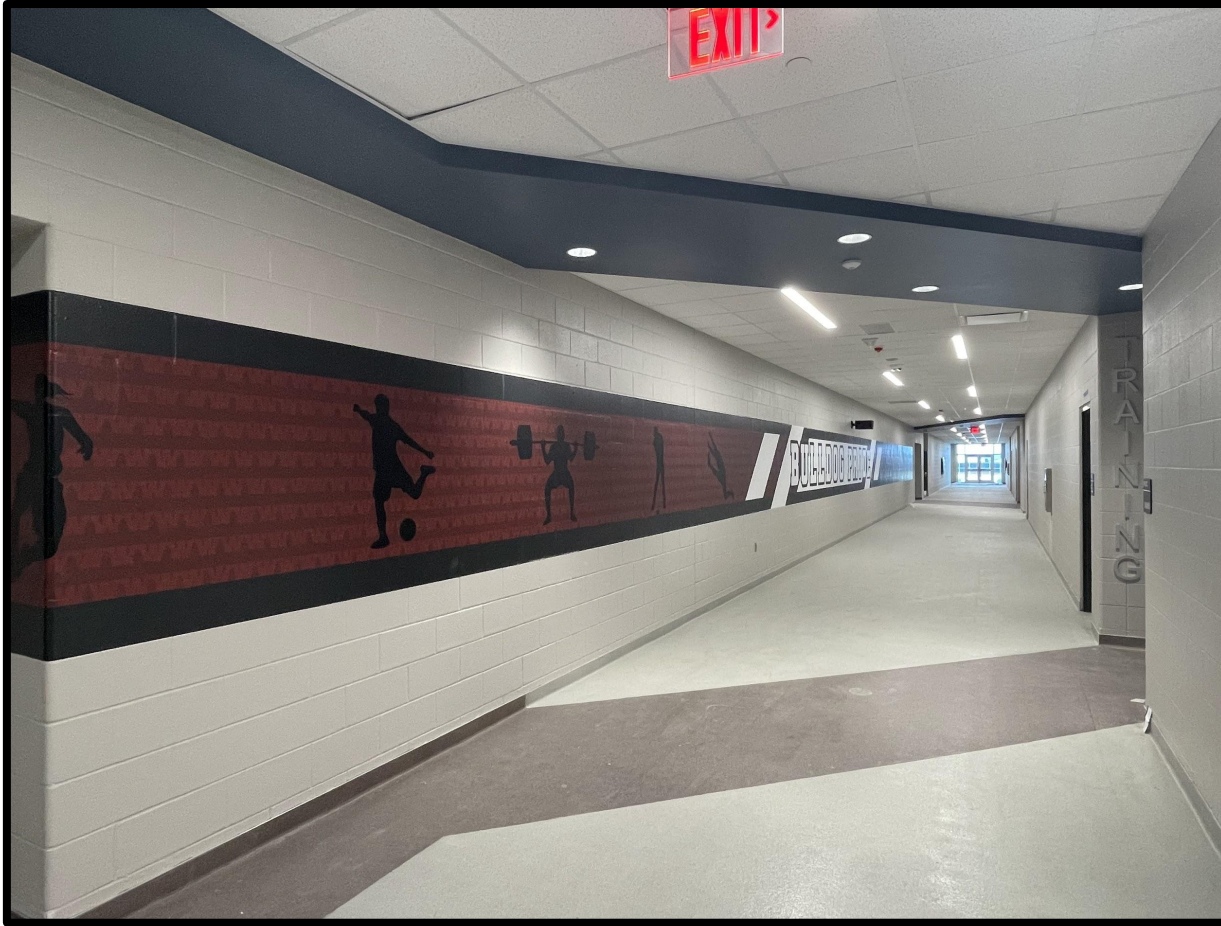

## Athletics Hallway and Wrestling Signage



# 2019 Bond Project Update

**Learning Stairs**



**Gym Lobby**



# 2019 Bond Project Update



**Classroom and  
Black Box**



# 2019 Bond Project Update



**Band Hall**



**Instrument  
Storage**



# 2019 Bond Project Update



**Aquatics Class**



**Pharmacy Tech Lab**



# 2019 Bond Project Update

---



**Front Landscape Area**



# 2019 Bond Project Update

---



## 2nd Floor NE Collaboration Space



# Project Update - New Waller High School

---

## Construction Activity Status

VLK has issued punch lists for 1st, 2nd, and 3rd floor classroom areas.

- All Life-Safety inspections compete and passed (fire alarm, sprinkler systems, etc)
- Waiting on the city of Waller to issue Certificate of Occupancy.
- Drymalla is working on final cleaning and punch lists items.
- Substantial Completion is planned on August 1<sup>st</sup>.
- Roadwork on Waller Spring Creek and Stokes Road is 99% complete.
- Harris County Health Dept is scheduled to inspect kitchens.
- Auditorium rigging complete. Lighting and local sound remaining.
- Wall graphics are ongoing.
- Intrusion alarm system operational.
- Security Cameras have been installed by WISD.
- Access control system installation is being finalized and being programed by WISD.
- Building Commissioning agent finalizing their review for building certification.

# WALLER JUNIOR HIGH CONSTRUCTION UPDATE





# 2019 Bond Project Update



**WJH Main Building  
North Rear Elevation**



# 2019 Bond Project Update

---



## WJH Cafeteria Elevation



# 2019 Bond Project Update



## Front WJH Entry Driveway and Parking



# 2019 Bond Project Update



**Bus Loop near Admin**



**SW Corner**



# 2019 Bond Project Update



**Main Staircase**



**Fire Protection**




# 2019 Bond Project Update



## Mechanical and Electrical



# 2019 Bond Project Update

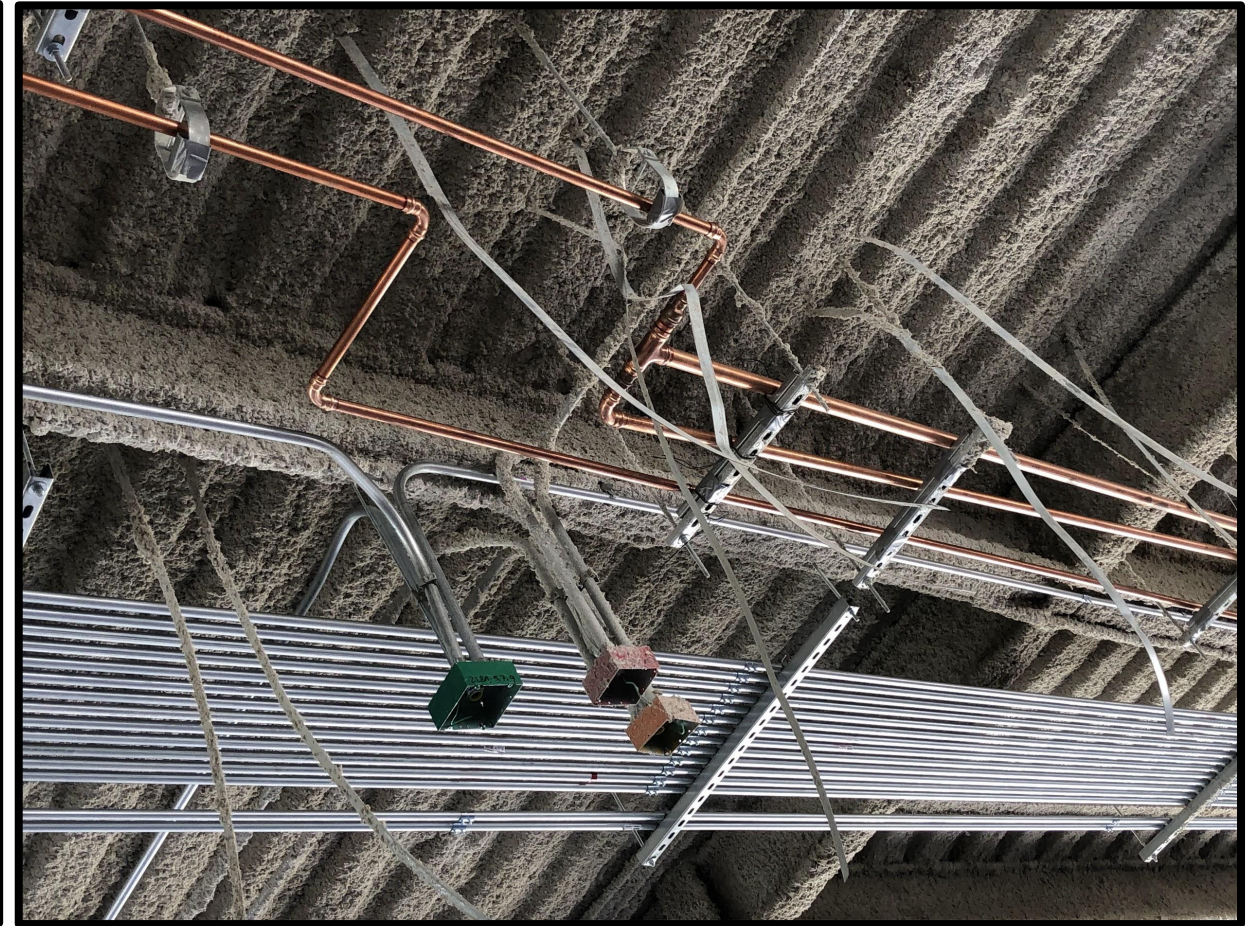

## Piping and Conduits



# 2019 Bond Project Update



**East Gym Reno**



**CMU Locker Room Wall**

# 2019 Bond Project Update

---

- Phase 1A summer paving in front of school is 95% complete.
- East Gym bleachers and lockers are on site.
- Gym renovation work is pending air handler deliveries.
- Gym wood refinishing and Epoxy locker room floors waiting on conditioned air.
- Slab pour is 90% complete with only the auxiliary gym remaining.
- Steel erection is complete, with minor detailing remaining and ongoing.
- 2<sup>nd</sup> Floor slab on deck concrete complete in the classroom addition.
- Metal roof deck is 80% complete.
- MEP rough-in has started on both 1st and 2nd floors of classroom addition.
- Transportation radio tower has been removed.




# SCHULTZ JUNIOR HIGH CONSTRUCTION UPDATE



*Waller*  
Independent School District

# 2019 Bond Project Update

PHASING PLAN  
PRIME CONTRACTORS, INC.  
02 June 2022

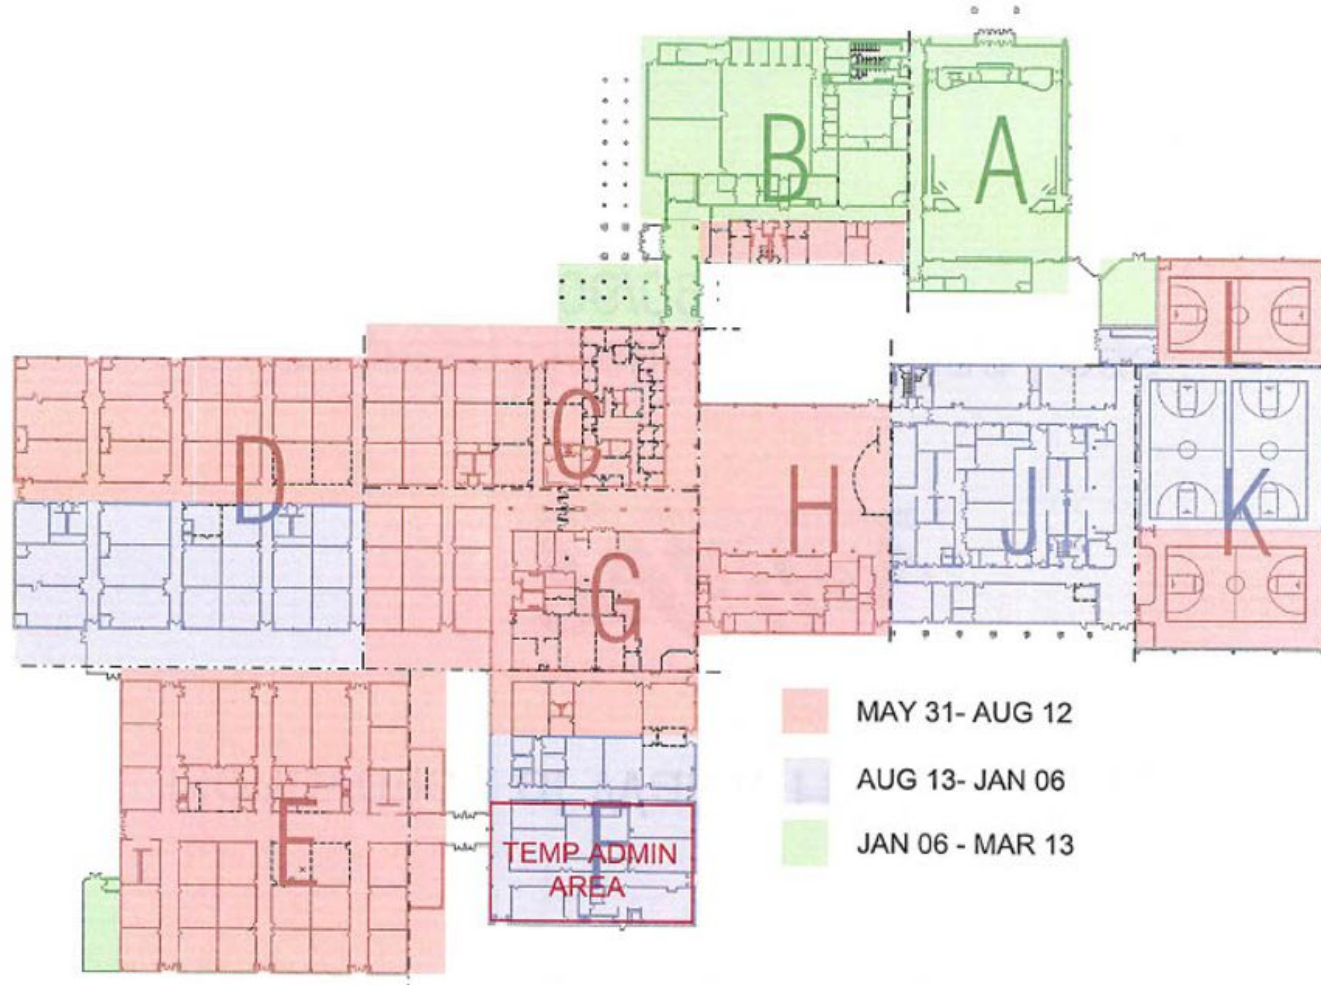




# 2019 Bond Project Update

## FIRE SPRINKLER SYSTEM LAYOUT

- SYSTEM #1 - EXISTING
- SYSTEM #2 - EXISTING
- SYSTEM #3 - NEW (TO BE ADDED)
- SYSTEM #4 - NEW (TO BE ADDED)
- SYSTEM #5 - NEW (TO BE ADDED)
- SYSTEM #6 - NEW (TO BE ADDED)

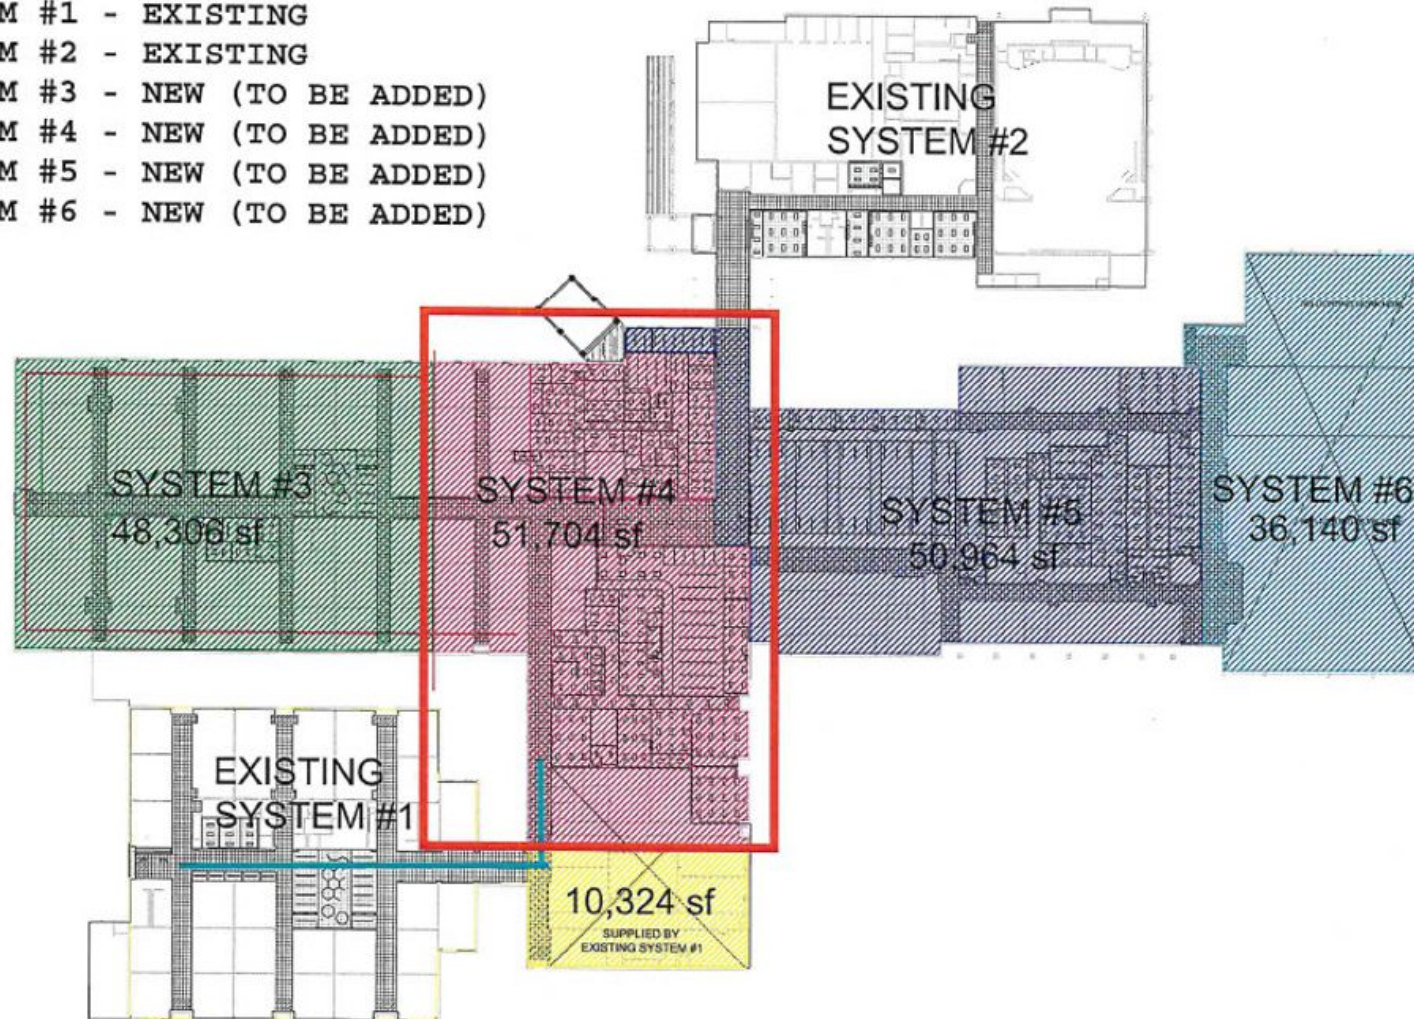



# 2019 Bond Project Update



## Entry Vestibule and Front Office Area



# 2019 Bond Project Update



**Nurse's Office**



**Admin Area Kitchenette**



# 2019 Bond Project Update



**Registrar Office**



**Classroom Flooring Tile**



# 2019 Bond Project Update



## Cafeteria



# 2019 Bond Project Update



**Library**



# 2019 Bond Project Update



**LGI Room**



**300 Hallway**



# 2019 Bond Project Update



**200 Hallway Collab Area**



**100 Hallway**



# 2019 Bond Project Update



**Hallway in front of Library**



**Old Receptionist Area**



# 2019 Bond Project Update



## Exterior



# Thank You!

