

2019 BOND

UPDATE


September 2021



Project Budgets

New Waller High School	\$ 195,019,130
Waller JH Renovation & Addition	\$ 61,922,314
Schultz Junior High (renovate existing WHS)	\$ 7,104,030
Holleman Elementary (renovate Schultz JH)	\$ 3,674,716
Roberts Road Elementary Vestibule	\$ 978,242
Other campus renovations (Priority 1)	\$ 3,231,093
Others (buses, tech., land, etc.)	\$ 23,295,476
TOTAL	\$ 295,225,000

2019 Bond Planning Schedule

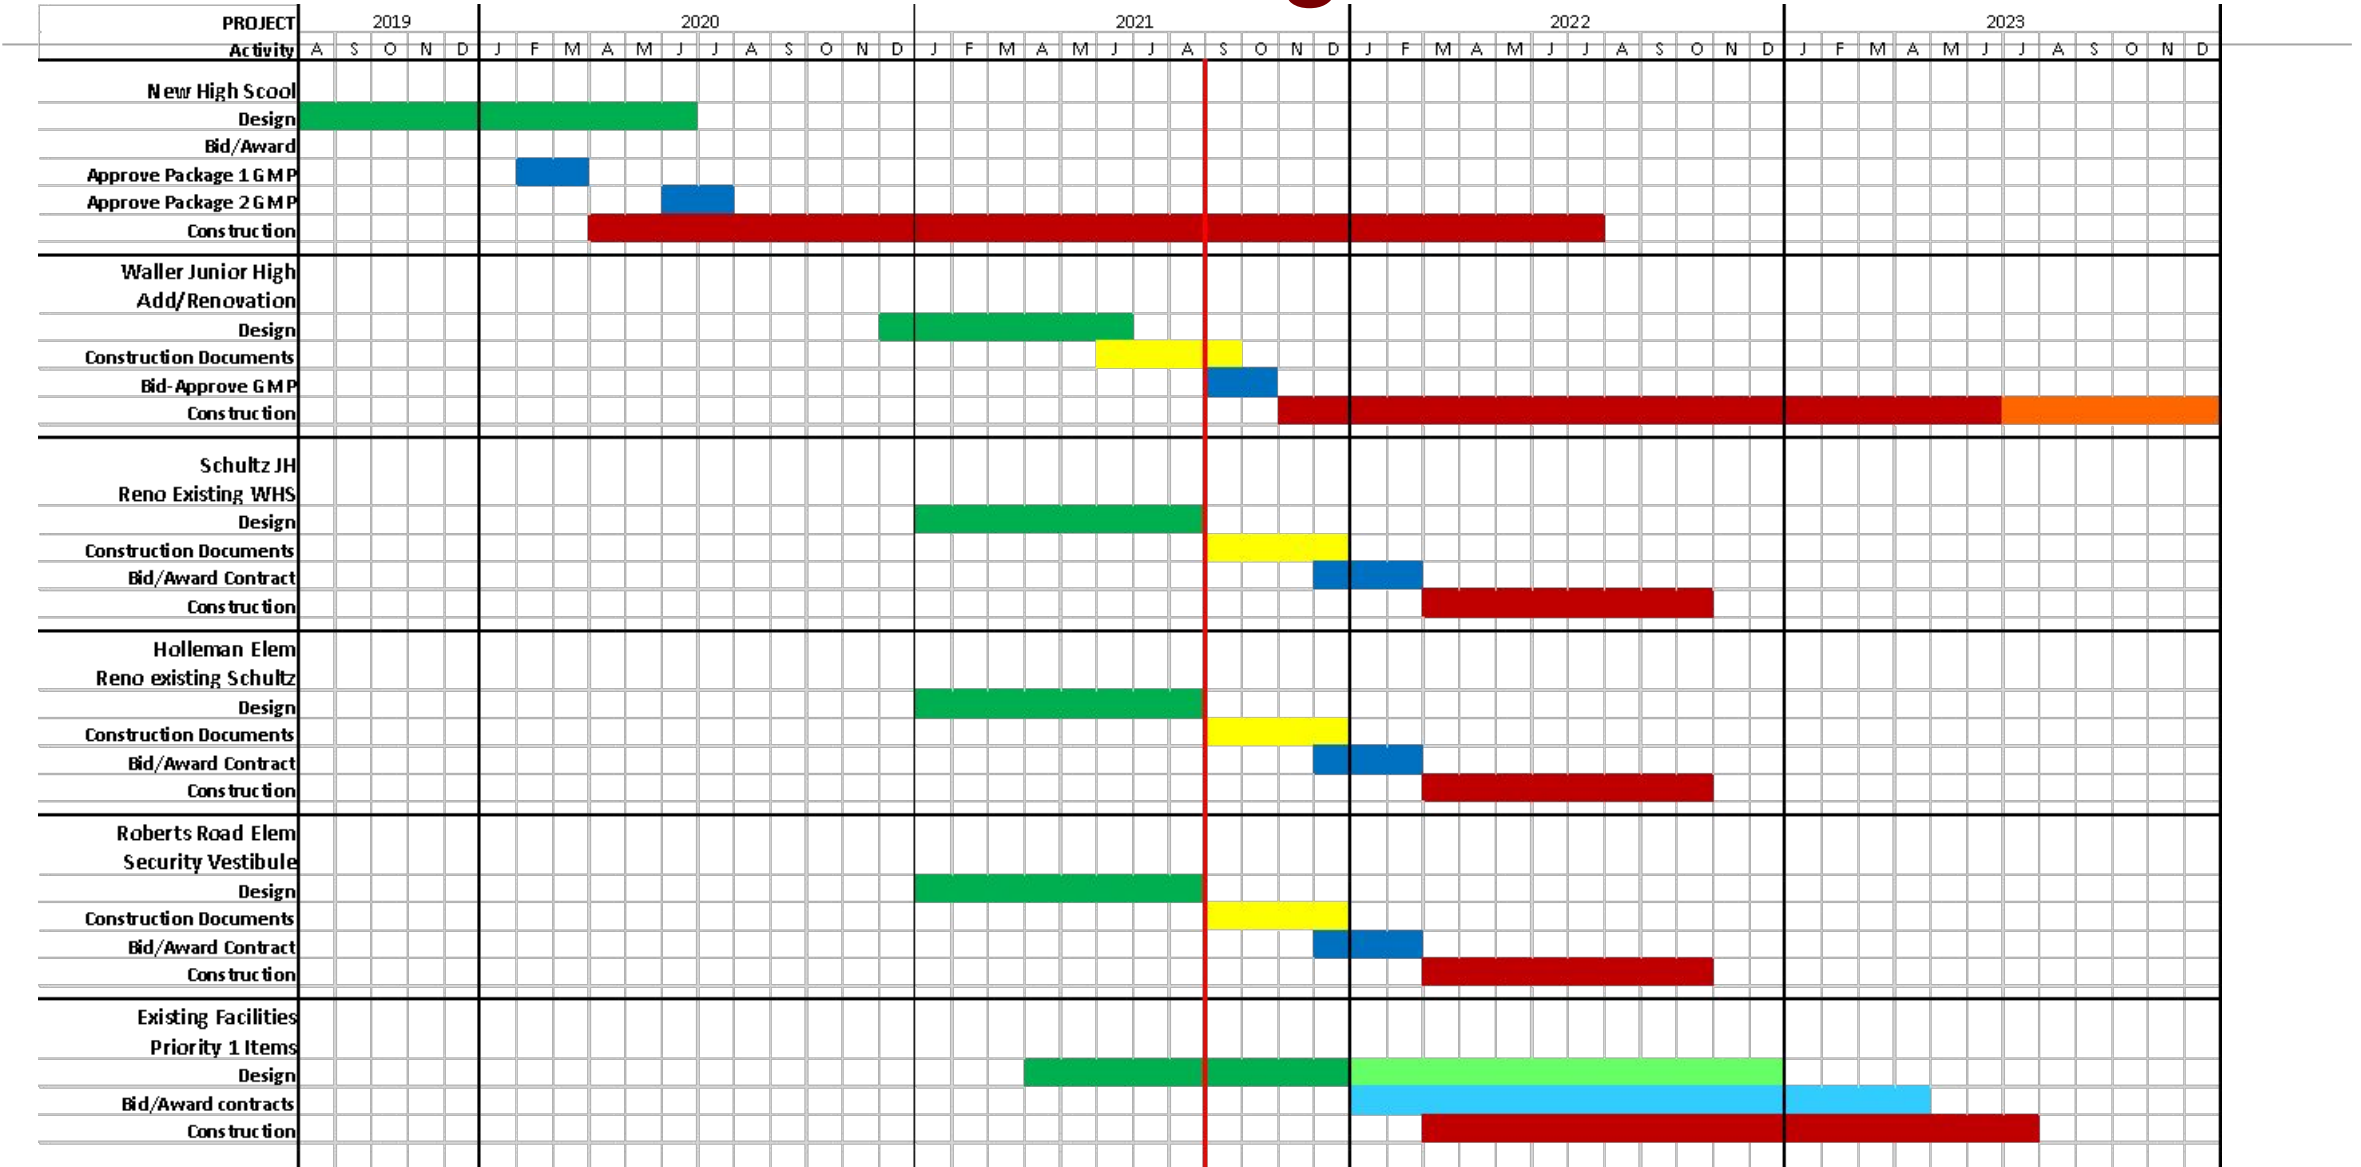

2019 Bond Project Update

September 2021


- ◆ **New Waller High School** - under construction and approximately 70% complete.
 - Remains on Budget and On Schedule for August 2022 opening.
 - Permanent Power in August with Conditioned Air schedule to commence in September.
 - Baseball and Softball reconstruction in progress and schedule to complete by Dec. 31st.
- ◆ **Waller Junior High School Renovations and Additions** –
 - Plans submitted to city for permitting and Construction Manager bidding.
 - Drymalla to receive subtrade quotes on September 22, 2021.
 - Drymalla to provide GMP for the October 2021 board meeting for WISD approval.
- ◆ **Schultz, Holleman, and Roberts Road Renovations**
 - Design Development is complete and VLK presentation to the Board in September.
 - Projects are scheduled to bid in January to award contracts in February.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

New Waller High School

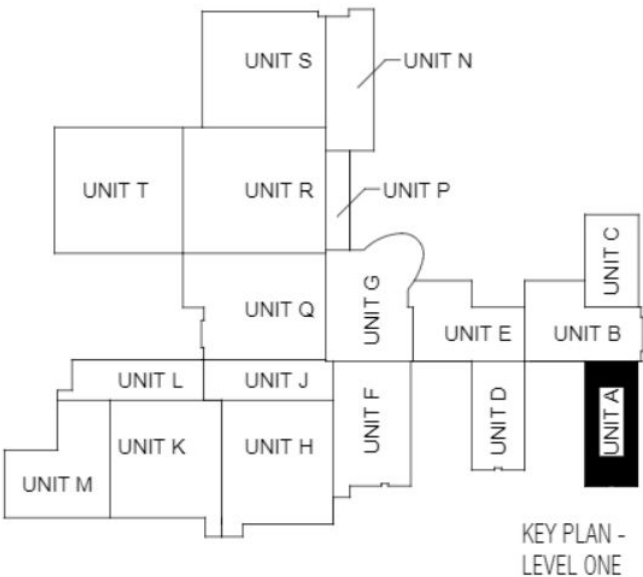

Floor Plan

2019 Bond Project Update

Southeast Elevation



Gym Lobby



2019 Bond Project Update



Auditorium



2019 Bond Project Update



Large Cafeteria



Central Staircase

**2nd Floor
Guardrails**



2019 Bond Project Update



Science Casework

2019 Bond Project Update

Educational Casework



2019 Bond Project Update



Central Plant



2019 Bond Project Update



Baseball and Softball complex



Project Update - New Waller High School

Construction Activity Status

- Baseball-Softball Reconstruction ongoing for December completion
- MEP interior rough-in remains ongoing
- Metal wall framing, gypsum, and ceiling grid are still going
- Interior CMU block walls are nearly complete
- Exterior brick ongoing on the northwest and southwest facades
- Base coat of wall paint complete in classroom areas, ongoing in athletic areas
- Restroom wall tile is ongoing, and prepping for wainscot in corridors
- Classroom and Metal Science Lab casework being delivered and installed
- Data cabling continues, and equipment racks being set in IDF/MDF closets.
- Final roof section above auditorium seating being installed.
- Building Envelope Commissioning is ongoing
- Temporary A/C started and HVAC flushing wrapping up
- Energized Permanent Power in August

Thank You!

