

Bond Update


February 8, 2016

Agenda:

- Bond Summary
- Project by Project Update
- Interior and Exterior Colors and Finishes (CTE & Ag)
- Roberts Road Site Layout
- Contractor Selection Criteria/Committee
- Questions / Suggestions



Bond Summary:



Total Expenditures to Date

- \$71,320,000 Budget
- \$3,022,253 Encumbered
- 4% Complete

Schedules

- Package A (Jones, RR, CTE, & Ag.)
 - On Schedule
 - Out to Bid 2/25/16
 - Complete by Fall 2017
- Package B (Schultz & Bus Paving)
 - On Schedule
 - Out to Bid 4/26/16
 - Complete by January 2017
- Package C (Schultz Mechanical/Electrical)
 - On Schedule (Start Design Fall 16)
 - Out to Bid 2/21/17
 - Complete by Fall 2018
- Miscellaneous (Portables, Paving, Buses, Technology)
 - Portables (3 purchased 6 pending)
 - Stadium Parking Complete
 - Bus Purchases (10 ordered)
 - Technology and Access Control TBD

Jones Elementary School:



Project Update

- Contract Documents 98% Complete
- Topographic Survey Complete

Budget Review

• \$24,860,000.00

Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- On Schedule for Fall 2017 Open

Look Ahead

Contractor Selection Criteria

Roberts Road Addition:



Project Update

- Contract Documents 98% Complete
- Traffic Study
- Door Color / Paint

Budget Review

• \$4,290,175+\$2,439,136 = \$6,729,311


Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- On Schedule for Fall 2017 Open

Look Ahead

Contractor Selection Criteria

High School CTE & Ag:

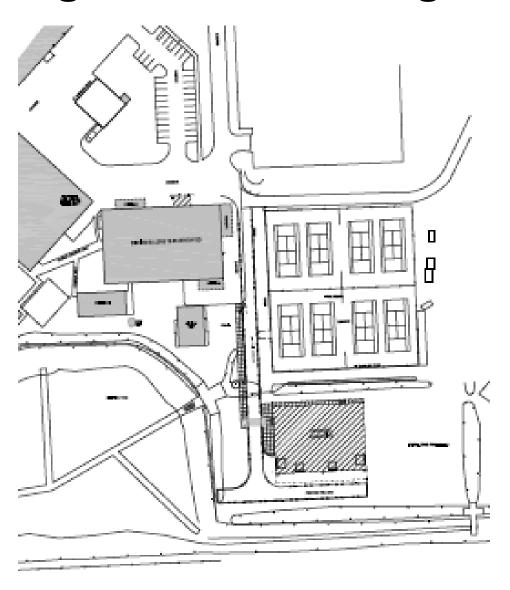

Project Update

- Contract Documents 75% Complete
- Survey (Topographic)
- Geotechnical Investigations

Budget Review

• \$4,019,120

Schedule

- Out to Bid 2/25/16
- Receive Proposal 3/24/16
- Award Construction Contract 4/11/16
- Ahead of Schedule for Fall 2017 Open

Look Ahead

Board Update 2/8/16 – Final Site Design

High School CTE & Ag:

Exterior Building Sketch // Agricultural Sciences Building





Schultz Tennis & Track:

Project Update

Schematic Design 100% Complete

Budget Review

• \$2,895,225


Schedule

- Out to Bid 4/26/16
- Receive Proposal 5/24/16
- Award Construction Contract 6/03/16
- Ahead of Schedule for 1/17 Open

Look Ahead

Receive Proposals May 24th

Thank You . . .



New Elementary School

(July 2015 - July 2017)

Robert's Road Addition

(August 2015 - July 2017)

Waller High School CTE / Ag

(August 2015 - July 2017)

Schultz Tennis Courts and Track

(January 2016 - August 2016)

Additional Bus Parking


(January 2016 - August 2016)

Mechanical / Electrical

(February 2016-August 2016???)

Miscellaneous (Portables, Technology, Buses, Etc.)
(Ongoing)

Packaging Projects:



r ISD Pi	roject	Summary		\$71,320,0	00.00
2015 Bo	nd		\$ 71,322,871.00	(Actual Bo	nd Amount
Student G	rowth		\$ 44,075,000.00		
	New Elen	nentary #6			\$ 30,500,000
		Buildings			\$ 720,000
	Land Ag	_			\$ 6,525,000
		Two Elementary S	ichools		
		One Junior High S	ichool		
		One High School			
	Roberts F	Road Elementary S	chool Additions		\$ 6,330,000
Facility Ad	lditions a	nd Renovations	\$ 16,250,000.00		
	Waller Hi	gh School CATE/A	g Building		\$ 5,320,000
		Existing CATE/AG	Building		
			Renovate Existing S	Shops	
		New CTE/Ag Build			
				oms, Locker Rooms	
	Facility A	ssesment – Carpet I	, Mechanical, Electric	al and Plumbing	\$10,930,000
Transporta			\$ 4,349,871.00		
	Busses F	Replacement and r	iew		\$ 3,849,87
		30 Regular Educa	ation Busses		
		9 Special Needs (Busses		
	Additiona	al Parking			\$ 500,000
Technolog	zv.		\$ 3,008,000.00		
	MDF Upg	rades at 8 Campus	ses		\$ 370,000
	IDF Upgr	ades at 8 Campuse	es		\$ 500,000
	Wireless	Accsess Points			\$ 708,000
	Compute	r Replacements			\$ 1,430,000
Athletics			\$ 2,890,000.00		
	Waller ISI	D Stadium – Crushe	ed Concrete Parking		\$ 210,000
Scultz Junior Hi		ınior High School -	_		\$ 1,780,000
:	Scultz Ju	ınior High School -	Tennis		\$ 900,000
Safety and Security		\$ 750,000.00			
	New Security Cameras and				\$ 250,000
I	Card Rea	ader's at All Access	: Points		\$ 500,000

Projects/Budgets:

