


2019 BOND

UPDATE

January 2022



2019 Bond Planning Schedule

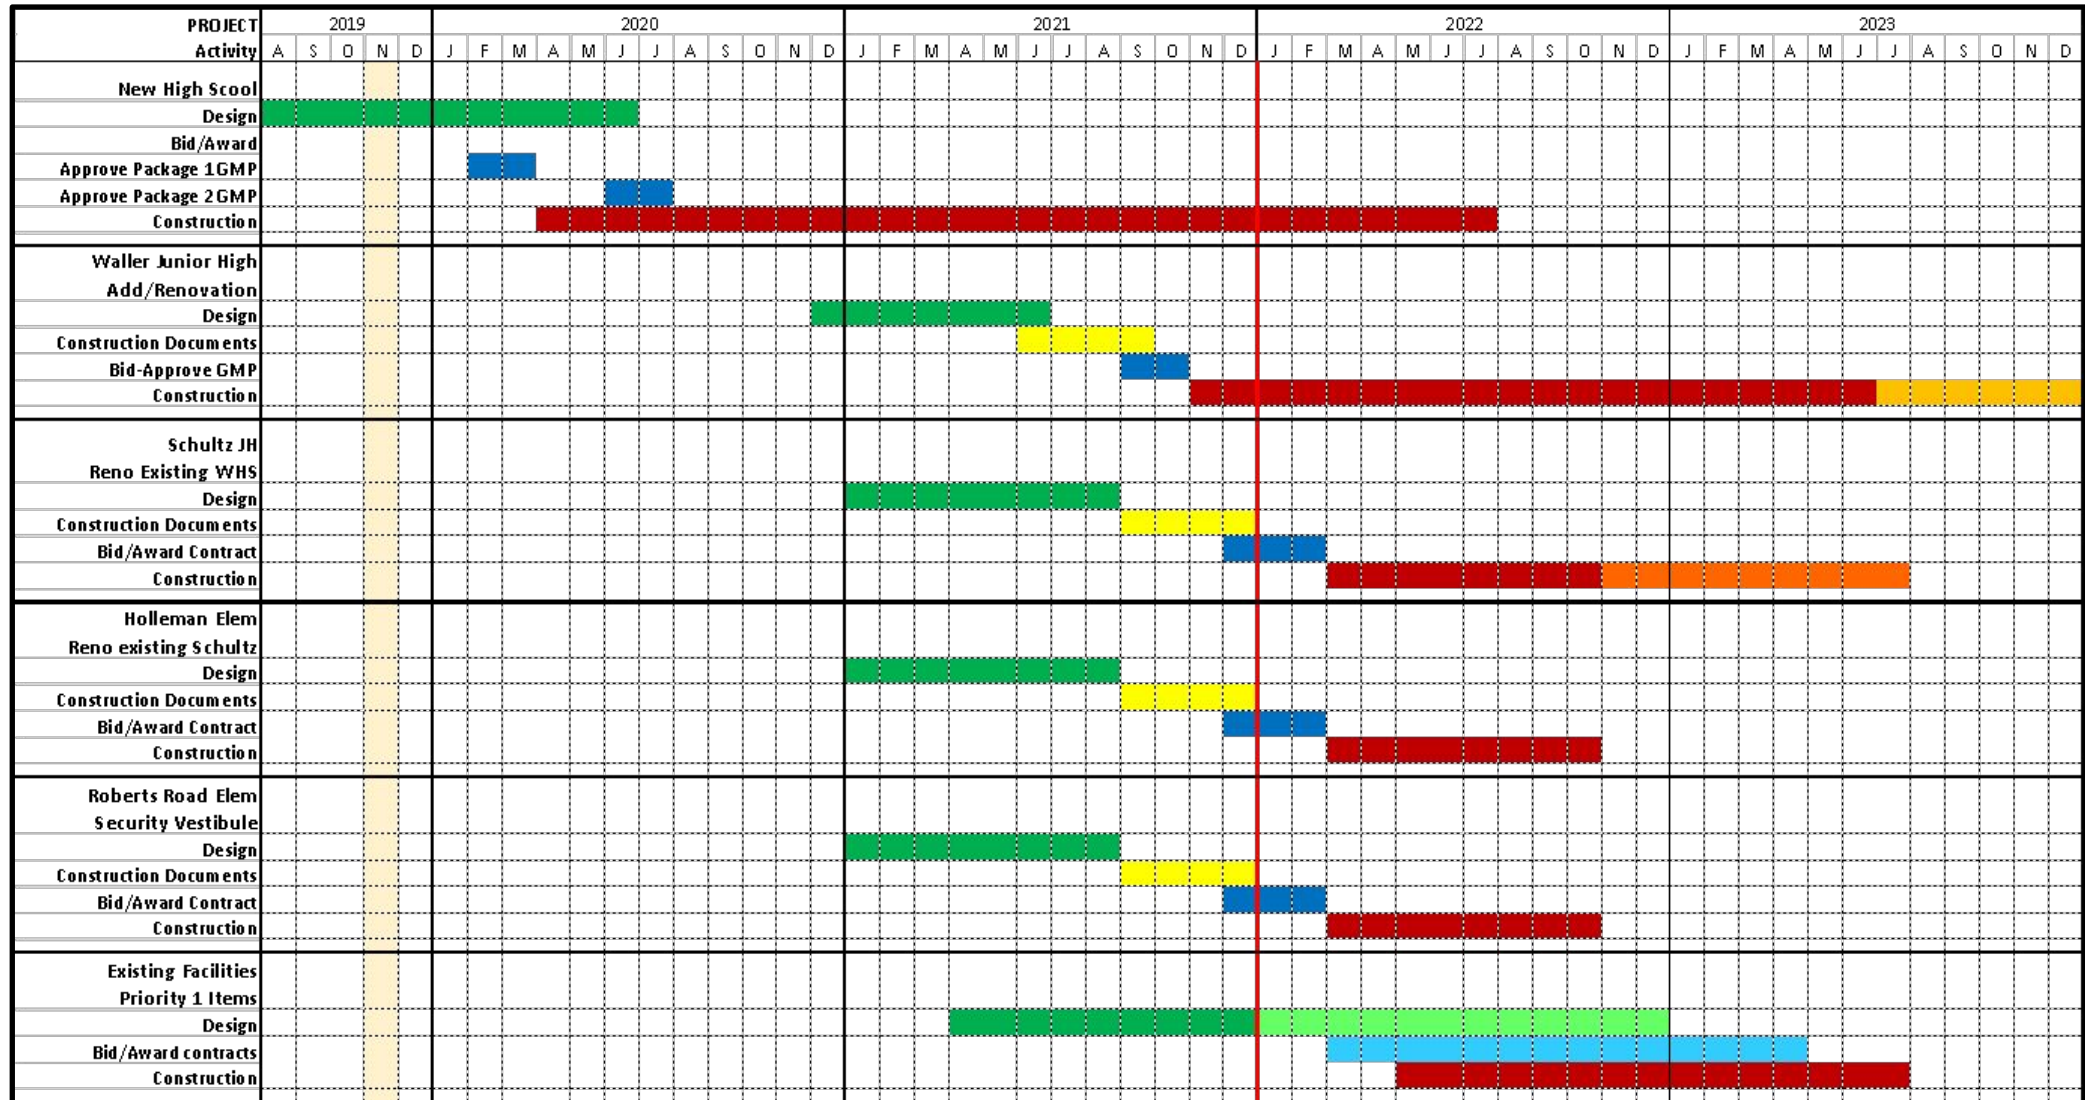

2019 Bond Project Update

January 2022 Update

- ❖ **New Waller High School** - under construction and approximately 84% complete.
 - ☐ Remains on Budget and On Schedule for August 2022 opening.
 - ☐ Baseball and Softball Complex reconstruction Substantially Complete 1/1/2022.
 - ☐ FF&E list being developed for balance of furniture and equipment.
- ❖ **Waller Junior High School Renovations and Additions**
 - ☐ Demolition of the Maintenance complex complete.
 - ☐ Asbestos Abatement and Demolition of Umland building complete.
 - ☐ Scheduled to remove existing foundations and installation of new drilled piers.
- ❖ **Schultz, Holleman, and Roberts Road Renovations**
 - ☐ Pre-Proposal meeting held January 6th with large contractor attendance.
 - ☐ Projects are scheduled to bids January 20th and 27th to award contracts in February.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update



Baseball – Softball Complex Rebuild

2019 Bond Project Update

Baseball – Softball Complex Rebuild



2019 Bond Project Update

Baseball – Softball Complex Rebuild



2019 Bond Project Update



Central Staircase

Restroom fixtures and partitions



Epoxy Flooring

2019 Bond Project Update




Life Skills



ROTC

2019 Bond Project Update

Culinary Lab

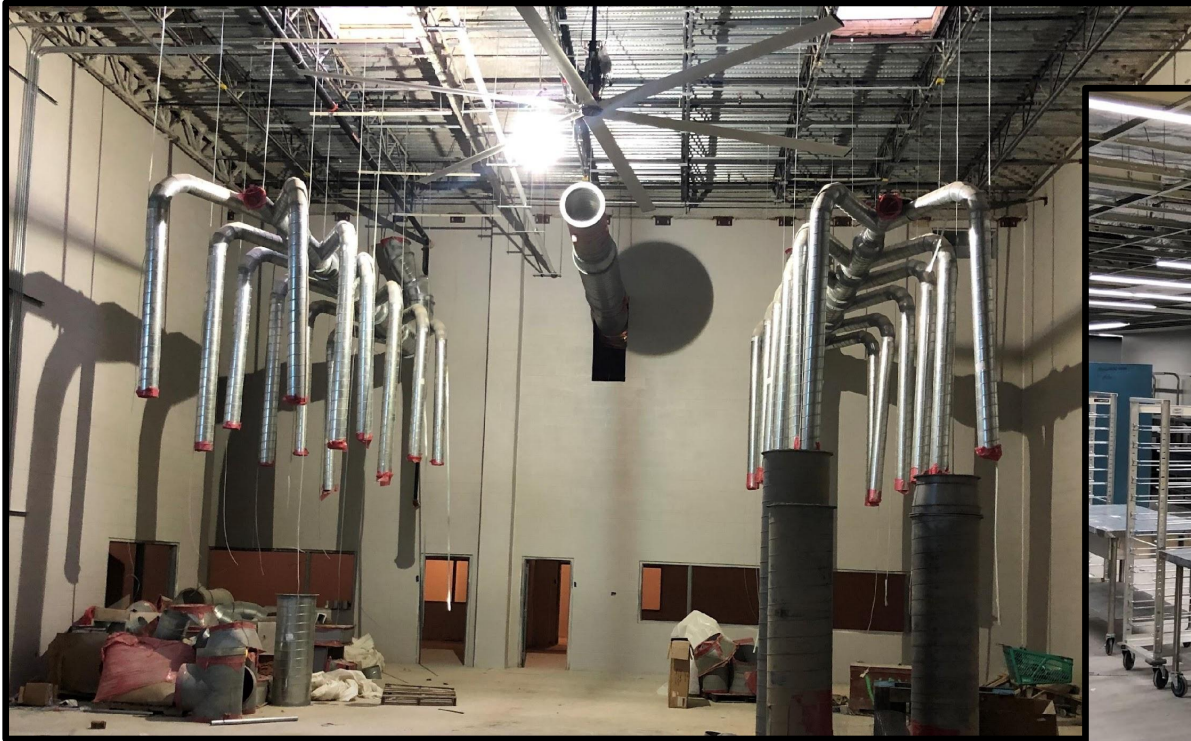

Welding Lab



2019 Bond Project Update




CTE Robotics Project Space



Project Update - New Waller High School

Construction Activity Status

- Baseball-Softball Complex is Substantially Complete.
- Kitchen equipment was delivered and being installed.
- Gym scoreboards are installed. Goals are in progress and wood floor is on site.
- Ceilings are being installed in high volume areas. (cafeteria, library, auditorium)
- Above ceiling punch list being corrected before ceiling cover-up.
- Restroom and hallway wainscot wall tile remains ongoing.
- Metal Science Lab casework installation is 90% complete. Classrooms ongoing
- HVAC system Testing & Balance has in progress. Heating system was started.
- Building Envelope System Commissioning is ongoing.
- Site clean up continues and site irrigation is being installed.



DESIGN UPDATE
JUNE 14, 2021

WALLER JUNIOR HIGH

ADDITIONS AND RENOVATIONS

CONSTRUCTION UPDATE

Waller
Independent School District

2019 Bond Project Update



Demolition of Maintenance Buildings

2019 Bond Project Update



Umland Building Abatement

2019 Bond Project Update



Relocated Chillers



Relocated Utilities

2019 Bond Project Update



Umland Demolition

Project Update - Waller Junior High Renovation

Construction Activity Status

- Daugherty Street Closed for duration of Phase 1.
- 4 Pad-mounted Chillers relocated for temporary service.
- Demolition of Maintenance Buildings is complete.
- Temporary rerouted of power, gas, data, and communications during the break.
- Asbestos Abatement and Demolition of Umland Building complete.
- 3 Temporary Classroom buildings installed on West Campus and ready for move-in.
- Rerouted East-West Campus canopy to entry through new library corridor.
- Temporary plywood wall constructed between construction and East-West canopy.
- Removal of concrete foundations, slabs, and paving has started.
- Drilled Pier Foundations scheduled to begin.
- Underground Utilities layout and installation being prepared.

Thank You!

