

# 2019 BOND

# UPDATE

## December 2021



# 2019 Bond Project Update

---

## December 2021

- ◆ **New Waller High School** - under construction and approximately 82% complete.
  - Remains on Budget and On Schedule for August 2022 opening.
  - Baseball and Softball Complex reconstruction scheduled for December 31<sup>st</sup> completion.
  - Furniture (FF&E) and technology being purchased for summer delivery.
- ◆ **Waller Junior High School Renovations and Additions** –
  - Demolition of the Maintenance complex started.
  - Asbestos Abatement of Umland building during winter break.
  - Utility relocations by the city and CenterPoint ongoing.
  - Drymalla to relocate chillers and reroute power, data, and communications over break.
- ◆ **Schultz, Holleman, and Roberts Road Renovations**
  - Construction documents submitted and approved for permits.
  - Projects are scheduled to bid January 20 to award contracts in February.

# NEW HIGH SCHOOL CONSTRUCTION UPDATE

*Waller*  
Independent School District



# 2019 Bond Project Update



**East Aerial**



# 2019 Bond Project Update



## Front Aerial



# 2019 Bond Project Update



**East Student Elevation**



# 2019 Bond Project Update



**Large Cafeteria**



**Central Staircase**


**2nd Floor  
Guardrails**





# 2019 Bond Project Update

**Learning Stairs**

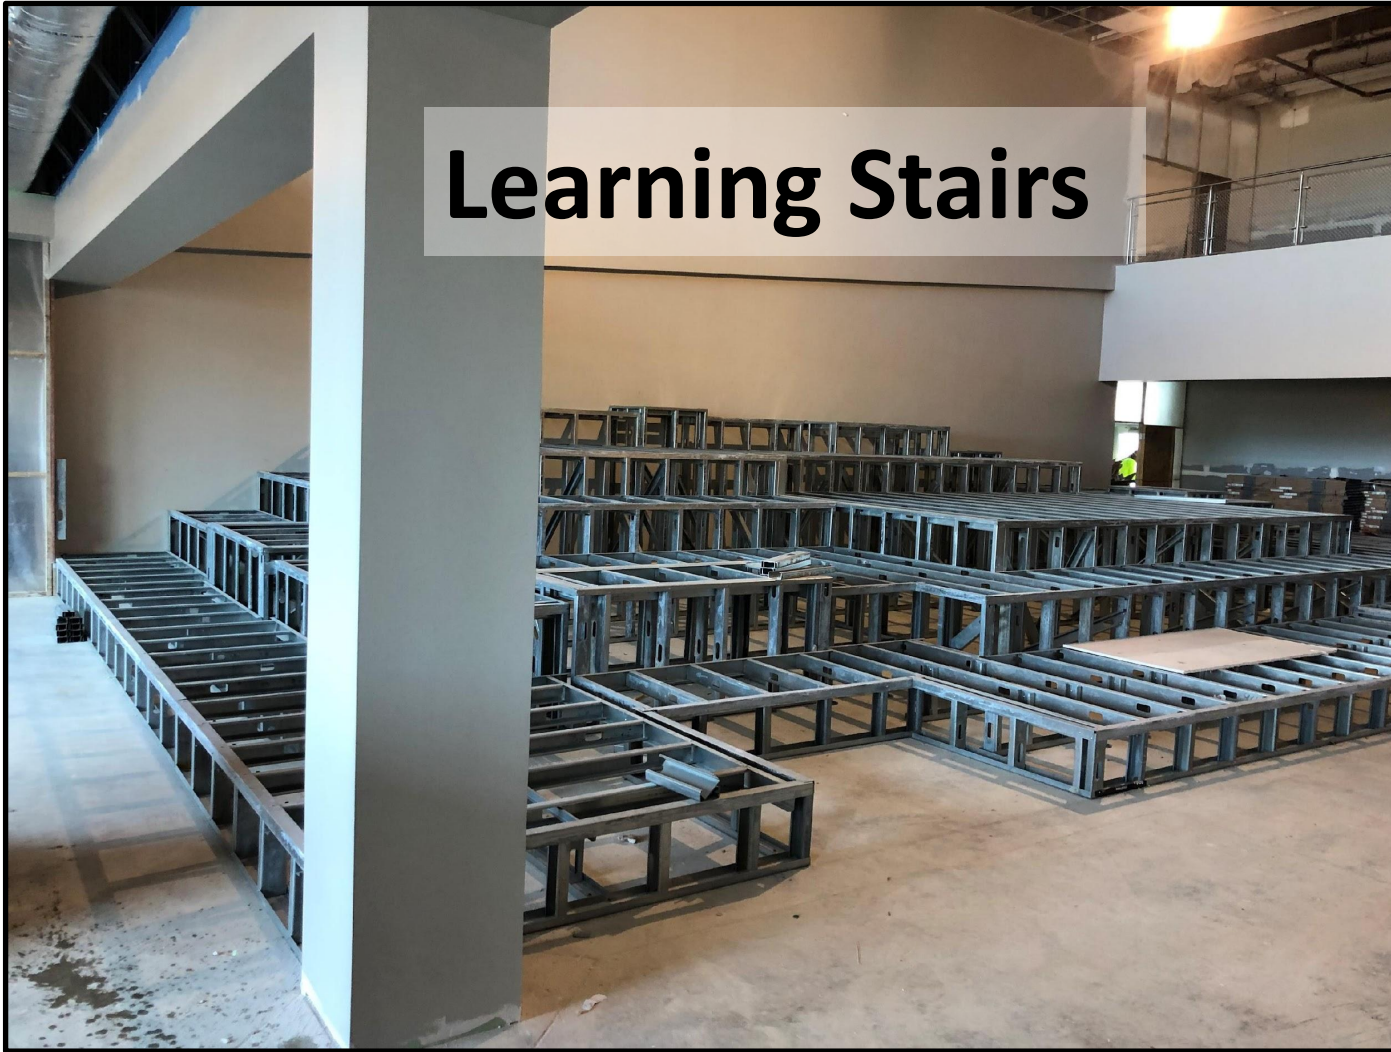

**2nd Floor  
Guardrails**



# 2019 Bond Project Update



**Science Casework**

# 2019 Bond Project Update

## Classroom Casework



## Cosmetology



# 2019 Bond Project Update



**Baseball and  
Softball complex**

# Project Update - New Waller High School

---

## Construction Activity Status

- Baseball-Softball fields grandstand complete, batting cages and dug out ongoing.
- Natural and synthetic turf installed for December completion
- Metal framing and gypsum walls are complete
- Ceiling grid complete in 3-story academic wing and started outgoing throughout.
- Above ceiling punch list being corrected before cover-up.
- Exterior brick is 99% complete with a few open locations
- Restroom wall tile hallway wainscot are ongoing.
- Metal Science Lab casework installation ongoing.
- Auditorium “dance floor” installed” and ceiling work started.
- Exterior windows are 98% installed, interior window have started.
- HVAC system Testing & Balance has started.
- Building Envelope System Commissioning is ongoing.
- Site clean up has started and sidewalks being installed.



# Thank You!

