


2019 BOND

UPDATE

February 2022



2019 Bond Planning Schedule

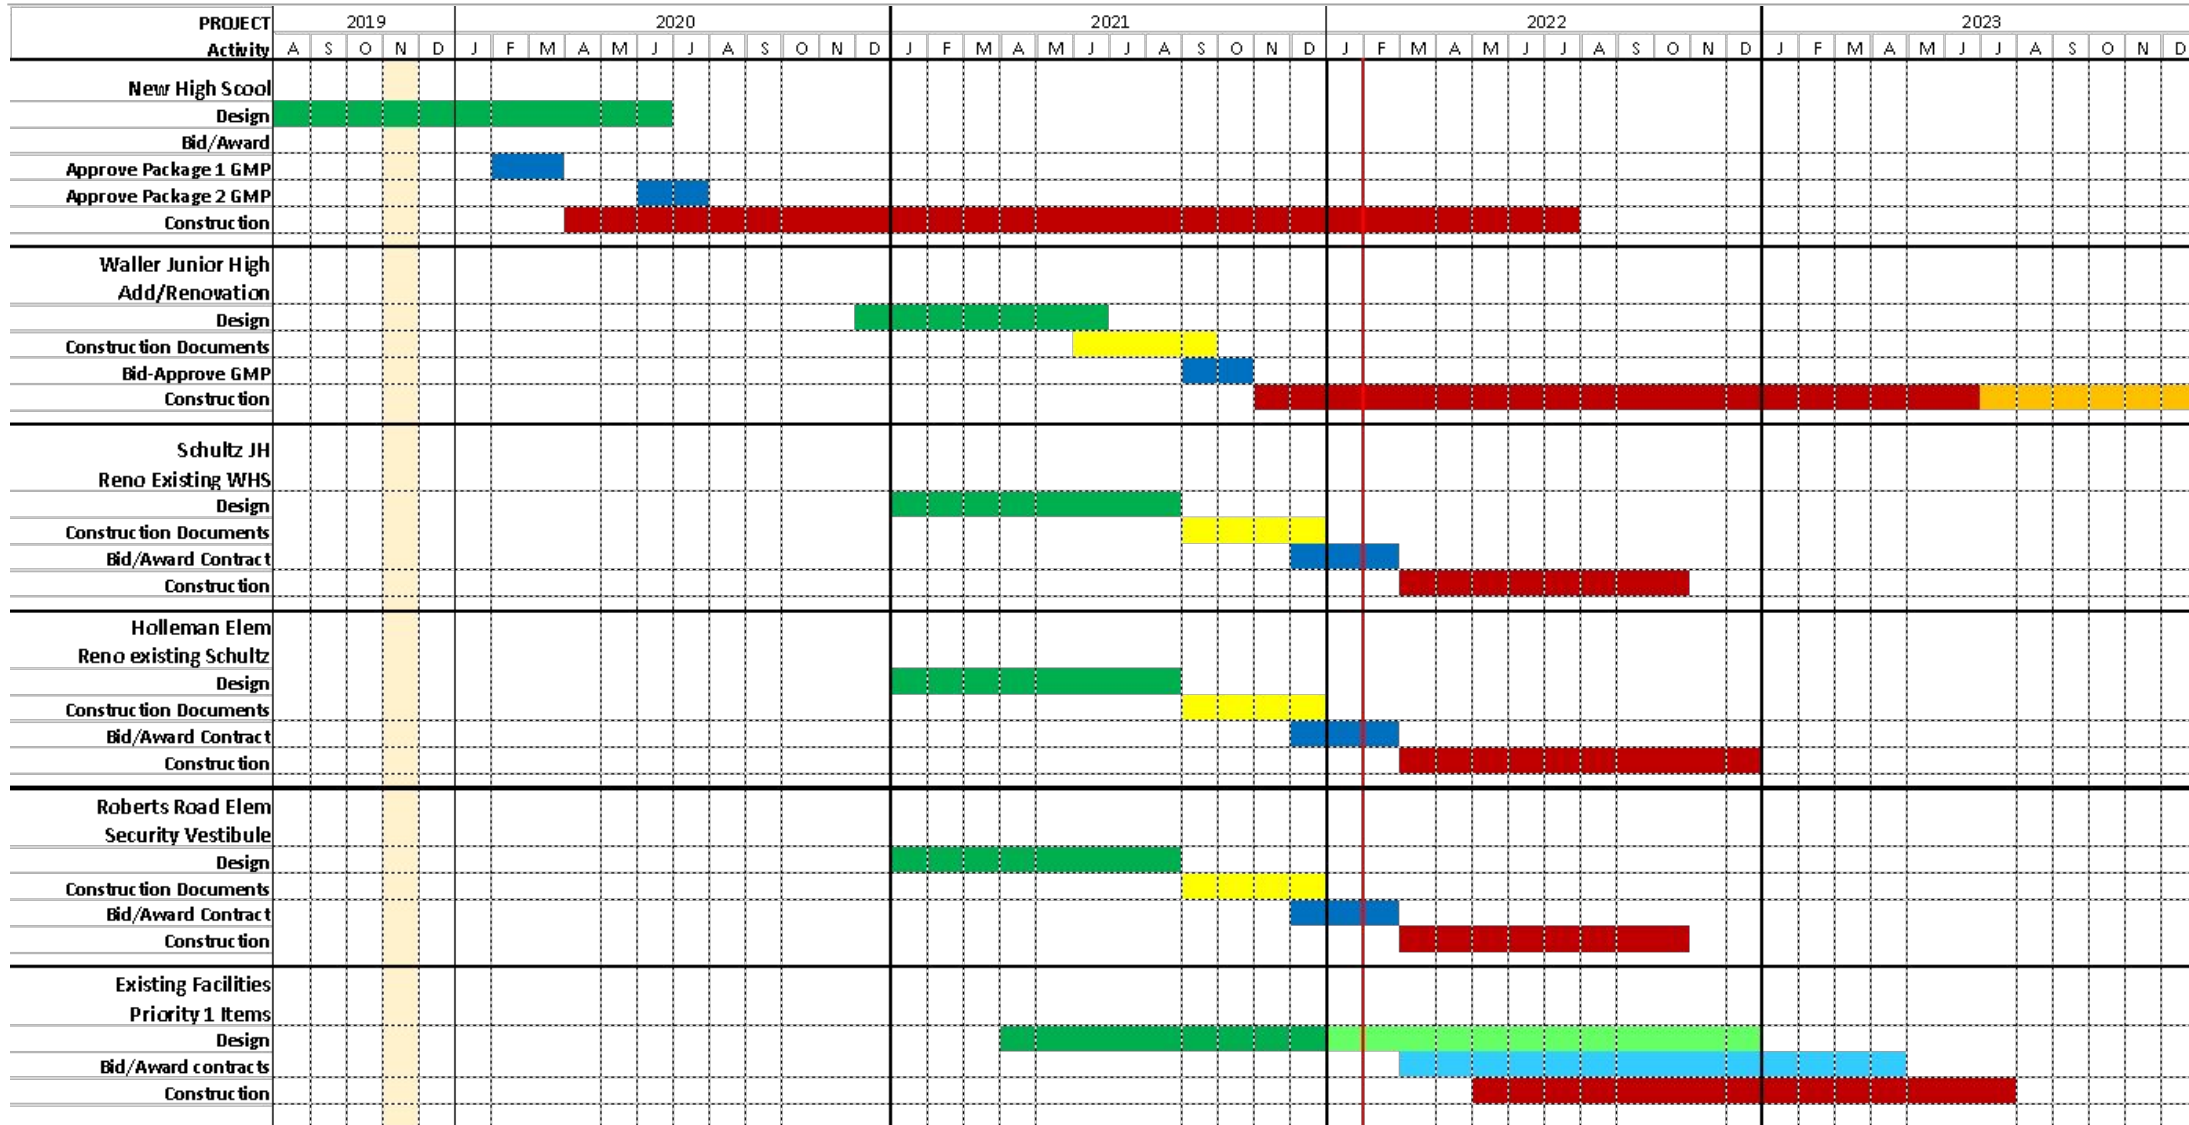

2019 Bond Project Update

February 2022 Update

- ◆ **New Waller High School** - approximately 86% complete.
 - Remains on Budget and On Schedule for August 2022 opening.
- ◆ **Waller Junior High School Renovations and Additions**
 - Selective demolition of sections of East campus in progress.
 - Building pad foundation and installation of drilled piers to start.
- ◆ **Schultz, Holleman, and Roberts Road Renovations**
 - Projects bid on January 20th and February 1st.
 - Schedule to award contracts at March board meeting.
- ◆ **Field Store Elementary Chiller Replacement**
 - Award contract to start design for replacement this year.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update

Rear Aerial Elevation



2019 Bond Project Update



Front Elevation

2019 Bond Project Update



Central Plant



Chillers

2019 Bond Project Update




Science Labs

2019 Bond Project Update



ROTC

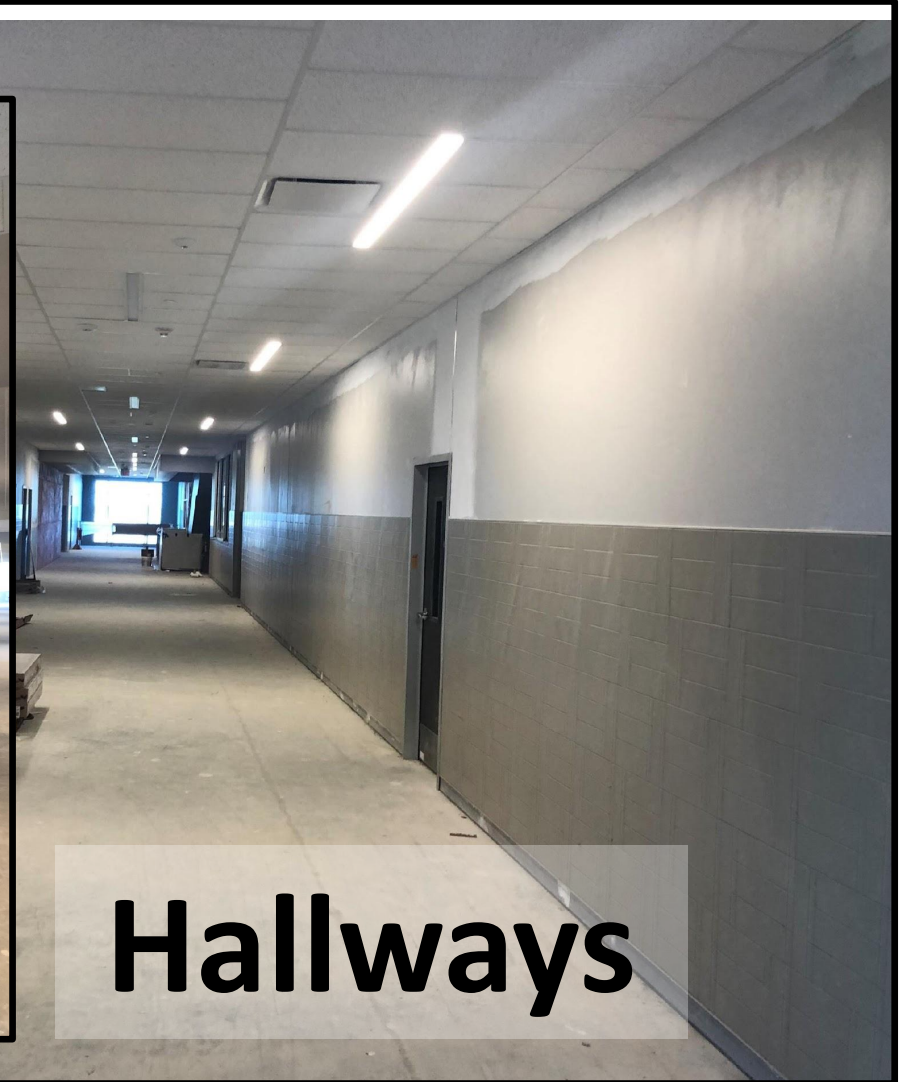

Hallways

2019 Bond Project Update

HCSO Visit



Main Gymnasium

2019 Bond Project Update





Library



2019 Bond Project Update

Central Staircase

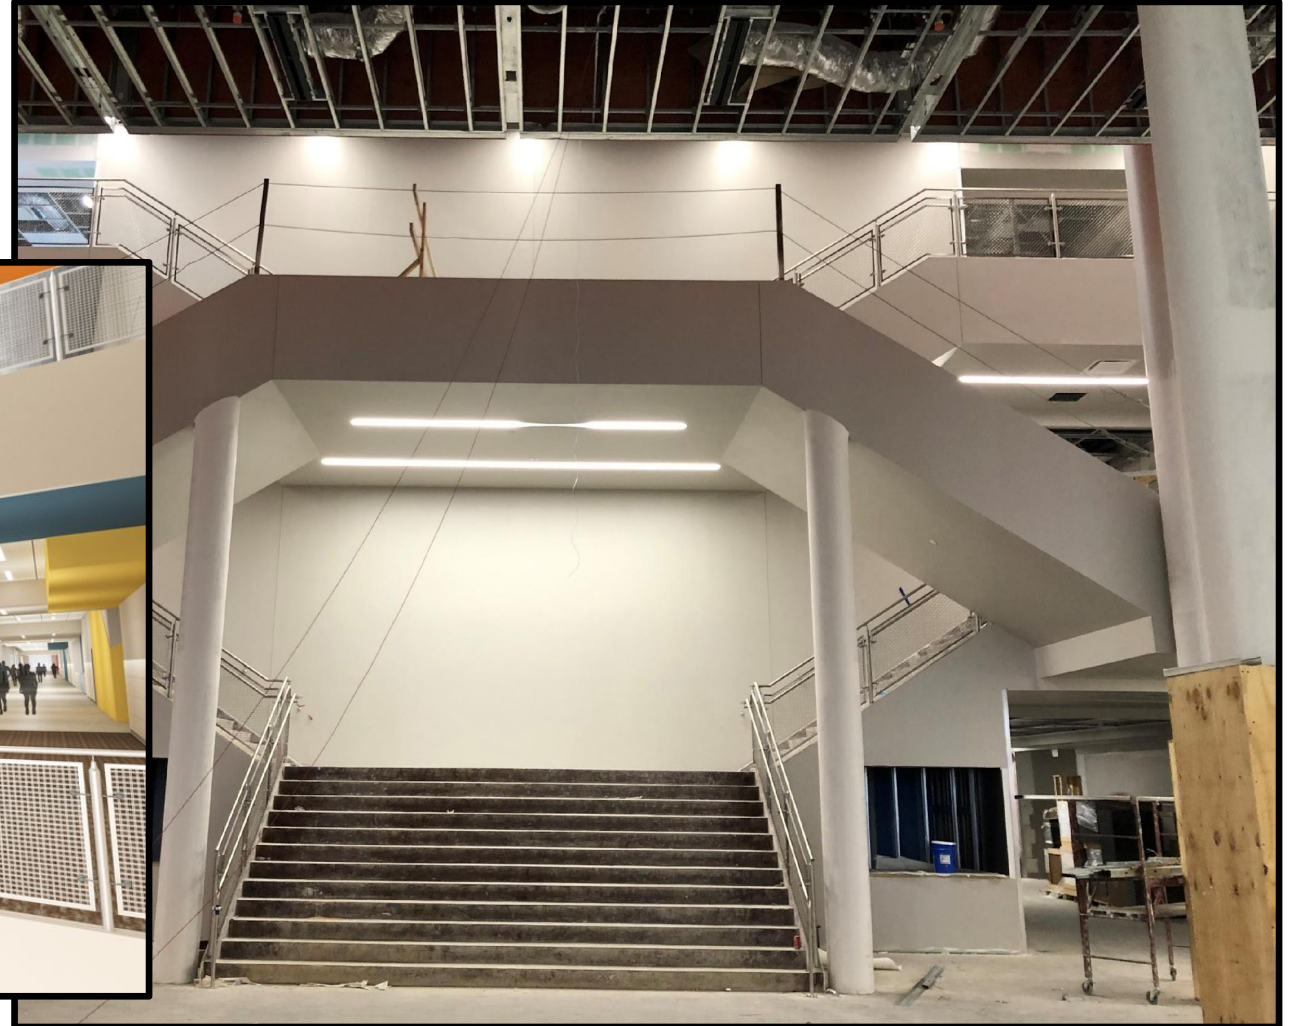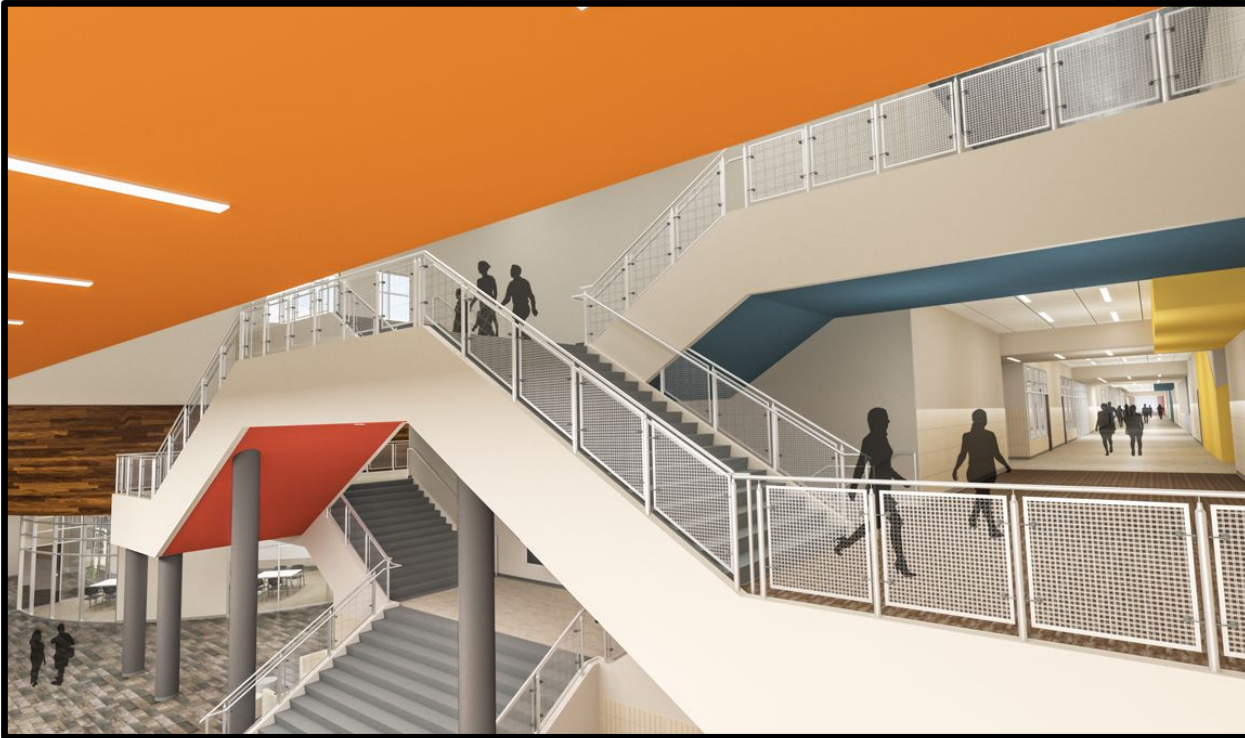

2019 Bond Project Update



Large Cafeteria


2019 Bond Project Update



Cafeteria Kitchen

2019 Bond Project Update


Learning Stairs

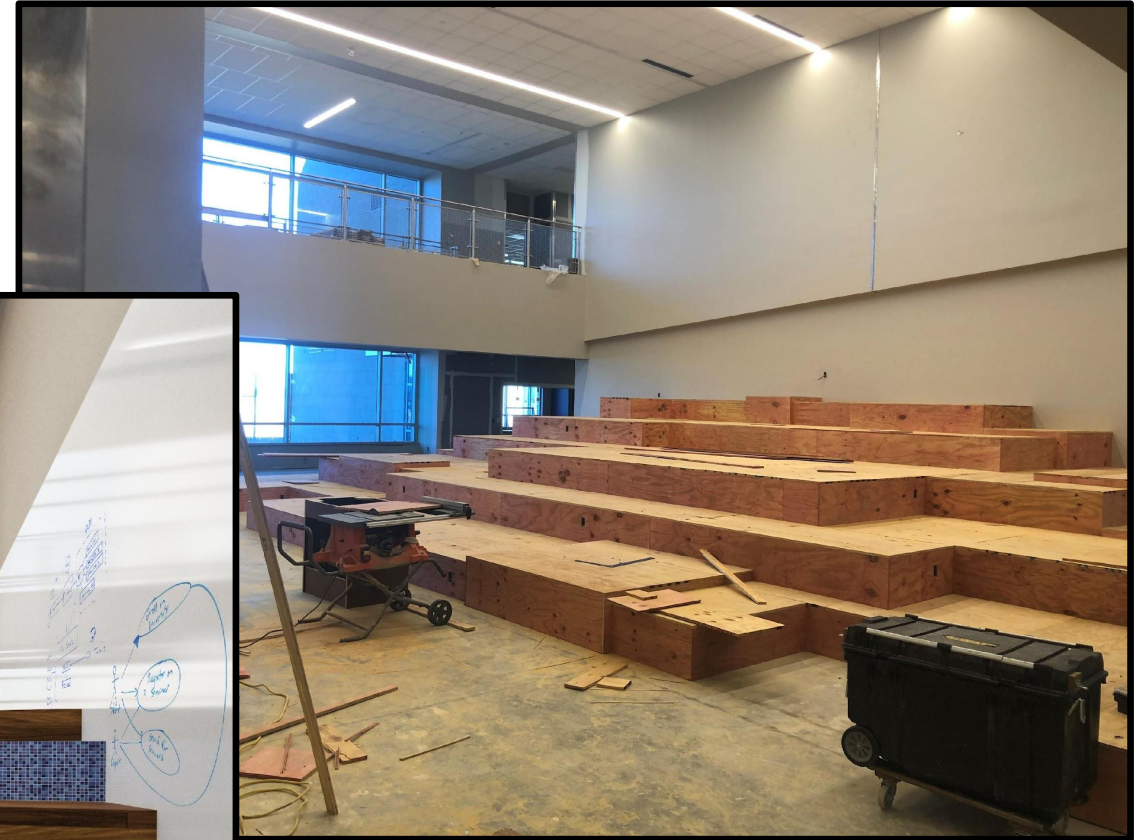

Project Update - New Waller High School

Construction Activity Status

- Kitchen equipment was delivered and being installed.
- Gym wood floors are in progress.
- Ceilings in high volume areas are still being installed. (cafeteria, library, auditorium)
- Restroom wall and hallway wainscot tile remains ongoing.
- Vinyl and marmoleum classroom floors in progress.
- Metal Science Lab casework installation is 95% complete.
- Laminate classroom and office casework is ongoing.
- MEP trim out continues of lights, receptacles, data, plumbing fixtures, air vents, etc.
- HVAC system Testing & Balance continues with Building Commissioning.
- Site clean up continues with site landscaping and irrigation being installed.

An architectural rendering of a modern school building, Waller Junior High. The building features a large glass entrance and a brick facade. In the foreground, there is a parking lot with a brown sedan and a blue SUV. Several people are walking around the building. To the left, there is a flagpole with the American and Texas state flags. The text "DESIGN UPDATE" and "JUNE 4, 2024" is faintly visible in the background.

DESIGN UPDATE JUNE 4, 2024

WALLER JUNIOR HIGH

ADDITIONS AND RENOVATIONS

CONSTRUCTION UPDATE

Waller
Independent School District

2019 Bond Project Update



East Campus Demolition

Project Update - Waller Junior High School

Construction Activity Status

- Relocated classes to 3 new portables on the West Campus.
- Selection Demolition of East Campus' north hallway remains in progress.
- Removal of Farr Street is complete. Working with city to finalize the dedication.
- Removal of concrete foundations, slabs, and paving in progress.
- Underground plumbing and electrical layout has started.
- Building pad and drilled piers are scheduled to begin.

Thank You!

