

2019 BOND

UPDATE

March 2022



2019 Bond Project Update

December 2021

- ◆ **New Waller High School** - under construction and approximately 85% complete.
 - Remains on Budget and On Schedule for August 2022 opening.
 - Furniture (FF&E) and technology being finalized and purchased for summer delivery.
- ◆ **Waller Junior High School Renovations and Additions** –
 - Utility relocations by the city and CenterPoint complete.
 - Site subgrading complete. Mixing in lime and fly ash prior to importing select fill.
 - Drilled piers are currently scheduled to begin in late March.
- ◆ **Schultz, Holleman, and Roberts Road Renovations**
 - Projects have been bid are under review for contracts.
 - Two contracts are being finalized for board consideration and approval.

NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

2019 Bond Project Update



South Aerial


2019 Bond Project Update

Auditorium



2019 Bond Project Update

Large Cafeteria

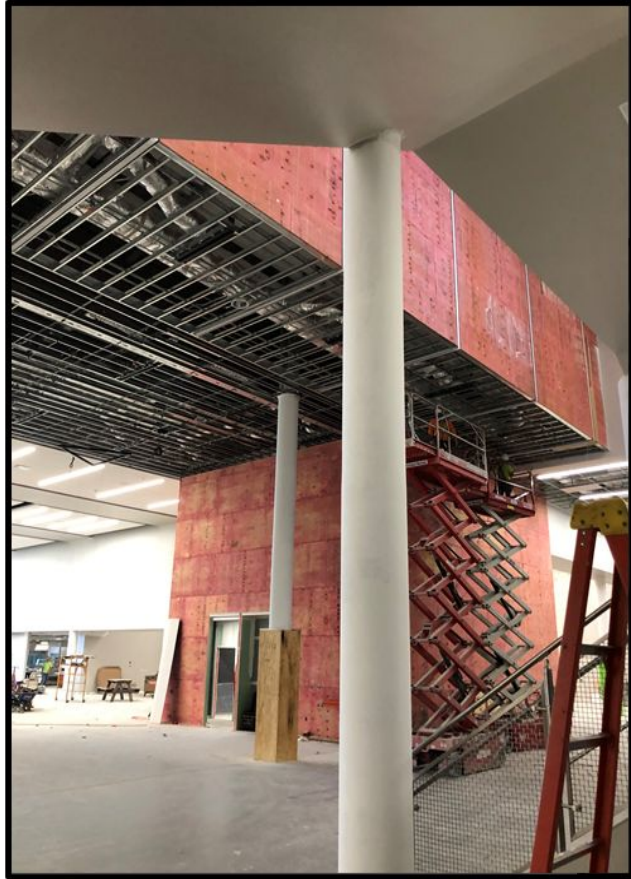

Library



Central Staircase

2019 Bond Project Update



Cafeteria Serving Lines

2019 Bond Project Update



**Competition
Gym**

2019 Bond Project Update



Dance Gym (Both Floors Unfinished)



Auxiliary Gym

2019 Bond Project Update



**Vinyl Flooring Install
Beginning on 3rd Floor**

2019 Bond Project Update



Classroom

2019 Bond Project Update



Science Classroom



2019 Bond Project Update

Culinary Kitchen



Cosmetology

2019 Bond Project Update

Collaboration Space



2019 Bond Project Update




**Baseball and
Softball complex**



Project Update - New Waller High School

Construction Activity Status

- Metal framing and gypsum walls are 99% complete
- Ceiling grid ongoing throughout Fine Art and front administrative area.
- Ceiling tile installation is 80% complete in 3 story academic wings.
- Wood gym floors are complete in 2 gyms and started in competition gym.
- Linear wood walls and ceiling are on site and scheduled to start.
- Above ceiling punch list is being corrected before cover-up.
- Hallway wainscot tiles are ongoing.
- Auditorium ceiling is complete, and below ceiling finishes to begin.
- Wall repair and final painting has started.
- Plastic wall panels have started in corridors.
- Site clean up ongoing, and sidewalks and site lighting are being installed.
- HVAC system Testing & Balance ongoing.
- Building Envelope System Commissioning is ongoing.

The image shows the exterior of Waller Jr. High school. The building is a single-story structure with a light-colored brick facade and a dark red roofline. A sign above the entrance reads "WALLER JR. HIGH". The entrance features large glass doors and windows. There are several trees in front of the building, including a large green tree on the right and smaller trees with reddish-brown foliage on the left. A paved walkway leads to the entrance, and a grassy area is in the foreground.

WALLER JR. HIGH

WALLER JUNIOR HIGH CONSTRUCTION UPDATE

2019 Bond Project Update



WJH Dirt Work

2019 Bond Project Update



**WJH East Campus
Demo Removal of
3rd Hallway 6
classes**



Thank You!

