

2019 BOND

UPDATE


April 2021



Project Budgets

New Waller High School	\$ 195,019,130
Waller JH Renovation & Addition	\$ 61,922,314
Schultz Junior High (renovate existing WHS)	\$ 7,104,030
Holleman Elementary (renovate Schultz JH)	\$ 3,674,716
Roberts Road Elementary Vestibule	\$ 978,242
Other campus renovations (Priority 1)	\$ 3,231,093
Others (buses, tech., land, etc.)	\$ 23,295,476
TOTAL	\$ 295,225,000

2019 Bond Planning Schedule

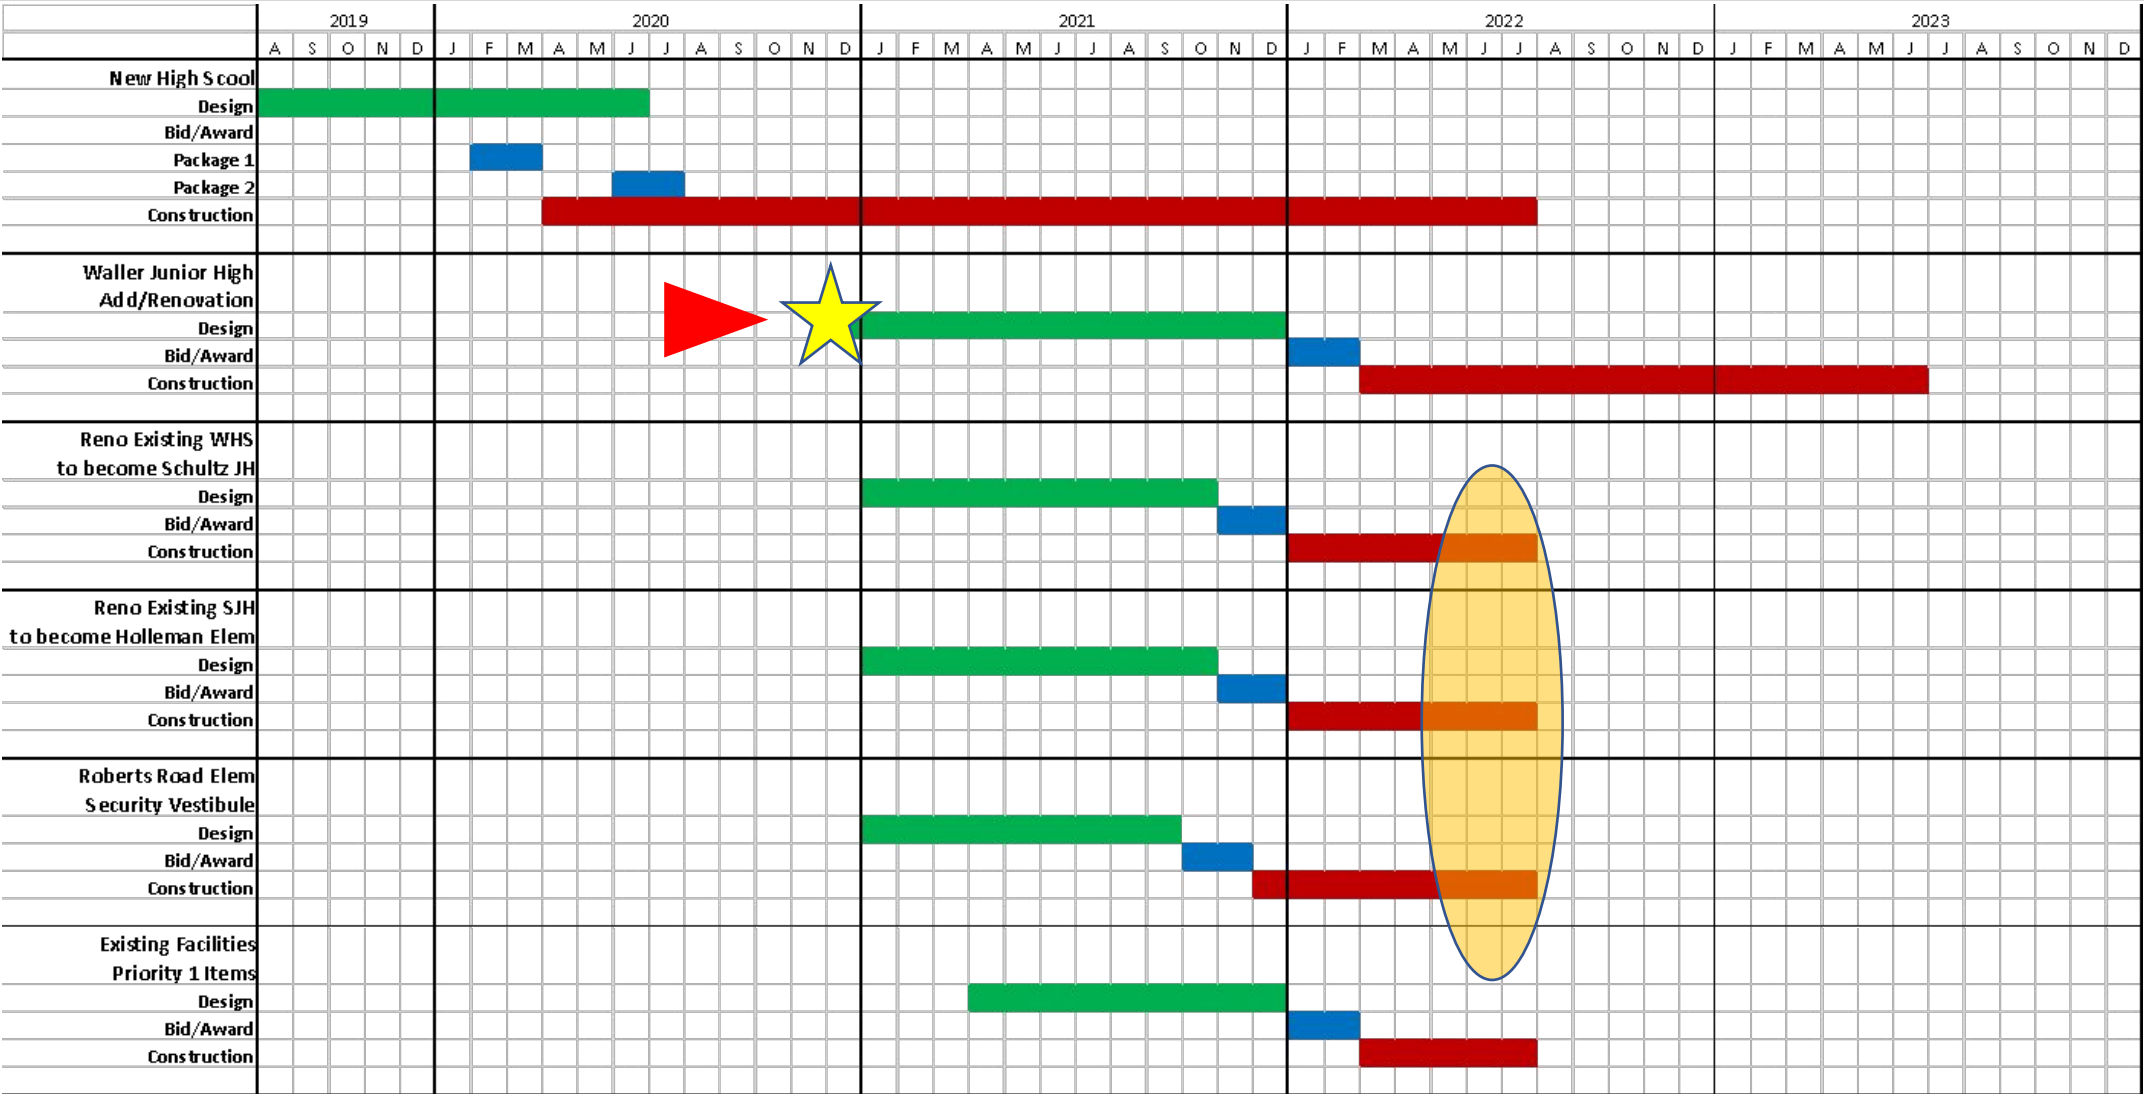

2019 Bond Project Update

- ◆ **New Waller High School** - under construction and 47% complete through 46% of scheduled.
Soccer/Track and Field House - June '21. Auto Tech shop – Aug. '21. Baseball/Softball – Dec. '21
- ◆ **Waller Junior High School Renovations and Additions** - Design Development 99% complete.
Meeting scheduled with City of Waller and utilities to coordinate Farr Street dedication.

Other Projects with VLK Architect designing, and scheduled for August 2022 completions

- Schultz Junior High Renovations of WHS
- Holleman Elementary Renovations of SJH
- Roberts Road Elementary Vestibule and Renovations

*Scope and Design Kickoff meetings are scheduled

Schematic Design

WALLER JUNIOR HIGH ADDITIONS & RENOVATIONS


Level One Floorplan



NEW HIGH SCHOOL CONSTRUCTION UPDATE



New Waller High School

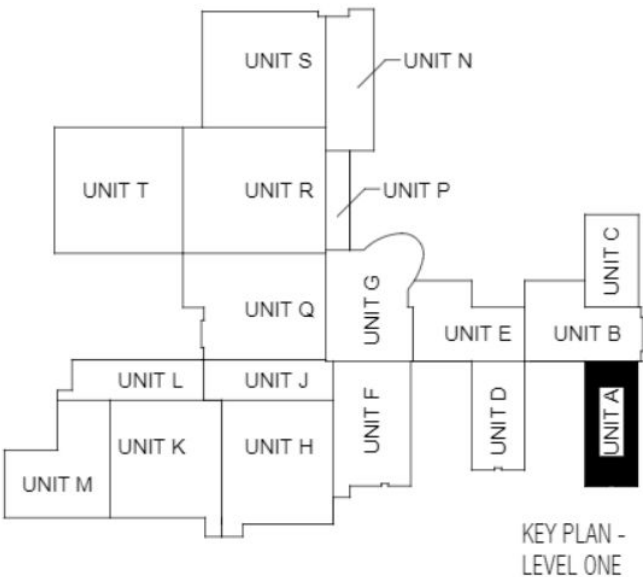

Floor Plan

New Waller High School



East Elevation from Student Parking

New Waller High School



Front-North Elevation from Waller Spring Creek

New Waller High School

Exterior Masonry continues



New Waller High School

Exterior Framing and Window Frames/ Glazing



New Waller High School



**Three Transformers
delivered and wire
being pulled in**

New Waller High School



Field House Renovations

New Waller High School



Field House Renovations

New Waller High School



Field House Renovations

New Waller High School

60 yard Synthetic Practice Field



Soccer and Track Complex



Project Update - New Waller High School

Construction Activity Status

- Stormwater Pump Station 99% complete
- Fire Proofing – ongoing in Areas Q and R
- Interior and Exterior CMU block walls continue
- Exterior Brick complete on east elevation, and continuing around the north and south.
- Metal wall framing and gypsum on going
- Window Frames/Glass ongoing
- MEP Interior rough-in – ongoing. 75% complete in Areas A-F. Chill and Hot water mains are 95% complete and flushing plan being finalized.
- Three transformers delivered and install for planned permanent power in June.
- Field House Renovation under way for June completion
- Track and Soccer Complex turf is down and 60-yard practice field to follow
- Baseball/Softball summer work being planned and coordinated

Thank You!

