


2019 BOND

UPDATE

April 2022



2019 Bond Planning Schedule

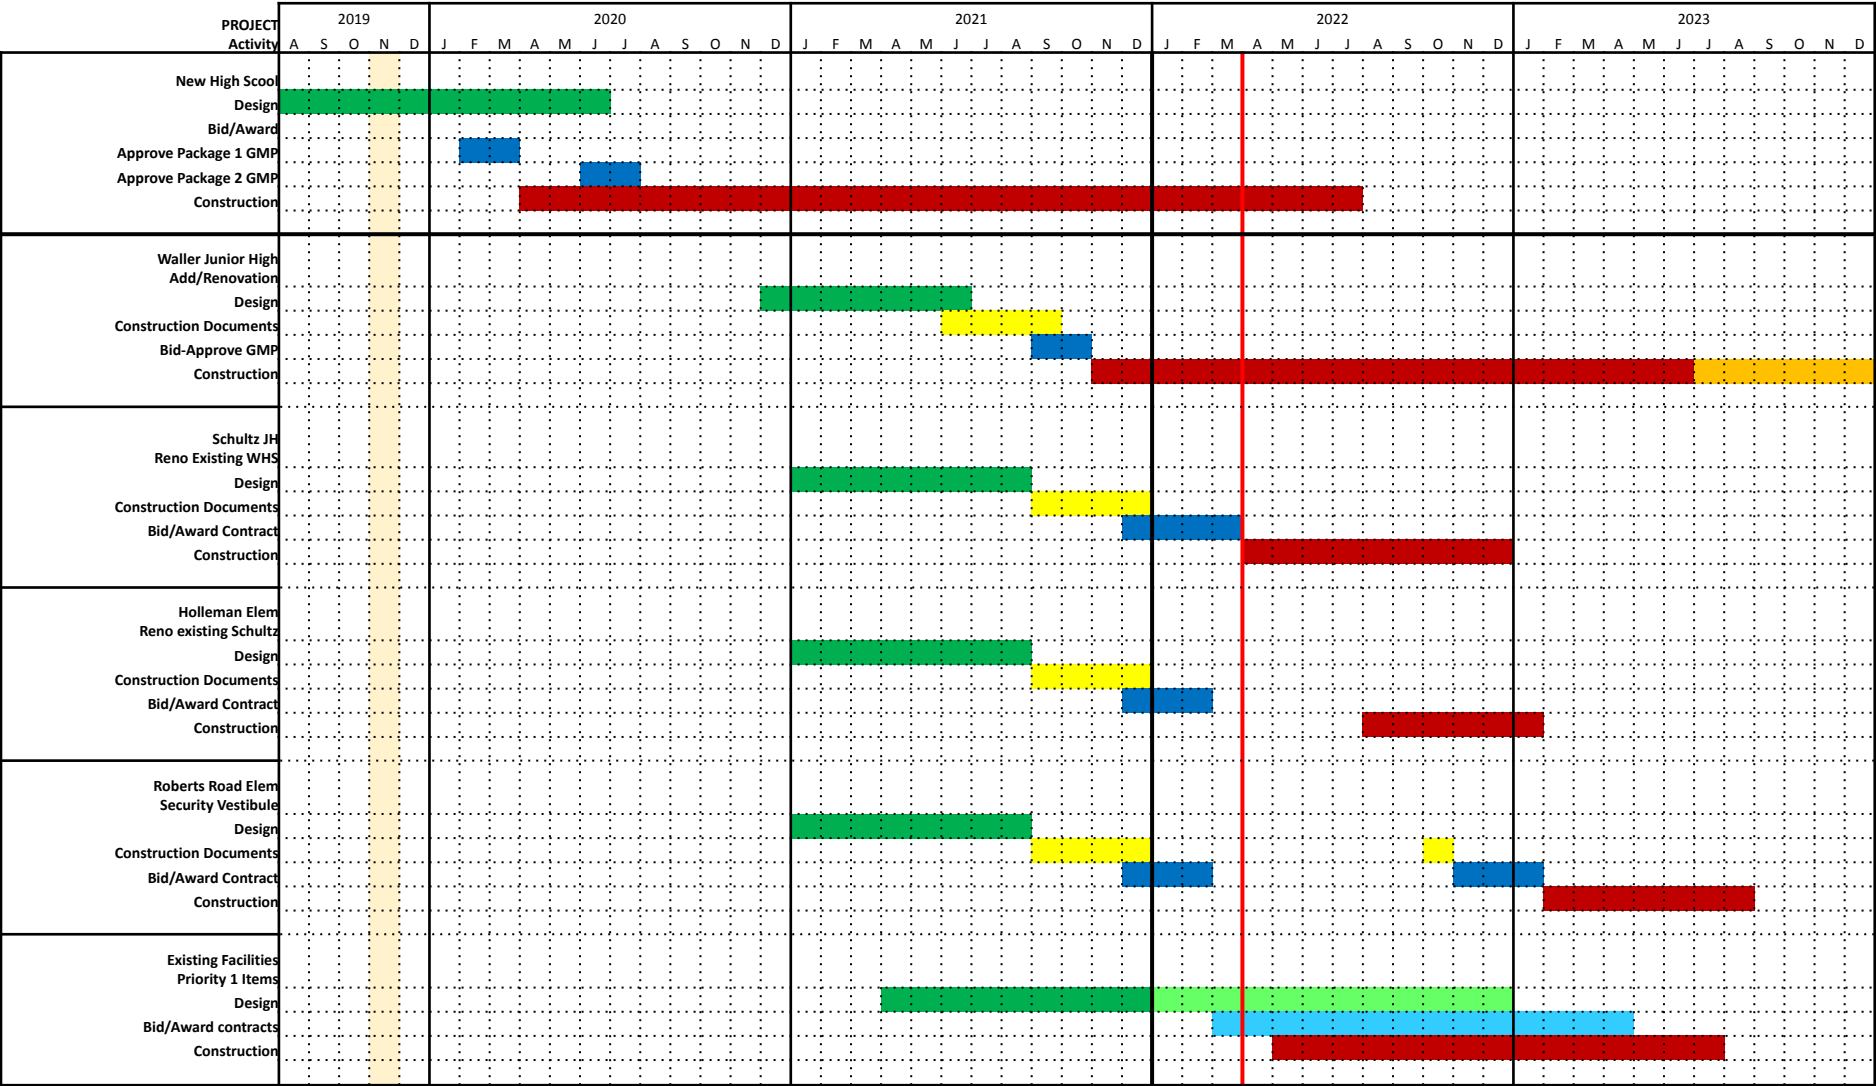


NEW HIGH SCHOOL CONSTRUCTION UPDATE



Waller
Independent School District

New Waller High School

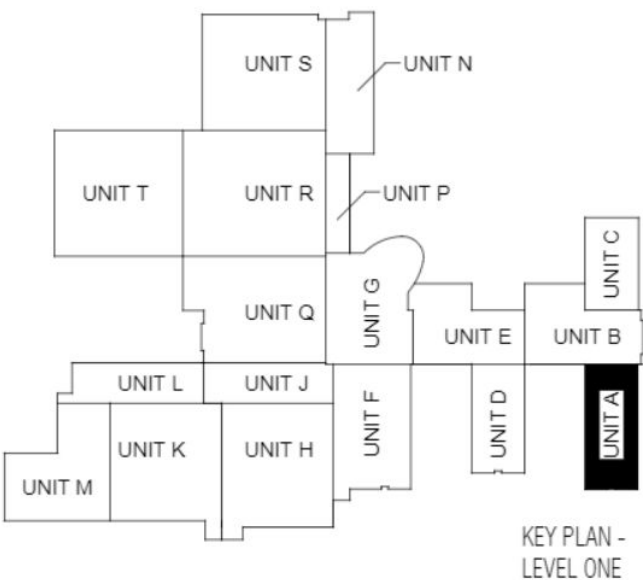

Floor Plan

2019 Bond Project Update

Auditorium



2019 Bond Project Update

Central Staircase



Large Cafeteria

2019 Bond Project Update



Large Cafeteria & Side Cafeteria

2019 Bond Project Update



**Competition
Gym**

2019 Bond Project Update



Dance Gym (Both Floors Unfinished)



Auxiliary Gym

2019 Bond Project Update

Plastic Wall Panels



**Administrative Suite
Wall**

2019 Bond Project Update



**Flooring Install on
Multiple Levels**

2019 Bond Project Update



2019 Bond Project Update



Science Classroom

2019 Bond Project Update

Welding Lab



Band Hall

2019 Bond Project Update

Culinary Kitchen



Culinary Classroom

2019 Bond Project Update

Bistro Kitchen



Cosmetology

2019 Bond Project Update


Collaboration Space



Project Update - New Waller High School

Construction Activity Status

- Ceiling grid ongoing and tile installation is 99% complete in 3 story wings.
- Interior window frames and glass 60% complete.
- Gym wood floors are installed. Painting and sealing in progress.
- Epoxy floors are complete in Athletic areas and kitchens. Working in hallways.
- Athletic lockers are 99% complete.
- Terrazzo flooring in gym lobby complete. In progress in auditorium lobby.
- Linear wood walls and ceiling are in progress.
- Hallway wainscot tiles are ongoing, and porcelain floor tile in progress.
- Classroom flooring and 2nd-3rd floor corridor LVT flooring complete.
- Window roller shades and blinds installation started.
- Kitchen and Bistro equipment 90% complete.
- Auditorium rigging, lighting, and local sound have all started.
- Data cabling and classroom front row sound in progress and 90% complete.
- Site clean up ongoing, and sidewalks and site lighting are being installed.

The image shows the exterior of Waller Jr. High school. The building is a single-story structure with a light-colored, textured facade and a dark red roofline. A sign above the entrance reads "WALLER JR. HIGH". The entrance features large glass doors and windows. There are several trees in the foreground, including a large green tree on the right and smaller trees with reddish-brown foliage on the left. A paved walkway leads from the bottom right towards the entrance. The overall scene is bright and clear, suggesting a sunny day.

WALLER JR. HIGH

WALLER JUNIOR HIGH CONSTRUCTION UPDATE

2019 Bond Project Update



WJH Building Pad

2019 Bond Project Update



WJH Building Pad

2019 Bond Project Update

- Building pad limed, compacted, and complete.
- Pier and underground plumbing layout has started.
- Drilled Piers are scheduled to start April 11th.
- East gym demolition complete. Locker room underground plumbing started.
- Structural steel shop drawings are approved and steel in fabrication.
- Contractor is working to have all their submittals completed this summer.
- Still waiting for utility abandonment documents before city can dedicate Farr St.

Thank You!

