


BOND UPDATE

August 2023

#ThankYouVoters

The background of the image features several square wooden blocks arranged on a dark surface. Each block has a different embossed design. One block in the foreground shows a detailed architectural drawing of a building with a dome. Another block shows a landscape with a winding path. The text is overlaid on these blocks.

2019 BOND CONSTRUCTION UPDATE

- **Waller Junior High Renovations and Additions**
 - City of Waller issued the Certificate of Occupancy on August 3rd.
 - Harris County Health Department inspection is scheduled for August 14th.
 - Furniture delivery is complete for Phase I.
- **Holleman Elementary Renovations**
 - New emergency generator is scheduled for shipment on November 15, 2023.
- **Priority 1 Projects**
 - Field Store Elementary Chillers have been released for bids due on August 30th.
 - Emergency Generators structural plans are being revised.

WALLER JUNIOR HIGH


PHASE 1 COMPLETION SUMMER 2023

PHASE 2 COMPLETION SUMMER 2024



WALLER JUNIOR HIGH

- Phase I is substantially complete and the district has moved in.
- Drymalla Construction and VLK Architects are writing punch lists.
- City of Waller has issued the Temporary Certificate of Occupancy (TCO) for Phase I.
- Mechanical Testing & Balance and Commissioning remain in progress.
- Gym wall pads are being installed.
- Technology installation (interactive boards, camera, access points) is 95% complete.
- Furniture was delivered and installed.
- Auxiliary Stadium bleacher removal is 75% completed.
- Demolition on old West campus has started and 70% complete.
- Phase II building pad is scheduled to begin in late August.

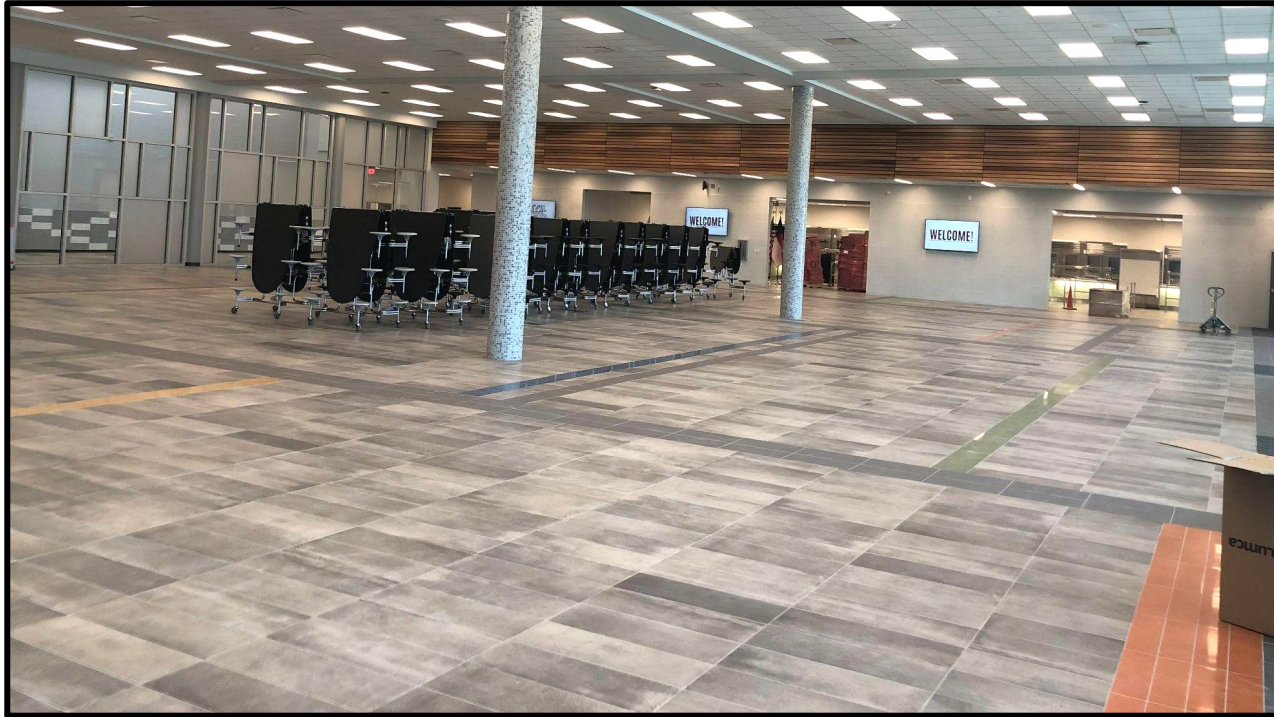

Cafeteria

WALLER JUNIOR HIGH



Kitchen Serving Lines



Media Center




WALLER JUNIOR HIGH



Main Hallways



Central Staircase

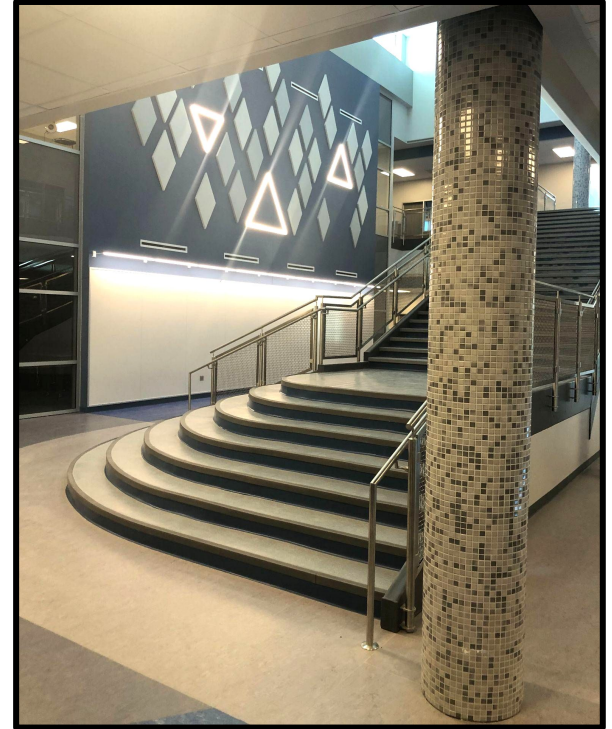

Collaboration Area and Blue Stairs



Classrooms with Furniture




Science Lab

WALLER JUNIOR HIGH



Elevator and Hallway

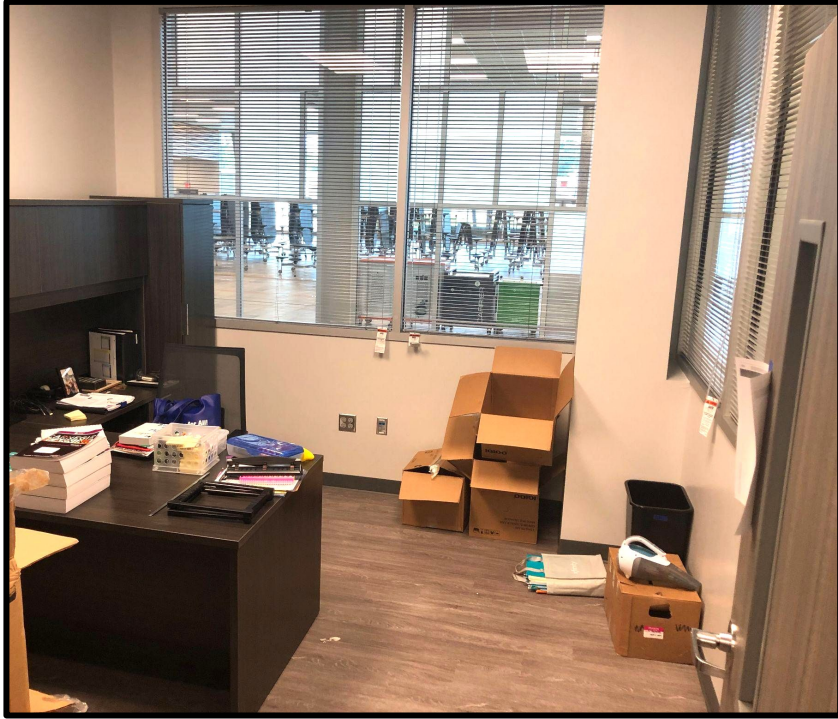


AP Office and Conference Room

WALLER JUNIOR HIGH



Phase II Demolition

An architectural rendering of a modern school building with a long, low profile and a corrugated metal roof. A large American flag flies on a tall pole in front of the building. Several people are depicted walking on the sidewalk and in the parking lot. A blue car is parked in the foreground, and a white pickup truck and a red car are parked further back. The scene is set against a clear sky with some clouds. The entire image has a semi-transparent dark red overlay.

2022 BOND CONSTRUCTION UPDATE

- **Elementary #6 & #7**
 - Steel deliveries have started and steel erection is commencing.
- **Agricultural Science Center and Education Service Center (ESC)**
 - Design development presented in June and construction documents have started.
 - Stewart Builders is providing preconstruction services.
 - Construction remains scheduled schedule for late 2023 start.
- **Turlington Elementary Priority 1 - Driveway Improvements**
 - New parent driveway pavement and light pole installation being completed.
 - Construction remains scheduled for August 4th completion and the start of school.
- **Schultz Junior High Priority 1 - Improvements**
 - Corridor wainscot and accent painting has been completed.
 - Graphics package is on order.

- Slab on Grade is complete.
- Site paving is on-going
- Steel deliveries have started and steel erection is commencing.

ELEMENTARY #6

DELLROSE





Site Aerial



Site Pavement in Progress



Steel Erection in Progress

ELEMENTARY #7

BRIDGELAND





Building Slab is Complete



Steel Erection in Progress



Plumbing Carriers onsite

Turlington Elementary

- Bus-Faculty and Parent driveways have been poured.
- New light poles and fixtures will begin installation in late August.
- Driveway signage has been ordered.



Parent Drive



Parent Drive



Bus and Faculty Drive




Additional Faculty Parking

- Field and Accent painting has been completed.
- Corridor wainscot is completed
- Graphics package signage has been ordered.
- Cafeteria microwave stations are being installed.
- Gym bleacher wall has been erected and painted.
- New bleacher install & eastern bleacher demo is scheduled in October.
- New Administrative and Collaboration furniture has been delivered.



Hallway Wainscot

SCHULTZ JUNIOR HIGH

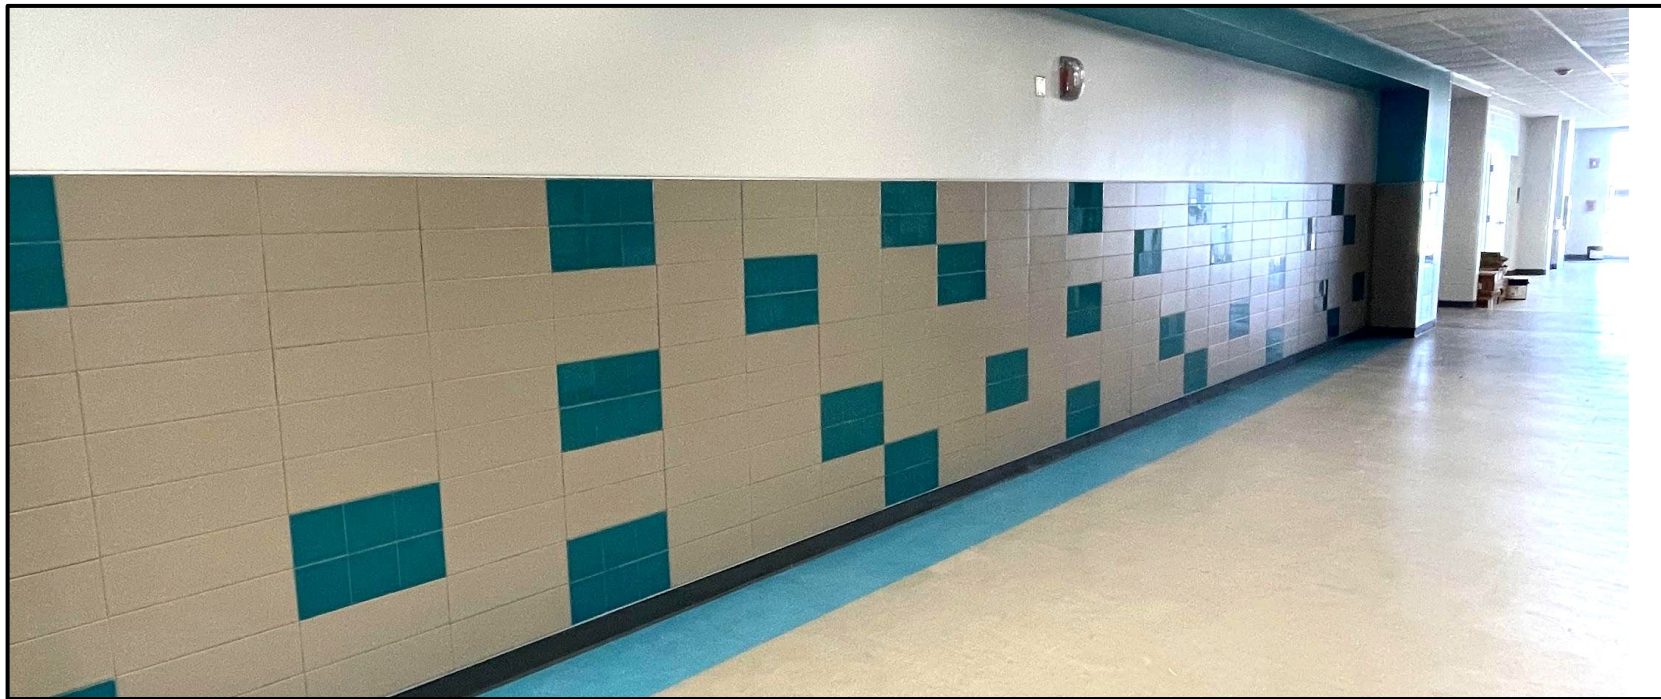


Hallway Wainscot



Cafeteria Wainscot



New Gym Wall

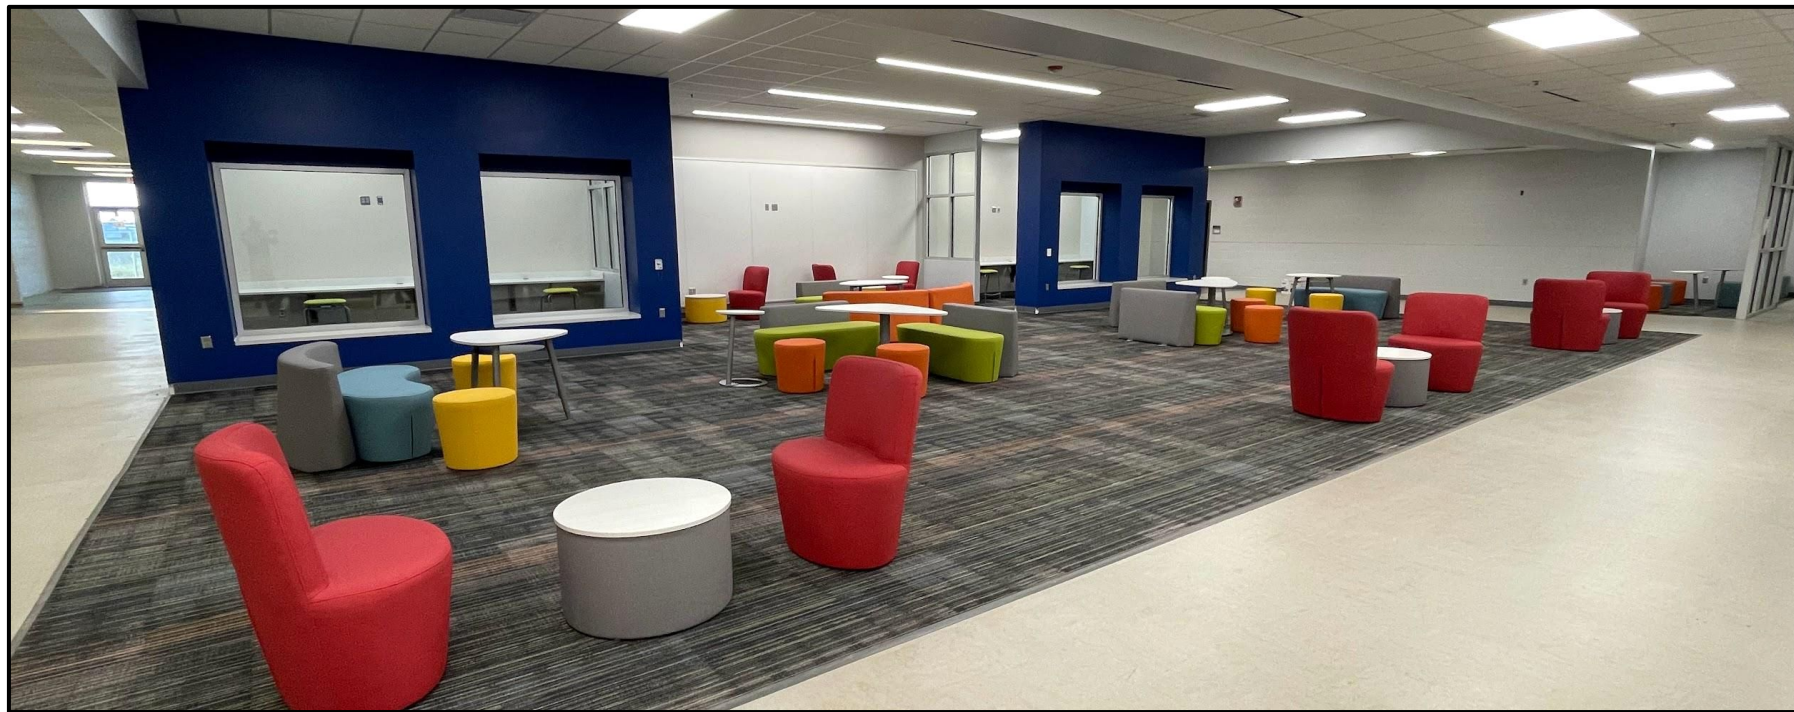

Collaboration Space Furniture



Administrative Furniture

A photograph of a classroom filled with children of various ages, from young children to teenagers. They are all expressing excitement, with many having their arms raised in the air. The children are seated at small, light-colored tables with blue chairs. The classroom has white walls, a tiled ceiling, and various educational posters and supplies visible in the background. The entire image is overlaid with a semi-transparent red filter.

#ThankYouVoters

Waller
Independent School District
