2019 BOND MAY 2020 UPDATE



Project Budgets

New Waller High School Waller JH Renovation & Addition Schultz Junior High (renovate existing WHS) Holleman Elementary (renovate Schultz JH) **Roberts Road Elementary Vestibule** Other campus renovations (Priority 1) Others (buses, tech., land, etc.) TOTAL

- \$ 195,019,130
- \$ 61,922,314
- \$ 7,104,030
- \$ 3,674,716
- \$ 978,242
- \$ 3,231,093
- \$ 23,295,476
- \$ 295,225,000



New Waller High School






New Waller High School





New Waller High School



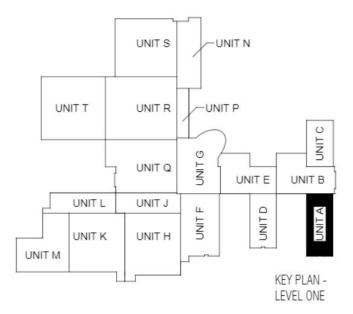



5

Project Update - New Waller High School

Completed/Current Activities

- Notice to Proceed: March 6th
- Site Clear and Grubbed 100%
- Building Pad 100%
- Detention Ponds 70%
- Site Fill 40%
- Drilled Piers 25%
- Grade Beams 10%
- Prefabricating Underground Plumbing

Upcoming Activities

- Site Utilities and Drainage
- Underground Plumbing
- Underground Electrical
- Building Slab on Grade
- Temporary Power
- Structural Steel Erection (June)
- Groundbreaking: TBD
- Package 2 Issued for Bids: June 5th
- Package 2 GMP approved: July



Project Photos - New Waller High School





Project Photos - New Waller High School





Prefabricated Underground **Plumbing**







Thank You!

